

JOB No.: TCS00975/18

**CEDD CONTRACT AGREEMENT NO. EDO/04/2018 -
ENVIRONMENTAL TEAM FOR CROSS BAY LINK, TSEUNG
KWAN O**

**MONTHLY ENVIRONMENTAL MONITORING & AUDITING
REPORT OF THE PROJECT – MARCH 2019**

**PREPARED FOR
CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT
(CEDD)**

Date	Reference No.	Prepared By	Certified By
12 April 2019	TCS00975/18/600/R0157v2	 Martin Li (Environmental Consultant)	 Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	8 April 2019	First Submission
2	12 April 2019	Amended against IEC's comments



Our ref: ASCL-2018009

AECOM Asia Company Limited
8/F., Grand Central Plaza, Tower 2
138 Shatin Rural Committee Road
Shatin, New Territories, Hong Kong

Attention: Mr. Conrad NG

12 April 2019

Dear Sir,

Contract No. NE/2017/07
Cross Bay Link, Tseung Kwan O – Main Bridge and Associated Works
Monthly EM&A Report for March 2019

I refer to the email of ET concerning the Monthly EM&A Report for March 2019 (Version 2) with Ref. No. TCS00975/18/600/R0157v2. We have no further comment on it and verify the captioned according to section 1.9 of Environmental Permit with No. EP-459-2013.

Yours faithfully,

A handwritten signature in black ink, appearing to be "Li Wai Ming".

Li Wai Ming Kevin
Independent Environmental Checker

cc. Mr. Tam (ETL)
Simon Wong (CEDD)

EXECUTIVE SUMMARY

- ES01 Civil Engineering and Development Department (hereafter referred as “CEDD”) is the Project Proponent and the Permit Holder of the Project Cross Bay Link, Tseung Kwan O (hereinafter referred as “the Project”) which is a Designated Project to be implemented under Environmental Permit number EP-459/2013 (hereinafter referred as “the EP-459/2013” or “the EP”).
- ES02 AUES was awarded the CEDD Contract Agreement No. EDO/04/2018 - Environmental Team for Cross Bay Link, Tseung Kwan O (hereinafter called “the Service Contract”). The Services under the Service Contract is to provide environmental monitoring and audit (EM&A) services for the Works Contracts pursuant to the requirement of Environmental Team (ET) under the Approved EM&A Manual to ensure that the environmental performance of the Works Contracts comply with the requirement specified in the EM&A Manual and EIA Report of Agreement No. CE 43/2008 (HY) Cross Bay Link, Tseung Kwan O - Investigation and other relevant statutory requirements.
- ES03 To facilitate management, the proposed Works of the project was divided into two Civil Engineering and Development Department (CEDD) Works contracts included *Contract 1 (Contract No. NE/2017/07)* and *Contract 2 (Contract No. NE/2017/08)*. The date for commencement of Contract 1 was **3rd December 2018** while the date for commencement of Contract 2 was **17th January 2019**.
- ES04 According to the Approved Environmental Monitoring & Audit (EM&A) Manual, air quality, noise and water quality monitoring are required to be conducted during the construction phase of the Project. As part of the EM&A programme, baseline monitoring shall undertake before the Project construction work commencement to determine the ambient environment condition. The baseline air quality, background noise and water quality monitoring has been carried out between **21st September 2018** and **13th November 2018** at the designated and interim locations. The baseline monitoring report under the EP-459/2013 has been compiled by the ET and verified by Independent Environmental Checker (hereinafter the “IEC”) prior submitted to EPD on **19th November 2018** for endorsement.
- ES05 This is the **4th** Monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **1st to 31st March 2019** (hereinafter ‘the Reporting Period’).

CONSTRUCTION WORKS CONDUCTED AT THE REPORTING MONTH

- ES06 The major construction activities of Contract 1 (Contract No. NE/2017/07) undertaken in this Reporting Period are:-
- Pre-drilling works at Portion II
 - Piling works at Portion II
- ES07 The major construction activities of Contract 2 (Contract No. NE/2017/08) undertaken in this Reporting Period are:-
- UU Detection Work at Portion VI
 - Trial Pit and Pre-drill Work at Portion III & VI

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES08 Environmental monitoring activities under the EM&A program in this Reporting Period are summarized in the following table.

Table ES-4 Summary Environmental Monitoring Activities Undertaken in the Reporting Period

Issues	Environmental Monitoring Parameters / Inspection		Sessions
Air Quality	1-Hour TSP		15
	24-Hr TSP		5
Construction Noise	Leq (30min) Daytime		4
	Leq (15min) Evening		3
Water Quality	Marine Water Sampling ^(Note 1)		13
Inspection / Audit	Contract 1	ET Regular Environmental Site Inspection	5
		Joint site audit with Project Consultant and IEC	1
	Contract 2	ET Regular Environmental Site Inspection	5
		Joint site audit with Project Consultant and IEC	1

Note 1 Total sessions are counted by monitoring days

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES09 No air quality monitoring exceedance was recorded in this Reporting Period. No daytime construction noise monitoring exceedance was recorded while three (3) evening additional construction noise monitoring exceedances were recorded in this Reporting Period. For water quality monitoring, one (1) Action Level and one (1) Limit Level exceedances were recorded for Suspended Solids in the reporting period. NOEs were issued to notify EPD, AFCD, WSD, IEC, the Contractor and the Project Consultant. The statistics of environmental exceedance and investigation of exceedance are summarized in the following table.

Table ES-5 Summary Environmental Monitoring Parameter Exceedance in the Reporting Period

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action	
				Investigation Results	Corrective Actions
Air Quality	1-Hour TSP	0	0	--	--
	24-Hr TSP	0	0	--	--
Construction Noise	Leq _{30min} Daytime	0	0	--	--
	Leq _{15min} Evening	0	3	Not project related	NA
Water Quality (Marine Water)	DO	0	0	--	--
	Turbidity	0	0	Not project related	NA
	SS	1	1		

ES10 For the evening construction noise monitoring exceedances recorded on 15, 21 and 28 March 2019, and marine water quality exceedances recorded on 20 March 2019, investigations were carried out and it was considered that the exceedances recorded are unlikely caused by the Project.

ENVIRONMENTAL COMPLAINT

ES11 One (1) environmental complaint was recorded in this Reporting Period for the Project. The statistics of environmental complaint are summarized in the following table.

Table ES-6 Summary Environmental Complaint Records in the Reporting Period

Reporting Period	Contract	Environmental Complaint Statistics			Related with the Works Contract(s)
		Frequency	Cumulative	Complaint Nature	
1 – 31 March 2019	1	1	1	Marine Water	Not Project Related
	2	0	0	NA	NA

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES12 No environmental summons or prosecutions was received in this Reporting Period for the Project. The statistics of environmental summons or prosecutions are summarized in the following tables.

Table ES-7 Summary Environmental Summons Records in the Reporting Period

Reporting Period	Contract	Environmental Summons Statistics			Related with the Works Contract(s)
		Frequency	Cumulative	Complaint Nature	
1 – 31 March 2019	1	0	0	NA	NA
	2	0	0	NA	NA

Table ES-8 Summary Environmental Prosecutions Records in the Reporting Period

Reporting Period	Contract	Environmental Prosecution Statistics			Related with the Works Contract(s)
		Frequency	Cumulative	Complaint Nature	
1 – 31 March 2019	1	0	0	NA	NA
	2	0	0	NA	NA

REPORTING CHANGE

ES13 There is no reporting change made for this monthly report.

SITE INSPECTION BY EXTERNAL PARTIES

ES14 No site inspection was undertaken by AFCD within the Reporting Period. EPD site inspection was undertaken on 20 March 2019 in relation to environmental complaint received in March 2019.

FUTURE KEY ISSUES

ES15 Due to wet season is approaching, the Contractor was reminded that all the works to undertaking must be fulfill environmental statutory requirement, especially water quality mitigation measures to prevent surface runoff into nearby water bodies or public areas.

ES16 In regards to the marine works, special attention should be paid on excavation works for the bridge pier foundations underway in which water quality mitigation measures such as erection of silt curtain should be properly implemented and maintained.

Table of Contents

1. INTRODUCTION	3
1.1 PROJECT BACKGROUND	3
1.2 REPORT STRUCTURE	3
2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS AND SUBMISSION	5
2.1 PROJECT ORGANIZATION	5
2.2 CONSTRUCTION PROGRESS	6
2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS	7
3. SUMMARY OF ENVIRONMENTAL MONITORING PROGRAMMES AND REQUIREMENTS	9
3.1 GENERAL	9
3.2 MONITORING PARAMETERS	9
3.3 MONITORING LOCATIONS	9
3.4 MONITORING FREQUENCY AND PERIOD	10
3.5 MONITORING EQUIPMENT	11
3.6 MONITORING PROCEDURES	12
3.7 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	15
3.8 DATA MANAGEMENT AND DATA QA/QC CONTROL	17
4. AIR QUALITY MONITORING	18
4.1 GENERAL	18
4.2 RESULTS OF AIR QUALITY MONITORING IN THE REPORTING MONTH	18
5. CONSTRUCTION NOISE MONITORING	19
5.1 GENERAL	19
5.2 RESULTS OF NOISE MONITORING	19
6. WATER QUALITY MONITORING	20
6.1 GENERAL	20
6.2 RESULTS OF WATER QUALITY MONITORING	20
7. WASTE MANAGEMENT	24
7.1 GENERAL WASTE MANAGEMENT	24
7.2 RECORDS OF WASTE QUANTITIES	24
8. SITE INSPECTION	25
8.1 REQUIREMENTS	25
8.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	25
9. LANDFILL GAS MONITORING	27
9.1 GENERAL REQUIREMENT	27
9.2 LIMIT LEVELS AND EVENT AND ACTION PLAN	27
9.3 LANDFILL GAS MONITORING	27
10. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	28
10.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	28
11. IMPLEMENTATION STATUS OF MITIGATION MEASURES	29
11.1 GENERAL REQUIREMENTS	29
11.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	29
11.3 IMPACT FORECAST	30
12. CONCLUSIONS AND RECOMMENDATIONS	31
12.1 CONCLUSIONS	31
12.2 RECOMMENDATIONS	31

LIST OF TABLES

TABLE 2-1	DOCUMENTS SUBMISSION UNDER ENVIRONMENTAL PERMIT REQUIREMENT
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE PROJECT WORKS (CONTRACT 1)
TABLE 2-3	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE PROJECT WORKS (CONTRACT 2)
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	DESIGNATED AIR QUALITY MONITORING LOCATION RECOMMENDED IN EM&A MANUAL
TABLE 3-3	DESIGNATED CONSTRUCTION NOISE MONITORING LOCATION RECOMMENDED IN EM&A MANUAL
TABLE 3-4	INTERIM ALTERNATIVE LOCATION FOR AIR QUALITY AND NOISE MONITORING
TABLE 3-5	LOCATION OF WATER QUALITY MONITORING STATION
TABLE 3-6	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-7	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-8	WATER MONITORING EQUIPMENT
TABLE 3-9	TESTING METHOD AND REPORTING LIMIT OF THE CHEMICAL ANALYSIS
TABLE 3-10	ACTION AND LIMIT LEVELS FOR AIR QUALITY
TABLE 3-11	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 3-12	ACTION AND LIMIT LEVELS FOR WATER QUALITY
TABLE 4-1	1-HOUR AND 24-HOUR TSP AIR QUALITY IMPACT MONITORING RESULTS
TABLE 5-1	CONSTRUCTION NOISE IMPACT MONITORING RESULTS
TABLE 6-1	RESULT SUMMARY OF DEPTH AVERAGE (SURFACE & MIDDLE LAYER) OF DO (MG/L)
TABLE 6-2	RESULT SUMMARY OF BOTTOM DEPTH OF DO (MG/L)
TABLE 6-3	RESULT SUMMARY OF DEPTH AVERAGE OF TURBIDITY (NTU)
TABLE 6-4	RESULT SUMMARY OF DEPTH AVERAGE OF SUSPENDED SOLID (MG/L)
TABLE 6-5	SUMMARY OF WATER QUALITY EXCEEDANCE
TABLE 7-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 7-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 8-1	SITE OBSERVATIONS OF CONTRACT 1
TABLE 8-2	SITE OBSERVATIONS OF CONTRACT 1
TABLE 9-1	ACTIONS IN THE EVENT OF LANDFILL GAS BEING DETECTED IN EXCAVATIONS
TABLE 10-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 10-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 10-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 11-1	ENVIRONMENTAL MITIGATION MEASURES IN THE REPORTING MONTH

LIST OF APPENDICES

APPENDIX A	PROJECT LAYOUT PLAN
APPENDIX B	PROJECT ORGANIZATION CHART & CONTACT DETAILS OF KEY PERSONNEL
APPENDIX C	3-MONTH ROLLING CONSTRUCTION PROGRAM
APPENDIX D	MONITORING LOCATION (AIR QUALITY, NOISE AND WATER QUALITY)
APPENDIX E	EVENT AND ACTION PLAN
APPENDIX F	IMPACT MONITORING SCHEDULE OF THE REPORTING MONTH AND COMING MONTH
APPENDIX G	CALIBRATION CERTIFICATES OF EQUIPMENT AND THE ACCREDITATION LABORATORY CERTIFICATE
APPENDIX H	DATABASE OF MONITORING RESULTS
APPENDIX I	GRAPHICAL PLOTS OF MONITORING RESULTS
APPENDIX J	METEOROLOGICAL DATA
APPENDIX K	WASTE FLOW TABLE
APPENDIX L	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)

1. INTRODUCTION

1.1 PROJECT BACKGROUND

1.1.1 Civil Engineering and Development Department (hereafter referred as “CEDD”) is the Project Proponent and the Permit Holder of the Project Cross Bay Link, Tseung Kwan O (hereinafter referred as “the Project”) which is a Designated Project to be implemented under Environmental Permit number EP-459/2013 (hereinafter referred as “the EP-459/2013” or “the EP”).

1.1.2 AUES was awarded the CEDD Contract Agreement No. EDO/04/2018 - Environmental Team for Cross Bay Link, Tseung Kwan O (hereinafter called “the Service Contract”). The Services under the Service Contract is to provide environmental monitoring and audit (EM&A) services for the Works Contracts pursuant to the requirement of Environmental Team (ET) under the Approved EM&A Manual to ensure that the environmental performance of the Works Contracts comply with the requirement specified in the EM&A Manual and EIA Report of Agreement No. CE 43/2008 (HY) Cross Bay Link, Tseung Kwan O - Investigation and other relevant statutory requirements.

1.1.3 To facilitate management, the proposed Works of *Cross Bay Link, Tseung Kwan O* (hereinafter called “the Project”) was divided into two Civil Engineering and Development Department (CEDD) Works contracts included *Contract 1 (Contract No. NE/2017/07)* and *Contract 2 (Contract No. NE/2017/08)*. The details of each contract Works are summarized below and the delineation of each contract is shown in [Appendix A](#).

Contract 1 (Contract No. NE/2017/07)

- (i) 400m section of marine viaducts of steel deck sections including the Eternal Arch Bridge;
- (ii) 600m section of marine viaducts of concrete deck sections;
- (iii) An E&M Plantroom and associated building services; and
- (iv) E&M provisions.

Contract 2 (Contract No. NE/2017/08)

- (i) Elevated deck structures along Road D9;
- (ii) A 210m section of cycle track and footpath ramp bridge;
- (iii) A 630m section of noise semi-enclosure covering the entire length of Road D9, and;
- (iv) Lift, staircase, modification of existing seawall along Road D9, landscaping and miscellaneous works.

1.1.4 The date for commencement of Contract 1 is **3rd December 2018** while the date for commencement of Contract 2 is **17th January 2019**.

1.1.5 As part of the EM&A programme, baseline monitoring shall be undertaken before the Project construction work commencement to determine the ambient environmental condition. The baseline air quality, background noise and water quality monitoring has been carried out between **21st September 2018** and **13th November 2018** at the designated and interim locations. The baseline monitoring report under the EP-459/2013 has been compiled by the ET and verified by Independent Environmental Checker (hereinafter the “IEC”) prior submitted to EPD on **19th November 2018** for endorsement.

1.1.6 This is the **4th** Monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **1st** to **31st March 2019** (hereinafter ‘the Reporting Period’).

1.2 REPORT STRUCTURE

1.2.1 The Environmental Monitoring and Audit (EM&A) Monthly Report is structured into the following sections:-

- Section 1** *Introduction*
- Section 2** *Project Organization and Construction Progress*
- Section 3** *Summary of Impact Monitoring Requirements*
- Section 4** *Air Quality Monitoring*

<i>Section 5</i>	<i>Construction Noise Monitoring</i>
<i>Section 6</i>	<i>Water Quality Monitoring</i>
<i>Section 7</i>	<i>Waste Management</i>
<i>Section 8</i>	<i>Site Inspections</i>
<i>Section 9</i>	<i>Landfill Gas Monitoring</i>
<i>Section 10</i>	<i>Environmental Complaints and Non-Compliance</i>
<i>Section 11</i>	<i>Implementation Status of Mitigation Measures</i>
<i>Section 12</i>	<i>Conclusions and Recommendations</i>

2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS AND SUBMISSION

2.1 PROJECT ORGANIZATION

2.1.1 The project organization is shown in *Appendix B*. The responsibilities of respective parties are:

The Project Consultant

2.1.2 The Project Consultant (hereinafter “the Consultant”) is responsible for overseeing the construction works and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the Consultant with respect to EM&A are:

- Monitor the Contractors’ compliance with contract specifications, including the implementation and operation of the environmental mitigation measures and their effectiveness
- Monitor Contractors’, ET’s and IEC’s compliance with the requirements in the Environmental Permit (EP) and EM&A Manual
- Facilitate ET’s implementation of the EM&A programme
- Participate in joint site inspection by the ET and IEC
- Oversee the implementation of the agreed Event / Action Plan in the event of any exceedance
- Adhere to the procedures for carrying out complaint investigation

The Contractor(s) of Works Contract(s)

2.1.3 There will be one contractor for each individual works contract. The Contractor(s) should report to the Consultant. The duties and responsibilities of the Contractor are:

- Comply with the relevant contract conditions and specifications on environmental protection
- Participate in the site inspections by the ET and IEC, and undertake any corrective actions
- Provide information / advice to the ET regarding works programme and activities which may contribute to the generation of adverse environmental impacts
- Submit proposals on mitigation measures in case of exceedances of Action and Limit levels in accordance with the Event / Action Plans
- Implement measures to reduce impact where Action and Limit levels are exceeded
- Adhere to the procedures for carrying out complaint investigation

Environmental Team (ET)

2.1.4 ET shall not be in any way an associated body of the Contractor(s) and employed by the Permit Holder (i.e., CEDD) to conduct the EM&A programme. The ET should be managed by the ET Leader. The ET Leader shall be a person who has at least 7 years’ experience in EM&A and has relevant professional qualifications. Suitable qualified staff should be included in the ET, and resources for the implementation of the EM&A programme should be allocated in time under the Contract(s), to enable fulfillment of the Project’s EM&A requirements as specified in the EM&A Manual during construction of the Project. ET shall report to the Project Proponent and the duties shall include:

- Conduct baseline monitoring, impact monitoring and post-construction monitoring and the associated in-situ and laboratory tests to monitor various environmental parameters as required in the EM&A Manual and the EP
- Analyze the environmental monitoring and audit data, review the success of EM&A programme and the adequacy of mitigation measures implemented, confirm the validity of the EIA predictions and identify any adverse environmental impacts arising
- Carry out regular site inspection to investigate and audit the Contractors’ site practice, equipment/plant and work methodologies with respect to pollution control and environmental mitigation, and effect proactive action to pre-empt problems
- Monitor compliance with conditions in the EP, environmental protection, pollution prevention and control regulations and contract specifications

- Audit environmental conditions on site
- Report on the environmental monitoring and audit results to EPD, the Consultant, the IEC and Contractor(s) or their delegated representatives
- Recommend suitable mitigation measures to the Contractor in the case of exceedance of Action and Limit levels in accordance with the Event and Action Plans
- Liaise with the IEC on all environmental performance matters and timely submit all relevant EM&A proforma for approval by IEC
- Advise the Contractor(s) on environmental improvement, awareness, enhancement measures etc., on site
- Adhere to the procedures for carrying out complaint investigation
- Set up a dedicated web site where the project information, all environmental monitoring and audit data and reports described in Condition 5.2 of the EP, and all finalized submissions and plans required under the EP are to be placed for public inspection
- Upload the environmental monitoring results to the dedicated web site in accordance with requirements of the EP and EM&A Manual
- To carry out the Operational Phase Landfill Gas monitoring during effluent drainage system maintenance for one year

Independent Environmental Checker (IEC)

2.1.5 IEC will be employed for this Project. The Independent Environmental Checker (IEC) should not be in any way an associated body of the Contractor(s) or the ET for the Project. The IEC should be employed by the Permit Holder (i.e., CEDD) prior to the commencement of the construction of the Project. The IEC should have at least 7 years' experience in EM&A and have relevant professional qualifications. The duty of IEC should be:

- Provide proactive advice to the Project Consultant and the Project Proponent on EM&A matters related to the project, independent from the management of construction works, but empowered to audit the environmental performance of construction
- Review and audit all aspects of the EM&A programme implemented by the ET
- Review and verify the monitoring data and all submissions in connection with the EP and EM&A Manual submitted by the ET
- Arrange and conduct regular, at least monthly site inspections of the works during construction phase, and ad hoc inspections if significant environmental problems are identified
- Check compliance with the agreed Event / Action Plan in the event of any exceedance
- Check compliance with the procedures for carrying out complaint investigation
- Check the effectiveness of corrective measures
- Feedback audit results to ET by signing off relevant EM&A proforma
- Check that the mitigation measures are effectively implemented
- Report the works conducted, the findings, recommendation and improvement of the site inspections, after reviewing ET's and Contractor's works, and advices to the Project Consultant and Project Proponent on a monthly basis

2.2 CONSTRUCTION PROGRESS

2.2.1 3-month rolling construction program of the each Works Contract is enclosed in [Appendix C](#); and the major construction activities undertaken in the Reporting Period is presented in below sub-sections.

Contract 1 (Contract No. NE/2017/07)

2.2.2 The major construction activities of Contract 1 undertaken in this Reporting Period are:-

- Pre-drilling works at Portion II
- Piling works at Portion II

Contract 2 (Contract No. NE/2017/08)

2.2.3 The major construction activities of Contract 2 undertaken in this Reporting Period are:-

- UU Detection Work at Portion VI
- Trial Pit and Pre-drill Work at Portion III & VI

2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 The required documents list below shall be to submit to EPD for retention:

Table 2-1 Documents Submission under Environmental Permit Requirement

EP condition	Submission to EPD	Requirement	Situation
1.11	Commencement date of construction of the Project	no later than 1 month prior to the commencement of construction of the Project	<ul style="list-style-type: none"> Contract 1 notified EPD on 19 Oct 2018 Contract 2 notified EPD on 12 Dec 2018
2.3	The date of setting up the Community Liaison Group (CLG), the membership, the terms of reference and the contact details	At least 1 month before the commencement of construction of the Project	<ul style="list-style-type: none"> CLG setting has submitted to EPD on 9 Oct 2018
2.4	Management Organization of Main Construction Companies	No later than 2 weeks before the commencement of construction of the Project	<ul style="list-style-type: none"> Management Organization of Contract 1 was submitted to EPD on 2 October 2018 Management Organization of Contract 2 was submitted to EPD on 12 December 2018
2.5	Waste Management Plan (WMP)	No later than 1 month before commencement of construction of the Project	<ul style="list-style-type: none"> WMP of Contract 1 was submitted to EPD in 11 October 2018 WMP of Contract 2 was submitted to EPD in 14 December 2018
2.6	Landscape Mitigation Plan (LSMP)	No later than 1 month before commencement of construction of the Project	<ul style="list-style-type: none"> LSMP was submitted on 1 Nov 2018
2.7	Detailed Qualitative Landfill Gas Hazards Assessment (QLGHA)	No later than 1 month before commencement of construction of the Project	<ul style="list-style-type: none"> QLGHA of the Project was submitted to EPD on 1 November 2018

2.3.2 Upon completed baseline monitoring, a Baseline Monitoring Report was verified by IEC on 19 November 2018 and submitted to EPD on that day for endorsement.

2.3.3 The notification of Project dedicated web site to EPD was made on 9 January 2019 (<http://www.envcbltko.hk/>).

2.3.4 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project are presented in *Table 2-2*.

Table 2-2 Status of Environmental Licenses and Permits of the Project Works (Contract 1)

Item	Description	License/Permit Status			
		Permit no./ Account no./ Ref. no.	Valid Period		Status
			From	To	
1	Notification pursuant to Air pollution Control (Construction Dust) Regulation	--	--	--	Notified on 11 July 2018
2	Chemical Waste Producer Registration	5213-839-C1232-19	28 August 2018	N/A	--
3	Water Pollution Control Ordinance - Discharge License	WT00032842-2018	1 Mar 2019	31 Mar 2024	Valid until 31 March 2024
		In progress (Ref:438585)	--	--	Application submitted on 23 October 2018

Item	Description	License/Permit Status			
		Permit no./ Account no./ Ref. no.	Valid Period		Status
			From	To	
4	Billing Account for Disposal of Construction Waste	7031412	24 July 2018	N/A	--
	Billing Account for Disposal of Construction Waste (through Vessel delivering)	7032666	10 January 2019	10 April 2019	Valid until 10 April 2019
5	Marine Dumping Permit	In progress (Ref:439218)	--	--	Application submitted on 9 November 2018
6	Construction Noise Permit	GW-RE0052-19	26 January 2019	25 March 2019	Valid until 25 March 2019
		GW-RE0212-19	26 March 2019	24 May 2019	Valid until 24 May 2019

Remark: Evening marine work at Portion II for Contract 1 was carried out on 11 – 16, 18 - 23 and 26 - 30 Mar 2019

Table 2-3 Status of Environmental Licenses and Permits of the Project Works (Contract 2)

Item	Description	License/Permit Status			
		Permit no./ Account no./ Ref. no.	Valid Period		Status
			From	To	
1	Notification pursuant to Air pollution Control (Construction Dust) Regulation	--	--	--	Notified on 31 October 2018
2	Chemical Waste Producer Registration	5213-839-B2500-04	22 November 2018	N/A	--
3	Water Pollution Control Ordinance - Discharge License	In progress	--	--	Application submitted on 20 December 2018
4	Billing Account for Disposal of Construction Waste	7032702	8 November 2018	N/A	--
5	Construction Noise Permit	GW-RE0905-18	10 December 2018	27 March 2019	Valid until 27 March 2019
		GW-RE0174-19	20 March 2019	19 June 2019	Valid until 19 June 2019

Remark: No evening work and night work was carried out for Contract 2

3. SUMMARY OF ENVIRONMENTAL MONITORING PROGRAMMES AND REQUIREMENTS

3.1 GENERAL

3.1.1 The Environmental Monitoring and Audit Programmes and requirements are set out in the Approved EM&A manual. Environmental issues such as air quality, construction noise and water quality were identified as the key issues during the construction phase of the Project. A summary of EM&A programmes and requirements are presented in the sub-sections below.

3.2 MONITORING PARAMETERS

3.2.1 Monitoring parameters of air quality, noise and water quality are summarized in *Table 3-1*.

Table 3-1 Summary of EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> 1-hour TSP by Real-Time Portable Dust Meter; and 24-hour TSP by High Volume Air Sampler
Noise	<ul style="list-style-type: none"> Leq (30min) in six consecutive Leq(5 min) between 07:00-19:00 on normal weekdays Supplementary information for data auditing, statistical results such as L₁₀ and L₉₀ shall also be obtained for reference.
Water Quality	<ul style="list-style-type: none"> In-situ measurement – Dissolved Oxygen (DO) concentration (mg/L) & saturation (%), pH, Salinity (mg/L), Temperature (°C) and Turbidity (NTU); and Laboratory analysis – SS (mg/L)

3.3 MONITORING LOCATIONS

Air Quality and Construction Noise

3.3.1 According to the Approved EM&A Manual Section 5.4 and Section 6.3, three (3) representative air sensitive receivers (ASR) and four (4) representative noise sensitive receivers were designated as monitoring stations. The designated air quality and noise monitoring locations are listed in *Table 3-2* and *Table 3-3*, and illustrated in *Appendix D*.

Table 3-2 Designated Air Quality Monitoring Location recommended in EM&A Manual

ID	Location in the EM&A Manual	Currently Situation
AM1	Tung Wah Group of Hospitals Aided Primary School & Secondary School	Not yet construct
AM2	Lohas Park Stage 2 (Planned Development in Area 86)	Under Construction
AM3	Lohas Park Stage 3 (Planned Development in Area 86)	Under Construction

Table 3-3 Designated Construction Noise Monitoring Location recommended by EM&A Manual

ID	Location	Currently Situation
CNMS-1	Lohas Park Stage 1(Planned Development in Area 86, Package 5) (Southeast facade)	Under Construction
CNMS-2	Lohas Park Stage 1 (Planned Development in Area 86, Package 6) (Southeast facade)	Under Construction
CNMS-3	Lohas Park Stage 3 (Planned Development in Area 86,Package 11) (West facade)	Under Construction
CNMS-4	Tung Wah Group of Hospitals Aided Primary School & Secondary School (Southwest facade)	Not yet construct

3.3.2 As observed and confirmed by ET and IEC during the joint site visit on 29th August 2018, the designated air quality and noise monitoring locations are under construction or yet to construct. It is considered that these designated locations are not appropriate to perform air quality and noise monitoring. In this regard, alternative locations were proposed as interim arrangement to carry out air quality and noise monitoring before occupation of the designated monitoring location. A letter enclosed with the alternative location proposal and IEC verification (Our Ref: TCS00975/18/300/L0038) was sent to EPD on 19th October 2018 and the proposal was agreed by

EPD. Therefore, air quality and construction noise impact monitoring would be performed at the agreed alternative locations until the designated sensitive receivers occupied and granted the premises.

3.3.3 The agreed alternative monitoring location for impact air quality and noise monitoring are summarized in Table 3-4 and illustrated in *Appendix D*.

Table 3-4 Interim alternative location for air quality and noise monitoring

Location ID	Monitoring Parameter	Location
AM4	1-Hour TSP Air Quality	Podium of Lohas Park Phase 2A (Le Prestige)
AM5	24-Hour TSP Air Quality	Boundary of Site Office near Junction of Wan Po Road and Wan O Road
CNMS-5	Noise (L_{eq} , L_{10} & L_{90})	Podium of Lohas Park Phase 2A (Le Prestige)

Remark: Since 24-Hour TSP Air Quality monitoring is not granted at AM4 Lohas Park Phase 2A, the 24-Hour TSP monitoring was therefore proposed at AM5 which is located at the boundary of the project site office.

Water Quality

3.3.4 According to Table 7.1 of the approved EM&A Manual Section 7.4, two Control Stations (C3 & C4), six (6) sensitive receivers (CC1, CC2, CC3, CC4, CC13 & SWI1) and one (1) Gradient station (I1) are recommended to perform water quality monitoring. Details and coordinate of these water quality monitoring stations are described in *Table 3-5* and the locations is shown in *Appendix D*.

Table 3-5 Location of Water Quality Monitoring Station

Station	Coordinates		Description
	Easting	Northing	
CC1	843201	816416	Sensitive Receiver – Coral Sites at Chiu Keng Wan
CC2	844076	817091	Sensitive Receiver – Coral Sites at Junk Bay
CC3	844606	817941	Sensitive Receiver – Coral Sites at Junk Island
CC4	845444	815595	Sensitive Receiver – Coral Sites at Fat Tong Chau West
CC13	844200	817495	Sensitive Receiver – Coral Sites at Junk Bay near Chiu Keng Wan
SWI1	845512	817442	Sensitive Receiver – Tseung Kwan O Salt Water Intake
C3	843821	816211	Control Station (Ebb Tide) – within Junk Bay
C4	844621	815770	Control Station (Flood Tide) – within Junk Bay
I1	844602	817675	Gradient Station – in between Lam Tin Tunnel (LTT) and CBL

3.4 MONITORING FREQUENCY AND PERIOD

3.4.1 To according with the approved *EM&A Manual*, impact monitoring requirements are presented as follows.

Air Quality Monitoring

3.4.2 Air quality impact monitoring frequency is as follows:

- Once every 6 days of 24-hour TSP and 3 times of 1-hour TSP monitoring; during course of works throughout the construction period

Construction Noise Monitoring

3.4.3 Construction noise monitoring frequency is as follows:

- One set of $Leq(30min)$ measurements in a weekly basis between 07:00 and 19:00 hours on normal weekdays during course of works as throughout the construction period
- If construction works are extended to include works during the hours of 1900-0700, additional weekly impact monitoring shall be carried out during evening and night-time works. Applicable permits under the NCO shall be obtained by the Contractor.

Water Quality (Marine Water) Monitoring

3.4.4 Marine water impact monitoring frequency is as follows:

- Three days a week, at mid ebb and mid flood tides during course of pile excavation works for the bridge pier foundations underway. Moreover, the intervals between 2 consecutive sets of monitoring day shall not be less than 36 hours.

3.5 MONITORING EQUIPMENT

Air Quality Monitoring

3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to prove that the instrument is capable of achieving a comparable results to the HVS. The instrument should be calibrated regularly, and the 1-hour sampling shall be determined on yearly basis by the HVS to check the validity and accuracy of the results measured by direct reading method. The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory. The equipment used for air quality monitoring is listed in **Table 3-6**.

Table 3-6 Air Quality Monitoring Equipment

Equipment		Model
24-hour TSP	High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170
	Calibration Kit	TISCH Model TE-5025A (S/N: 438320)
1- hour TSP	Portable Dust Meter	Laser Dust Monitor Sibata LD-3B Laser Dust Monitor (S/N: 3Y6503)

Noise Monitoring

3.5.2 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms⁻¹. Noise equipment will be used for impact monitoring is listed in **Table 3-7**.

Table 3-7 Construction Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	Rion NL-31 (S/N: 00410221)
Calibrator	Rion NC-74 (S/N: 34657230)
Portable Wind Speed Indicator	Anemometer AZ Instrument 8908

Water Quality Monitoring

3.5.3 For water quality monitoring, the equipment should fulfill the requirement under the Approved *EM&A Manual Section 7.2*. The requirement is summarized below:

- **Dissolved Oxygen and Temperature Measuring Equipment** – The instrument should be a portable, weatherproof dissolved oxygen measuring instrument completed with cable, sensor, comprehensive operation manuals, and should be operable from a DC power source. It should be capable of measuring: dissolved oxygen levels in the range of 0-20 mg/L and 0-200% saturation; and a temperature of 0-45 degrees Celsius. It should have a membrane electrode with automatic temperature compensation complete with a cable of not less than 35 m in length. Sufficient stocks of spare electrodes and cable should be available for replacement where necessary.
- **Turbidity Measurement Equipment** – The instrument shall be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment shall use a DC power source. It shall have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU.
- **Salinity Measurement Instrument** – A portable salinometer capable of measuring salinity in the range of 0-40 ppt should be provided for measuring salinity of the water at each monitoring location.

- **Water Depth Detector** – A portable, battery-operated echo sounder should be used for the determination of water depth at each designated monitoring station. A detector affixed to the bottom of the works boat, if the same vessel is to be used throughout the monitoring programme, is preferred.
- **Positioning Device** – hand-held or boat-fixed type digital Global Positioning System (GPS) with way point bearing indication or other equipment instrument of similar accuracy, should be provided and used during water quality monitoring to ensure the monitoring vessel is at the correct location before taking measurements.
- **Water Sampling Equipment** – A water sampler, consisting of a transparent PVC or glass cylinder of not less than two liters, which can be effectively sealed with cups at both ends, should be used. The water sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth.

3.5.4 Equipment used for water quality impact monitoring is listed in *Table 3-8*.

Table 3-8 Water Monitoring Equipment

Equipment	Model
A Digital Global Positioning System	GPS12 Garmin
Water Depth Detector	Eagle Sonar CUDA 300
Water Sampler	A 2-litre transparent PVC cylinder with latex cups at both ends
Thermometer & DO meter	YSI ProDSS Digital Sampling System Water Quality Meter (S/N: 15H102620/15H103928)
pH meter	
Turbidimeter	
Salinometer	
Sample Container	High density polythene bottles (provided by laboratory)
Storage Container	'Willow' 33-litter plastic cool box with Ice pad

3.6 MONITORING PROCEDURES

Air Quality

1-hour TSP

3.6.1 The 1-hour TSP monitor was a brand named “*Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter*” which is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90° light scattering. The 1-hour TSP monitor consists of the following:

- A pump to draw sample aerosol through the optic chamber where TSP is measured;
- A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
- A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.

24-hour TSP

3.6.2 The equipment used for 24-hour TSP measurement is TISCH, Model TE-5170 TSP High Volume Air Sampler, which complied with *EPA Code of Federal Regulation, Appendix B to Part 50*. The High Volume Air Sampler (HVS) consists of the following:

- An anodized aluminum shelter;
- A 8”x10” stainless steel filter holder;
- A blower motor assembly;
- A continuous flow/pressure recorder;
- A motor speed-voltage control/elapsed time indicator;
- A 7-day mechanical timer, and
- A power supply of 220v/50 Hz

3.6.3 For HVS for 24-hour TSP monitoring, the HVS is mounted in a metallic cage with a top for protection and also it is sat on the existing ground or the roof of building. The flow rate of the HVS between 0.6m³/min and 1.7m³/min will be properly set in accordance with the manufacturer’s instruction to within the range recommended in *EPA Code of Federal*

Regulation, Appendix B to Part 50. Glass Fiber Filter 8" x 10" of TE-653 will be used for 24-Hour TSP monitoring and would be supplied by laboratory. The general procedures of sampling are described as below:-

- A horizontal platform with appropriate support to secure the samples against gusty wind should be provided;
- No two samplers should be placed less than 2 meters apart;
- The distance between the sampler and an obstacle, such as building, must be at least twice the height that the obstacle protrudes above the sample;
- A minimum of 2 meters of separation from any supporting structure, measured horizontally is required;
- Before placing any filter media at the HVS, the power supply will be checked to ensure the sampler work properly;
- The filter paper will be set to align on the screen of HVS to ensure that the gasket formed an air tight seal on the outer edges of the filter. Then filter holder frame will be tightened to the filter hold with swing bolts. The holding pressure should be sufficient to avoid air leakage at the edge.
- The mechanical timer will be set for a sampling period of 24 hours (00:00 mid-night to 00:00 mid-night next day). Information will be recorded on the field data sheet, which would be included the sampling data, starting time, the weather condition at current and the filter paper ID with the initial weight;
- After sampling, the filter paper will be collected and transfer from the filter holder of the HVS to a sealed envelope and sent to a local HOKLAS accredited laboratory for quantifying.

- 3.6.4 All the sampled 24-hour TSP filters will be kept in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal.
- 3.6.5 The HVS used for 24-hour TSP monitoring will be calibrated in two months interval for in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A) to establish a relationship between the follow recorder meter reading in cfm (cubic feet per minute) and the standard flow rate, Qstd, in m³/min. Motor brushes of HVS will be regularly replaced. The calibration certificates of the air quality monitoring equipment used for the impact monitoring and the HOKLAS accredited certificate of laboratory was provided in Appendix G.

Noise Monitoring

- 3.6.6 As referred to in the Technical Memorandum (TM) issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.
- 3.6.7 All noise measurements will be performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq_(30 min) in six consecutive Leq_(5 min) measurements will be used as the monitoring parameter for the time period between 07:00-19:00 hours on weekdays throughout the construction period.
- 3.6.8 The sound level meter will be mounted on a tripod at a height of 1.2 m and placed at the assessment point and oriented such that the microphone is pointed to the site with the microphone facing perpendicular to the line of sight. The windshield will be fitted for all measurements. Where a measurement is to be carried out at a building, the assessment point would normally be at a position 1 m from the exterior of the building façade. Where a measurement is to be made for noise being received at a place other than a building, the assessment point would be at a position 1.2 m above the ground in a free-field situation, i.e. at least 3.5 m away from reflective surfaces such as adjacent buildings or walls.

- 3.6.9 Immediately prior to and following each noise measurement the accuracy of the sound level meter will be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 3.6.10 Noise measurements will not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed will be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 3.6.11 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis. The calibration certificates of noise monitoring equipment used for the impact monitoring was provided in Appendix G.

Marine Water Quality

- 3.6.12 Marine water quality monitoring would be conducted at all designated locations in accordance with Table 7.1 of the approved EM&A Manual. The procedures of water sampling, in-situ measurement and chemical analysis are described as below:
- A Global Positioning System (GPS) will be used to ensure that the correct location was selected prior to sample collection. A portable, battery-operated echo sounder was used for the determination of water depth at each designated monitoring station.
 - The marine water sampler will be lowered into the water body at a predetermined depth. The trigger system of the sampler is activated with a messenger and opening ends of the sampler are closed accordingly then the sample of water is collected.
 - During the sampling, the sampling container will be rinsed to use a portion of the marine water sample before the water sample is transferred to the container. Upon sampling completion, the container will be sealed with a screw cap.
 - Before the sampling process, general information such as the date and time of sampling, weather condition and tidal condition as well as the personnel responsible for the monitoring will be recorded on the monitoring field data sheet.
 - In-situ measurement including water temperature, turbidity, dissolved oxygen, salinity, pH and water depth will be recorded at the identified monitoring station and depth. At each station, marine water samples will be collected at three depths: 1m below water surface, 1m above sea bottom and at mid-depth when the water depth exceeds 6m. Samples at 1m below water surface and 1m above sea bottom will be collected when the water depth is between 3m and 6m. And sample at mid-depth will be taken when the water depth is below 3m.
 - For the in-situ measurement, two consecutive measurements of sampling depth, temperature, dissolved oxygen, salinity, turbidity and pH concentration will be measured at the sea. The YSI ProDSS Multifunctional Meter will be retrieved out of the water after the first measurement and then re-deployed for the second measurement. Where the difference in the value between the first and second readings of each set is more than 25% of the value of the first reading, the reading is discarded and further readings is taken.
 - Marine water sample will be collected by using a water sampler. The high-density polythene bottles will be filled after the water sample collected from the sea. Before the water sample being fills into the sampling bottles, the sampling bottles will be pre-rinsed with the same water sample. The sampling bottles will then be packed in cool-boxes (cooled at 4°C without being frozen), and delivered to HOKLAS accredited laboratory for the chemical analysis as followed APHA *Standard Methods for the Examination of Water and Wastewater* 19ed 2540D, unless otherwise specified.
- 3.6.13 Before each round of monitoring, the dissolved oxygen probe will be calibrated by wet bulb method; a zero check in distilled water will be performed with the turbidity and salinity probes. The turbidity probe also will be checked with a standard solution of known NTU and known value of the pH standard solution were used to check the accuracy of pH value before each

monitoring day. Moreover, all in-situ measurement equipment used marine water monitoring will be calibrated at three months interval.

Laboratory Analysis

3.6.14 All water samples included the duplicate samples, was tested with chemical analysis as specified in the EM&A Manual by a HOKALS accredited laboratory - ALS Technichem (HK) Pty Ltd. The chemicals analysis method and reporting limit show **Table 3-9**.

Table 3-9 Testing Method and Reporting Limit of the Chemical Analysis

Parameter	ALS Method Code	In-house Method Reference ⁽¹⁾	Reporting Limit
Total Suspended Solids	EA025	APHA 2540D	1 mg/L

Note:

1. The exact method shall depend on the laboratory accredited method. APHA = Standard Methods for the Examination of Water and Wastewater by the American Public Health Association.

3.6.15 The determination works will start within 24 hours after collection of the water samples or within the holding time as advised by the laboratory.

Meteorological Information

3.6.16 The meteorological information including wind direction, wind speed, humidity and temperature etc. of impact monitoring is extracted from the closest Tseung Kwan O Hong Kong Observatory Station. Moreover, the data of rainfall and air pressure would be extracted from King’s Park Station.

3.6.17 For marine water quality monitoring, tidal information would be referred to tide gauge at Tai Miu Wan.

3.7 DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

3.7.1 The baseline results form the basis for determining the environmental acceptance criteria for the impact monitoring. A summary of the Action/Limit (A/L) Levels for air quality, construction noise and water quality are shown in **Tables 3-10, 3-11** and **3-12** respectively.

Table 3-10 Action & Limit Levels of Air Quality (1-Hour & 24-Hr TSP)

Monitoring Station	Action Level (µg /m ³)		Limit Level (µg/m ³)	
	1-Hour TSP	24-Hr TSP	1-Hour TSP	24-Hr TSP
AM4	278	NA	500	NA
AM5	NA	190	NA	260

Note: 1-Hour & 24-Hr TSP of Action Level = (Average Baseline Results × 1.3 + Limit level)/2

Table 3-11 Action and Limit Levels for Construction Noise, dB(A)

Monitoring Location	Action Level	Limit Level
CNMS-5	Time Period: 0700-1900 hours on normal weekdays (Leq30min)	
	When one or more documented complaints are received	75 dB(A)
	Time Period: 1900-2300 hours on all days (Leq15min)	
	When one or more documented complaints are received	55 dB(A)
<i>Remarks:</i>		
1. Construction noise monitoring will be resumed at the designated locations CNMS-1, CNMS-2, CNMS-3 and CNMS4 once they are available and permission are granted;		
2. The designated locations CNMS-1, CNMS-2 and CNMS-3 are located at residential building which are still under construction, Limit Level of 75dB(A) will be adopted until they are occupied;		
3. The designated location CNMS-4 is located at planned school and still not yet to construction. When the school occupied and operated, Limit Level of 70dB(A) should be adopted and should be reduced to 65dB(A) during examination period; and		
4. If construction works are required during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority shall be followed.		

Table 3-12 Action and Limit Levels for Water Quality

Monitoring Station	Depth Average of SS (mg/L)			
	Action Level		Limit Level	
CC1	7.8	OR 120% of upstream control station at the same tide of the same day (Control Station C3 at Ebb tide and Control Station C4 at Flood tide), whichever is higher	9.3	OR 130% of upstream control station at the same tide of the same day (Control Station C3 at Ebb tide and Control Station C4 at Flood tide), whichever is higher
CC2	9.0		9.2	
CC3	8.2		9.0	
CC4	13.8		15.4	
CC13	8.9		10.3	
SWI1	8 mg/L		10 mg/L	
Monitoring Location	Dissolved Oxygen (mg/L)			
	Depth Average of Surface and Mid-depth		Bottom	
	Action Level	Limit Level	Action Level	Limit Level
CC1	5.8	5.7	5.3	5.2
CC2	5.8	5.7	5.3	5.1
CC3	5.5	5.4	4.9	4.7
CC4	5.7	5.7	5.5	5.4
CC13	5.6	5.5	5.3	5.2
SWI1	5.4	4.8	5.1	5.0
Monitoring Location	Depth Average of Turbidity (NTU)			
	Action Level		Limit Level	
CC1	5.8	OR 120% of upstream control station at the same tide of the same day (Control Station C3 at Ebb tide and Control Station C4 at Flood tide), whichever is higher	6.0	OR 130% of upstream control station at the same tide of the same day (Control Station C3 at Ebb tide and Control Station C4 at Flood tide), whichever is higher
CC2	4.6		5.5	
CC3	4.8		5.4	
CC4	6.1		7.1	
CC13	6.0		6.3	
SWI1	6.1		7.1	

3.7.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in [Appendix E](#).

3.8 DATA MANAGEMENT AND DATA QA/QC CONTROL

3.8.1 All monitoring data will be handled by the ET's in-house data recording and management system. The monitoring data recorded in the equipment will be downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data will input into a computerized database properly maintained by the ET. The laboratory results will be input directly into the computerized database and checked by personnel other than those who input the data.

3.8.2 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.

4. AIR QUALITY MONITORING

4.1 GENERAL

4.1.1 In the Reporting Period, 1-Hour TSP and 24-Hr TSP of air quality monitoring were respectively performed at interim alternative monitoring locations AM4 and AM5. The air quality monitoring schedule is presented in [Appendix F](#).

4.1.2 Valid calibration certificates of monitoring equipment are shown in [Appendix G](#) and the monitoring results are summarized in the following sub-sections

4.2 RESULTS OF AIR QUALITY MONITORING IN THE REPORTING MONTH

4.2.1 During the Reporting Period, **15** sessions of 1-hour TSP and **5** sessions of 24-hours TSP monitoring were carried out and the monitoring results are summarized in **Table 4-1**. The detailed 24-hour TSP monitoring data are presented in [Appendix H](#) and the relevant graphical plots are shown in [Appendix I](#).

Table 4-1 1-Hour and 24-Hour TSP Air Quality Impact Monitoring Results

AM5		AM4				
24-Hr TSP ($\mu\text{g}/\text{m}^3$)		1-Hour TSP ($\mu\text{g}/\text{m}^3$)				
Date	Meas. Result	Date	Start Time	1 st Meas.	2 nd Meas.	3 rd Meas.
4-Mar-19	165	2-Mar-19	10:08	59	57	55
9-Mar-19	163	8-Mar-19	9:37	43	44	42
15-Mar-19	127	14-Mar-19	9:18	54	50	46
21-Mar-19	97	20-Mar-19	9:22	76	83	85
27-Mar-19	169	26-Mar-19	9:48	59	57	55

4.2.2 As shown in **Table 4-1**, all the 1-hour TSP and 24-hour TSP monitoring results were below the Action / Limit Levels. No Notification of Exceedance (NOE) was issued in this Reporting Period.

4.2.3 The meteorological data during impact monitoring period is summarized in [Appendix J](#).

5. CONSTRUCTION NOISE MONITORING

5.1 GENERAL

5.1.1 In the Reporting Period, construction noise quality monitoring was performed at interim alternative monitoring location CNMS-5. The noise quality monitoring schedule is presented in [Appendix F](#).

5.1.2 Valid calibration certificates of monitoring equipment is shown in [Appendix G](#) and the construction noise monitoring results are summarized in the following sub-sections

5.2 RESULTS OF NOISE MONITORING

5.2.1 4 sessions of daytime construction noise monitoring were performed at the interim alternative location CNMS-5 in the reporting period. The daytime noise monitoring results at interim alternative location is summarized in [Table 5-1](#). The detailed noise monitoring data are presented in [Appendix H](#) and the relevant graphical plots are shown in [Appendix I](#).

Table 5-1 Daytime Construction Noise Impact Monitoring Results

Date	Time of Starting	Time of Finishing	Measurement Result (dB(A))	
			L _{eq30min}	Façade Correction
8-Mar-19	10:14	11:46	62.7	NA
14-Mar-19	10:28	11:54	63.7	NA
20-Mar-19	10:54	14:11	65.8	NA
26-Mar-19	13:42	11:12	61.8	NA

5.2.2 As shown in [Table 5-1](#), all the measured results were below 75dB(A) of the acceptance criteria. Furthermore, no complaint on daytime construction noise was registered, indicating no exceedance of Action Level.

5.2.3 In the reporting period, evening marine work was carried out by Contractor of Contract 1 at Portion II from 11 to 16, 18 to 23 and 26 to 30 March 2019. Additional weekly evening construction noise monitoring were performed at the interim alternative location CNMS-5 in the reporting period. The evening noise monitoring results at interim alternative location is summarized in [Table 5-2](#). The detailed noise monitoring data are presented in [Appendix H](#).

Table 5-2 Evening Construction Noise Impact Monitoring Results

Date	Time of Starting	Time of Finishing	Measurement Result (dB(A))	
			L _{eq15min}	Façade Correction
15-Mar-19	19:06	19:21	59.0	NA
21-Mar-19	19:24	19:39	62.2	NA
28-Mar-19	19:16	19:31	61.3	NA

5.2.4 According to [Table 5-2](#), the measured results on 15, 21 and 28 March 2019 were higher than 55dB(a) of the acceptance criteria, Therefore a total of three (3) limit level evening noise monitoring exceedances were recorded in the reporting period and investigations were undertaken by ET accordingly. Since the evening noise monitoring result obtained on 15, 21 and 28 March 2019 were within the range of evening noise obtained from baseline monitoring and external noise source such as traffic noise was noted during the course of monitoring, it was considered the exceedances recorded were unlikely due to the Project.

6. WATER QUALITY MONITORING

6.1 GENERAL

6.1.1 The water quality monitoring schedule is presented in *Appendix F* and the monitoring results are summarized in the following sub-sections.

6.1.2 Valid calibration certificates of monitoring equipment and the laboratory accredited certificate is shown in *Appendix G*. The water quality monitoring results are summarized in the following sub-sections.

6.2 RESULTS OF WATER QUALITY MONITORING

6.2.1 In this Reporting Period, a total of **13** sampling days were performed for marine water monitoring at the nine designated locations. Monitoring results of 3 key parameters: dissolved oxygen (DO), turbidity and suspended solids are summarized in *Tables 6-1* to *6-4*.

Table 6-1 Results Summary of Depth Average (Surface & Middle Layer) of DO (mg/L)

Tidal	Sampling date	CC1	CC2	CC3	CC4	CC13	SWI1	C3	C4	I1
Mid-Ebb	2-Mar-19	7.1	7.2	7.1	7.2	7.2	7.2	7.2	7.2	7.1
	4-Mar-19	7.2	7.2	7.4	7.1	7.2	7.2	7.2	7.3	7.3
	7-Mar-19	6.8	6.9	6.8	6.9	6.8	6.4	6.7	6.8	6.9
	9-Mar-19	6.8	6.7	6.6	6.8	6.7	6.5	6.7	6.7	6.5
	11-Mar-19	6.4	6.4	6.4	6.4	6.4	6.2	6.2	6.3	6.4
	13-Mar-19	6.5	6.6	6.7	6.3	6.5	6.5	6.3	6.3	6.6
	15-Mar-19	6.7	6.8	6.3	6.6	6.5	6.5	6.6	6.9	6.5
	18-Mar-19	7.0	6.8	6.8	6.6	6.7	6.4	7.0	7.4	6.7
	20-Mar-19	6.8	6.6	6.6	6.6	6.5	6.4	6.5	6.5	6.6
	22-Mar-19	6.7	6.5	6.2	6.3	6.3	6.4	6.4	6.5	6.3
	25-Mar-19	6.7	6.8	6.5	6.6	6.6	6.7	6.8	6.8	6.7
	27-Mar-19	6.7	6.7	6.5	6.4	6.7	6.7	6.6	6.9	6.5
30-Mar-19	6.6	6.6	6.5	6.4	6.7	6.7	6.6	6.8	6.5	
Mid-Flood	2-Mar-19	7.2	7.2	7.1	7.2	7.0	7.1	7.1	7.3	7.2
	4-Mar-19	7.3	7.3	7.4	7.2	7.2	7.2	7.2	7.4	7.3
	7-Mar-19	6.8	6.9	6.9	6.9	6.8	6.6	6.8	6.6	6.8
	9-Mar-19	6.6	6.5	6.6	6.4	6.5	6.6	6.7	6.7	6.6
	11-Mar-19	6.5	6.4	6.3	6.2	6.4	6.2	6.3	6.3	6.4
	13-Mar-19	6.3	6.4	6.5	6.0	6.4	6.2	6.4	6.2	6.5
	15-Mar-19	6.4	6.5	6.6	6.9	6.6	6.1	6.6	6.7	6.7
	18-Mar-19	7.0	6.8	6.8	6.8	6.8	6.7	6.7	7.3	6.8
	20-Mar-19	6.4	6.4	6.2	6.5	6.4	6.3	6.5	6.7	6.4
	22-Mar-19	6.2	6.2	6.5	6.3	6.3	6.2	6.4	6.5	6.3
	25-Mar-19	6.6	6.5	6.4	6.7	6.5	6.6	6.7	6.7	6.5
	27-Mar-19	6.6	6.7	6.4	6.6	6.6	6.6	6.6	6.6	6.5
30-Mar-19	6.6	6.6	6.4	6.6	6.6	6.6	6.6	6.6	6.5	

Table 6-2 Results Summary of Bottom Depth of DO (mg/L)

Tidal	Sampling date	CC1	CC2	CC3	CC4	CC13	SWI1	C3	C4	I1
Mid-Ebb	2-Mar-19	7.0	7.0	7.1	NA	7.1	7.2	7.2	7.1	7.1
	4-Mar-19	7.1	7.0	7.2	NA	7.1	7.2	7.1	7.1	7.0
	7-Mar-19	6.7	6.7	6.8	NA	6.7	6.4	6.7	6.8	6.7
	9-Mar-19	6.7	6.7	6.5	NA	6.5	6.5	6.7	6.7	6.6
	11-Mar-19	6.2	6.3	6.1	NA	6.2	6.2	6.1	6.4	6.1
	13-Mar-19	6.3	6.3	6.3	NA	6.5	6.2	6.3	6.5	6.4
	15-Mar-19	6.5	6.4	6.2	NA	6.5	6.5	6.5	6.5	6.4
	18-Mar-19	6.6	6.6	6.7	NA	6.5	6.4	6.7	7.0	6.6
	20-Mar-19	6.6	6.7	6.5	NA	6.5	6.3	5.8	6.5	6.3
22-Mar-19	6.6	6.4	5.9	NA	6.4	5.9	6.6	6.5	6.3	

Tidal	Sampling date	CC1	CC2	CC3	CC4	CC13	SWI1	C3	C4	I1
	25-Mar-19	6.7	6.7	6.4	NA	6.6	6.6	6.7	6.7	6.5
	27-Mar-19	6.5	6.4	6.5	NA	6.5	6.6	6.5	6.6	6.4
	30-Mar-19	6.5	6.4	6.2	NA	6.5	6.7	6.5	6.6	6.4
Mid-Flood	2-Mar-19	7.1	7.1	7.2	NA	7.1	7.2	7.1	7.3	7.1
	4-Mar-19	7.2	7.1	7.3	NA	7.1	7.2	7.1	7.2	7.0
	7-Mar-19	6.7	6.7	6.7	NA	6.7	6.7	6.7	6.6	6.7
	9-Mar-19	6.5	6.6	6.6	NA	6.5	6.5	6.8	6.8	6.6
	11-Mar-19	6.4	6.3	6.1	NA	6.2	6.2	6.3	6.5	6.3
	13-Mar-19	6.2	6.2	6.3	NA	6.3	6.1	6.4	6.6	6.4
	15-Mar-19	6.3	6.3	6.0	NA	6.3	6.1	6.4	6.5	6.6
	18-Mar-19	6.8	6.9	6.7	NA	6.7	6.5	6.0	6.8	6.6
	20-Mar-19	6.3	6.4	6.0	NA	6.2	6.1	6.7	6.7	6.2
	22-Mar-19	6.1	6.3	6.2	NA	6.0	6.0	6.5	6.6	6.1
	25-Mar-19	6.5	6.6	6.4	NA	6.5	6.5	6.7	6.7	6.5
	27-Mar-19	6.5	6.4	6.0	NA	6.5	6.5	6.5	6.6	6.5
30-Mar-19	6.4	6.4	6.0	NA	6.5	6.5	6.5	6.6	6.4	

Remark: No Dissolved Oxygen (Bottom) monitoring data available for CC4 due to the water depth measured at CC4 during the monitoring days were less than 3 meters.

Table 6-3 Results Summary of Depth Average of Turbidity (NTU)

Tidal	Sampling date	CC1	CC2	CC3	CC4	CC13	SWI1	C3	C4	I1
Mid-Ebb	2-Mar-19	0.6	0.9	0.8	1.9	0.5	0.5	0.5	0.6	0.9
	4-Mar-19	0.9	1.0	1.1	1.7	0.9	0.8	0.8	0.8	1.2
	7-Mar-19	0.8	0.8	0.9	0.6	1.0	2.0	0.8	0.6	1.3
	9-Mar-19	1.0	1.0	0.9	1.5	2.2	0.9	1.1	1.1	1.6
	11-Mar-19	0.6	0.3	0.4	0.7	1.0	0.3	0.4	0.4	0.7
	13-Mar-19	0.4	0.4	0.5	0.5	0.4	0.5	0.3	0.5	0.9
	15-Mar-19	0.9	0.8	1.7	0.8	1.0	1.4	0.7	0.9	1.1
	18-Mar-19	1.0	0.8	0.5	0.6	1.3	0.4	0.5	0.9	0.6
	20-Mar-19	1.4	1.3	1.4	1.4	1.3	1.2	1.4	1.2	1.0
	22-Mar-19	0.5	0.5	1.9	0.6	1.5	0.5	0.4	0.5	0.6
	25-Mar-19	1.1	1.2	1.3	1.4	1.3	0.7	0.9	1.2	1.3
	27-Mar-19	1.2	1.5	1.4	1.5	1.1	0.8	1.6	1.2	1.5
30-Mar-19	1.4	1.5	1.6	1.5	1.2	0.8	1.5	1.9	1.5	
Mid-Flood	2-Mar-19	0.5	0.6	0.7	4.8	1.3	0.5	0.4	0.3	1.0
	4-Mar-19	0.9	1.0	1.1	1.1	1.1	1.2	0.8	0.9	1.3
	7-Mar-19	0.9	1.4	1.1	1.0	1.0	1.5	0.9	0.8	1.2
	9-Mar-19	0.9	0.8	1.2	1.0	2.7	0.9	1.2	1.0	1.0
	11-Mar-19	0.4	0.3	1.0	0.5	0.8	0.8	0.6	0.7	0.8
	13-Mar-19	0.5	0.6	0.7	0.3	0.4	0.5	0.9	0.7	0.6
	15-Mar-19	1.0	1.3	1.1	1.0	1.1	1.9	0.9	1.0	1.0
	18-Mar-19	0.7	0.7	0.6	0.5	2.3	0.5	0.8	0.6	1.0
	20-Mar-19	1.3	1.7	1.3	1.7	1.4	1.4	1.2	1.6	1.1
	22-Mar-19	1.4	0.9	0.3	0.8	0.5	0.5	0.6	1.0	0.4
	25-Mar-19	1.1	0.7	1.3	1.0	0.7	1.0	1.3	1.3	0.8
	27-Mar-19	1.0	1.3	2.2	1.0	1.0	0.9	1.5	1.4	1.2
30-Mar-19	1.1	1.4	2.0	1.0	0.9	0.9	1.6	1.3	1.3	

Table 6-4 Results Summary of Depth Average of Suspended Solids (mg/L)

Tidal	Sampling date	CC1	CC2	CC3	CC4	CC13	SWI1	C3	C4	II
Mid-Ebb	2-Mar-19	1.1	1.5	2.2	3.0	1.2	1.9	1.6	1.4	1.5
	4-Mar-19	1.0	2.7	1.2	2.5	1.4	2.5	1.0	1.8	1.8
	7-Mar-19	1.8	1.4	2.0	1.3	2.3	4.4	1.7	1.9	1.6
	9-Mar-19	1.2	1.2	2.1	2.5	4.9	1.6	1.0	1.0	3.4
	11-Mar-19	3.6	3.1	2.7	2.0	3.6	2.5	1.8	3.7	2.3
	13-Mar-19	3.3	5.4	5.4	6.4	4.1	5.9	4.4	3.3	4.7
	15-Mar-19	2.4	2.3	3.0	2.5	3.2	2.9	1.5	1.6	2.0
	18-Mar-19	3.4	3.6	2.7	2.5	7.6	3.4	2.9	2.0	4.0
	20-Mar-19	3.8	4.9	5.7	5.0	6.6	5.8	6.0	5.2	5.8
	22-Mar-19	1.1	1.0	1.0	1.2	1.2	1.2	2.1	2.2	1.2
	25-Mar-19	4.8	5.3	5.6	5.5	4.9	3.9	6.6	4.9	4.5
	27-Mar-19	2.8	4.2	3.2	3.5	3.3	3.5	2.2	1.4	2.5
30-Mar-19	2.2	2.5	5.8	3.7	2.2	2.3	1.9	1.9	2.2	
Mid-Flood	2-Mar-19	1.2	2.2	1.6	2.5	2.8	2.2	2.1	1.9	2.0
	4-Mar-19	1.9	2.7	1.2	1.2	1.8	3.8	2.3	1.7	1.2
	7-Mar-19	1.5	2.4	1.9	1.5	1.9	1.7	2.3	1.7	4.4
	9-Mar-19	1.3	1.5	1.8	2.7	6.4	2.0	1.6	2.0	1.6
	11-Mar-19	2.8	2.5	3.7	5.1	2.8	3.5	2.5	3.2	3.1
	13-Mar-19	4.9	3.4	4.0	5.6	4.7	5.5	7.3	7.4	6.7
	15-Mar-19	2.7	2.9	1.8	2.0	3.0	4.6	1.8	2.7	2.3
	18-Mar-19	3.3	3.7	2.5	2.8	4.2	2.0	2.8	4.3	2.2
	20-Mar-19	7.1	7.3	5.0	6.5	9.8	14.6	7.2	7.8	6.0
	22-Mar-19	1.3	1.3	1.4	1.5	1.7	1.9	1.9	1.8	1.9
	25-Mar-19	6.8	6.8	6.0	4.9	3.7	7.6	7.6	3.7	4.1
	27-Mar-19	3.2	3.2	3.2	2.7	4.9	3.5	2.1	1.8	2.7
30-Mar-19	2.0	2.4	2.2	2.8	3.3	4.1	2.7	4.3	5.0	

Remark: *Italic and bold value indicated Action Level exceedance*
Underlined and bold value indicated Limit Level exceedance

- 6.2.2 During the Reporting Period, field measurements showed that temperatures of marine water were within 19.1°C to 21.3°C; the salinity concentrations within 32.2 to 35.5 ppt and pH values within 8.0 to 8.6.
- 6.2.3 The monitoring results including in-situ measurements and laboratory testing results are provided in [Appendix H](#). The graphical plots are shown in [Appendix I](#).
- 6.2.4 A summary of exceedances for the four parameters: dissolved oxygen (DO), turbidity and suspended solids (SS) are shown in [Table 6-5](#).

Table 6-5 Summary of Water Quality Exceedance

Station	DO (Ave of Top & mid-depth)		DO (Bottom Depth)		Turbidity (Depth Ave)		SS (Depth Ave)		Total Exceedance for the Station	
	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
CC1	0	0	0	0	0	0	0	0	0	0
CC2	0	0	0	0	0	0	0	0	0	0
CC3	0	0	0	0	0	0	0	0	0	0
CC4	0	0	NA	NA	0	0	0	0	0	0
CC13	0	0	0	0	0	0	1	0	1	0
SWI1	0	0	0	0	0	0	0	1	0	1
No of Exceedance	0	0	0	0	0	0	1	1	1	1

- 6.2.5 In this Reporting Period, a total of one (1) Action Level and one (1) Limit Level exceedances of Suspended Solids recorded.
- 6.2.6 Upon confirmation of the monitoring result, Notification of Exceedances (NOEs) have been issued to relevant parties. Investigation for the cause of exceedance was carried out by ET subsequently.
- 6.2.7 As advised by the Contractor of Contract 1, pre-drilling work and excavation work by Reverse Circulation Drill (RCD) for bored pile were carried out on 20 March 2019. As water quality mitigation measures, silt curtains were properly implemented and maintained at locations in accordance with EP's condition. No abnormal and turbid discharge made from the construction site was observed during the course of marine water sampling. It is considered that the exceedances of suspended solid recorded in this period were unlikely caused by the Project. Nevertheless, the Contractor was reminded to check the implementation of silt curtain regularly to ensure no seepage of muddy water into the marine water body.

7. WASTE MANAGEMENT

7.1 GENERAL WASTE MANAGEMENT

7.1.1 Waste management would be carried out by an on-site Environmental Officer or an Environmental Consultant from time to time.

7.2 RECORDS OF WASTE QUANTITIES

7.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste; and
- General Refuse

7.2.2 According to the information provided by Contractor of Contract 1 and Contract 2, waste disposal was made in the Reporting period are summarized in *Tables 7-1* and *7-2*.

Table 7-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
C&D Materials (Inert) ('000m ³)	0.042	TKO 137	0.042	TKO 137
Reused in this Contract (Inert) ('000m ³)	0	-	0	-
Reused in other Projects (Inert) ('000m ³)	0	-	0	-
Disposal as Public Fill (Inert) ('000m ³)	0.042	TKO 137	0.042	TKO 137

Table 7-2 Summary of Quantities of C&D Wastes

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
Recycled Metal ('000kg)	0	-	0	-
Recycled Paper / Cardboard Packing ('000kg)	0.029	Collected by paper recycling company	0	-
Recycled Plastic ('000kg)	0	-	0	-
Chemical Wastes ('000kg)	0	-	0	-
General Refuses ('000m ³)	0.081	NENT	0.229	NENT

7.2.3 The Monthly Summary Waste Flow Table of the Contracts 1 and Contract 2 are shown in [Appendix K](#).

8. SITE INSPECTION

8.1 REQUIREMENTS

8.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

8.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

Contract 1

8.2.1 In this Reporting Month, weekly joint site inspection to evaluate site environmental performance for the *Contract 1* was carried out by the Project Consultant, ET and the Contractor on **6, 13, 18, 20 & 29 March 2019**. Moreover, the Independent Environmental Checker (IEC) perform monthly site inspection was on **13 March 2019**. During site inspections, no non-compliance was noted.

8.2.2 The findings / deficiencies of *Contract 1* that observed during the weekly site inspection are listed in **Table 8-1** and the site layout plan was provided in **Appendix A**.

Table 8-1 Site Observations of the Contract 1

Date	Findings / Deficiencies	Follow-Up Status
27 February 2019	<p><u>Observation:</u></p> <ul style="list-style-type: none"> Sorting should be provided for the waste dispose from site. C&D waste and general refuse storage in the same waste skip was observed. (Works Area A) Proper dust mitigation measures should be provided for stockpile storage over-night. (Portion V) 	<ul style="list-style-type: none"> Proper notice was displayed in the waste skip to identify the type of waste storage area. (Rectified on 6 March 2019) Stockpile storage over-night had been covered with tarpaulin sheets to reduce dust impact. (Rectified on 6 March 2019)
6 March 2019	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection. 	<ul style="list-style-type: none"> NA
13 March 2019	<p><u>Observation:</u></p> <ul style="list-style-type: none"> Hole under the drip tray should be plugged properly to prevent leakage. (Works Area A) Oil and water mixture cumulated inside the drip tray should be cleared to prevent leakage into the water body. (Portion II) Drip tray should be provided for chemical storage on-site. (Portion II) Silt-curtain should be installed properly. Part of the silt-curtain damage was observed. (Portion II, Jack-up barge) 	<ul style="list-style-type: none"> Hole under the drip tray had been plugged properly. (Rectified on 18 March 2019) Oil and water mixture cumulated inside the drip tray had been cleaned and treated as chemical waste. (Rectified on 18 March 2019) Drip tray had been provided for chemical storage on-site. (Rectified on 18 March 2019) Silt-curtain had been fixed properly. (Rectified on 18 March 2019)
18 March 2019	<p><u>Observation:</u></p> <ul style="list-style-type: none"> Stagnant water cumulated inside the temporary u-channel should be cleaned to prevent mosquito breeding. (Works Area A) 	<ul style="list-style-type: none"> Removal work of stagnant water inside the temporary u-channel was implemented. (Rectified on 20 March 2019)

Date	Findings / Deficiencies	Follow-Up Status
	<ul style="list-style-type: none"> Gap was observed at the over-lap area of the silt curtain. Proper maintenance should be provided for the silt curtain. (Portion II – W2) 	<ul style="list-style-type: none"> The silt curtain was fixed and no gap was observed at the overlap area of silt curtain. (Rectified on 20 March 2019)
20 March 2019	<p><u>Observation:</u></p> <ul style="list-style-type: none"> Silt curtain should be fixed properly before the drilling works commence. (Jack-up Barge – Portion II) 	<ul style="list-style-type: none"> Silt curtain was fixed before the drilling works commence. (Rectified before 29 March 2019)
29 March 2019	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection. 	<ul style="list-style-type: none"> NA

Contract 2

8.2.3 In this Reporting Month, weekly joint site inspection to evaluate site environmental performance for the *Contract 2* were carried out by the Project Consultant, ET and the Contractor on **6, 13, 18, 20 & 29 March 2019**. Moreover, the Independent Environmental Checker (IEC) perform monthly site inspection was on **13 March 2019**. During site inspections, no non-compliance was noted.

8.2.4 The findings / deficiencies of *Contract 2* that observed during the weekly site inspection are listed in **Table 8-2** and the site layout plan was provided in **Appendix A**.

Table 8-2 Site Observations of the Contract 2

Date	Findings / Deficiencies	Follow-Up Status
6 March 2019	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection 	<ul style="list-style-type: none"> Nil
13 March 2019	<p><u>Observation:</u></p> <ul style="list-style-type: none"> Drip tray should be provided for chemical storage on-site. (Works Area B) 	<ul style="list-style-type: none"> Chemical container storage on-site without drip tray had been removed. (Rectified on 18 March 2019)
18 March 2019	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection 	<ul style="list-style-type: none"> Nil
20 March 2019	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection 	<ul style="list-style-type: none"> Nil
29 March 2019	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection 	<ul style="list-style-type: none"> Nil

9. LANDFILL GAS MONITORING

9.1 GENERAL REQUIREMENT

- 9.1.1 Pursuant to Section 13 of the Project’s EM&A Manual, Landfill gas monitoring shall perform during construction activities within the 250m Consultation Zone of Tseung Kwan O Stage II & III Landfill. For landfill gas monitoring requirements, pre entry and routine measurement shall be undertaken in accordance with the *Factories and Industrial Undertaking (Confined Spaces) Regulation*.
- 9.1.2 According to Environmental Mitigation Implementation Schedule (EMIS) S14.7.6, portable monitoring equipment can be used to conduct landfill gas monitoring. Moreover, the frequency and areas to be monitored should be set down prior to commencement of the works either by the Safety Officer or by an appropriately qualified person.

9.2 LIMIT LEVELS AND EVENT AND ACTION PLAN

- 9.2.1 In event of the trigger levels specified in Table 14.6 of the EIA report being exceeded, a person, such as the Safety Officer, shall be nominated, with deputies, to be responsible for dealing with any emergency which may occur due to LFG. In an emergency situation the nominated person, or his deputies, shall have the necessary authority and shall ensure that the confined space is evacuated and the necessary works implemented for reducing the concentrations of gas. The Limit levels and relevant Action Plans for landfill gas detected in utilities and any on-site areas following construction is listed in *Table 9-1*.

Table 9-1 Actions in the Event of Landfill Gas Being Detected in Excavations

Parameter	Limit Level	Actions
Methane	>10% LEL (i.e. >0.5% by volume)	<ul style="list-style-type: none"> Post “No Smoking” signs Prohibit hot works Ventilate to restore methane to <10% LEL
	>20% LEL (i.e. >1% by volume)	<ul style="list-style-type: none"> Stop excavation works Evacuate personnel/prohibit entry Increase ventilation to restore methane to <10% LEL
Carbon dioxide	>0.5%	<ul style="list-style-type: none"> Ventilate to restore carbon dioxide to <0.5%
	>1.5%	<ul style="list-style-type: none"> Stop excavation works Evacuate personnel/prohibit entry Increase ventilation to restore carbon dioxide to <0.5%
Oxygen	<19%	Ventilation to restore oxygen >19%
	<18%	<ul style="list-style-type: none"> Stop excavation works Evacuate personnel/prohibit entry Increase ventilation to restore oxygen to >19%

- 9.2.2 In the event of the trigger levels specified in Table 9-1 being exceeded, the Safety Officer shall be responsible for dealing with any emergency which may occur due to landfill gas.

9.3 LANDFILL GAS MONITORING

- 9.3.1 Since the major construction activities under the Project were not yet commenced within the 250m Consultation Zone of Tseung Kwan O Stage II & III Landfill, no landfill gas monitoring was undertaken by the Contractors in the Reporting Period.

10. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

10.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

10.1.1 In the Reporting Period, one (1) environmental complaint was received with respect to the marine water concerns arising from Contract 1 of the Project. Besides, no summons and prosecution under the EM&A Programme was lodged for the project. Investigation for the complaint was undertaken by the ET and presented below.

Complaint received for Contract 1

10.1.2 EPD referred a case to CEDD on 14 March 2019, which the complainant complained about muddy water and mud was discharged from work barges under CBL between 7:00 pm – 10:00 pm. Joint site inspection was carried out on 18 March 2019 and the status of implemented mitigation measures provided by Contractor of Contract 1 was inspected. It was observed that water mitigation measures including silt curtain and cofferdam are properly implemented on site and no sign of muddy discharge was observed. Nevertheless, the Contractor of Contract 1 was reminded to strictly implement all the water mitigation measures as stated in EP and EM&A Manual. Investigation Report has been completed by ET and verified by IEC.

10.1.3 The statistical summary table of environmental complaint is presented in *Tables 10-1, 10-2 and 10-3*.

Table 10-1 Statistical Summary of Environmental Complaints

Reporting Period	Contract	Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 – 31 March 2019	1	1	1	Marine Water
1 – 31 March 2019	2	0	0	NA

Table 10-2 Statistical Summary of Environmental Summons

Reporting Period	Contract	Environmental Summons Statistics		
		Frequency	Cumulative	Summons Nature
1 – 31 March 2019	1	0	0	NA
1 – 31 March 2019	2	0	0	NA

Table 10-3 Statistical Summary of Environmental Prosecution

Reporting Period	Contract	Environmental Prosecution Statistics		
		Frequency	Cumulative	Prosecution Nature
1 – 31 March 2019	1	0	0	NA
1 – 31 March 2019	2	0	0	NA

11. IMPLEMENTATION STATUS OF MITIGATION MEASURES

11.1 GENERAL REQUIREMENTS

11.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in [Appendix L](#).

11.1.2 The Contractors had been implementing the required environmental mitigation measures according to the Environmental Monitoring and Audit Manual subject to the site condition. Environmental mitigation measures generally implemented by the Contractors in this Reporting Month are summarized in [Table 11-1](#).

Table 11-1 Environmental Mitigation Measures in the Reporting Month

Issues	Environmental Mitigation Measures
Construction Noise	<ul style="list-style-type: none"> Regularly to maintain all plants, so only the good condition plants were used on-site ; If possible, all mobile plants onsite operation has located far from NSRs; When machines and plants (such as trucks) were not in using, it was switched off; Wherever possible, plant was prevented oriented directly the nearby NSRs; Provided quiet powered mechanical equipment to use onsite; Weekly noise monitoring was conducted to ensure construction noise meet the criteria.
Air Quality	<ul style="list-style-type: none"> Stockpile of dusty material was covered entirely with impervious sheeting or sprayed with water so as to maintain the entire surface wet; The construction plants regularly maintained to avoid the emissions of black smoke; The construction plants switched off when it not in use; Water spraying on haul road and dry site area was provided regularly; Where a vehicle leaving the works site is carrying a load of dusty materials, the load has covered entirely with clean impervious sheeting; and Before any vehicle leaving the works site, wheel watering has been performed.
Water Quality	<ul style="list-style-type: none"> Debris and refuse generated on-site collected daily; Oils and fuels were stored in designated areas; The chemical waste storage as sealed area provided; Site hoarding with sealed foot were provided surrounding the boundary of working site to prevent wastewater or site surface water runoff get into public areas; and Portable chemical toilets were provided on-site. A licensed contractor was regularly disposal and maintenance of these facilities. Silt curtain was installed and maintained in accordance with EP condition
Waste and Chemical Management	<ul style="list-style-type: none"> Excavated material reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible; Waste arising kept to a minimum and be handled, transported and disposed of in a suitable manner; Disposal of C&D wastes to any designated public filling facility and/or landfill followed a trip ticket system; and Chemical waste handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.
General	<ul style="list-style-type: none"> The site is generally kept tidy and clean. Mosquito control is performed to prevent mosquito breeding on site.

11.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

11.2.1 Tentative construction activities to be undertaken in **April 2019** should be included:-

Contract 1

- Pre-drilling Works at Portion II
- Piling Works at Portion II

Contract 2

- Trial Pit Work at Portion II & VI
- Pre-drill Work at Portion VI
- Bored pile construction work (Portion VI)
- Sheet pile construction work (Portion VI)

11.3 IMPACT FORECAST

11.3.1 Potential environmental impacts arising from the works of the Contracts 1 and Contract 2 include:

- Construction waste
- Air quality
- Construction noise
- Water quality

11.3.2 Environmental mitigation measures will be properly implemented and maintained as per the Mitigation Implementation Schedule in [Appendix L](#) to ensure site environmental performance is acceptable.

12. CONCLUSIONS AND RECOMMENDATIONS


12.1 CONCLUSIONS

- 12.1.1 This is the monthly EM&A report as presented the monitoring results and inspection findings for the reporting period from *1st* to *31st March 2019*.
- 12.1.2 In the Reporting Period, no daytime construction noise monitoring results that triggered the Limit Level was recorded and no noise complaint (which is an Action Level exceedance) was received by the Project Consultant, EPD and the Contractors. However, three (3) evening additional construction noise monitoring results triggered the Limit Level. Investigation was undertaken by ET and it was considered that the exceedances recorded are unlikely caused by the Project.
- 12.1.3 In this Reporting Period, no 1-Hour TSP or 24-Hr TSP air quality monitoring exceedance was recorded. No NOE or the associated corrective actions were therefore issued.
- 12.1.4 For water quality monitoring, one (1) Action Level and one (1) Limit Level exceedance were recorded for Suspended Solids in the reporting period. Investigation was undertaken by ET and it was considered that the exceedances recorded are unlikely caused by the Project.
- 12.1.5 In the Reporting Period, one (1) environmental complaint was received with respect to the marine water concerns arising from the Contract 1 of the Project. Investigation for the complaint by site investigation was undertaken by ET and it was observed that water mitigation measures including silt curtain and cofferdam are properly implemented on site and no sign of muddy discharge was observed. Nevertheless, the Contractor of Contract 1 was reminded to strictly implement all the water mitigation measures as stated in EP and EM&A Manual.
- 12.1.6 No documented complaint, notification of summons or prosecution were received and recorded for the Project.

12.2 RECOMMENDATIONS


- 12.2.1 Due to wet season is approaching, the Contractor was reminded that all the works to undertaking must be fulfill environmental statutory requirement, especially water quality mitigation measures to prevent surface runoff into nearby water bodies or public areas.
- 12.2.2 In regards to the marine works, special attention should be paid on excavation works for the bridge pier foundations underway in which water quality mitigation measures such as erection of silt curtain should be properly implemented and maintained.

Appendix A
Project Layout Plan

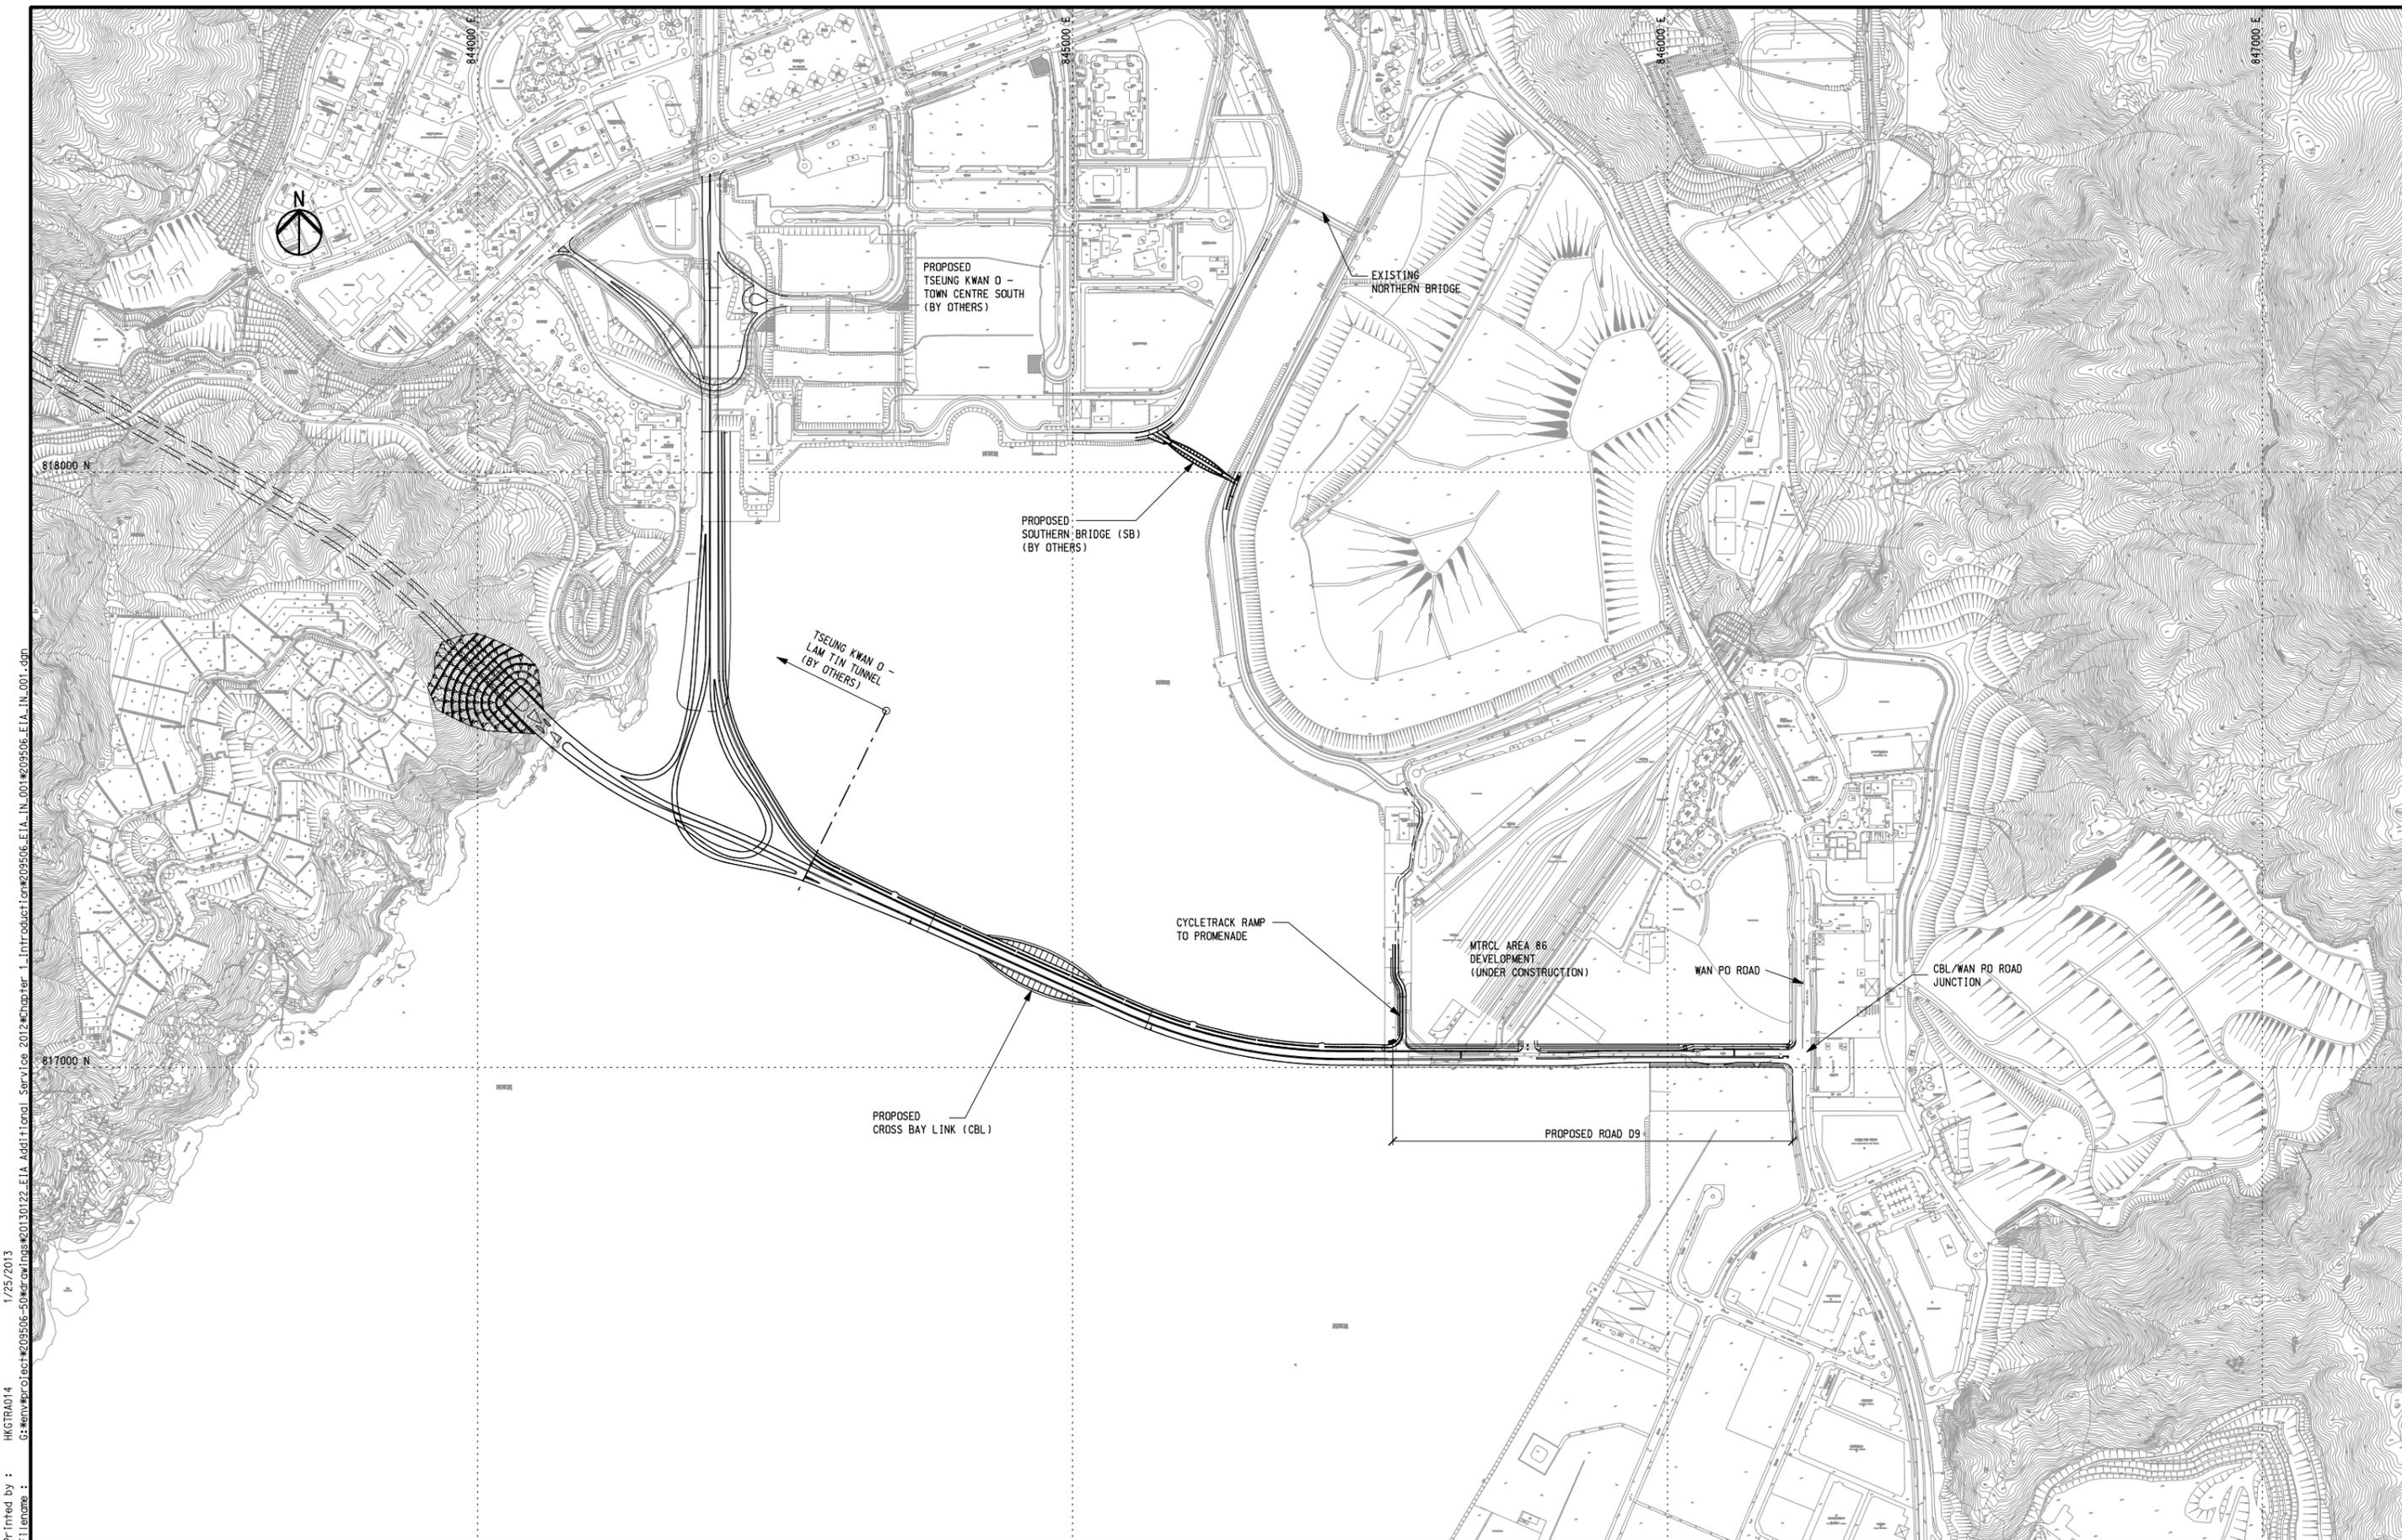

Printed by : HKGTAA014
 File name : G:\env\proj\lect\209506-50\draw\Inis\20130122_EIA_Additional_Serv\ce_2012\chapter_1_Introduction\209506_EIA_IN_001.dgn
 1/25/2013

 土木工程拓展署 Civil Engineering and Development Department	 ARUP Ove Arup & Partners Hong Kong Limited	Job Title Agreement No. CE 43/2008(HY) Cross Bay Link, Tseung Kwan O - Investigation	Drawing Title GENERAL LAYOUT PLAN		Drawn GL	Date 01/13	Drawing No. 209506/EIA/IN/001	
			Checked JP	Approved ST	B SECOND ISSUE 01/13	A FIRST ISSUE 07/11		Status FINAL
			Scale 1:5000 on A1 & 1:10000 on A3	Date				
			Rev. Description					

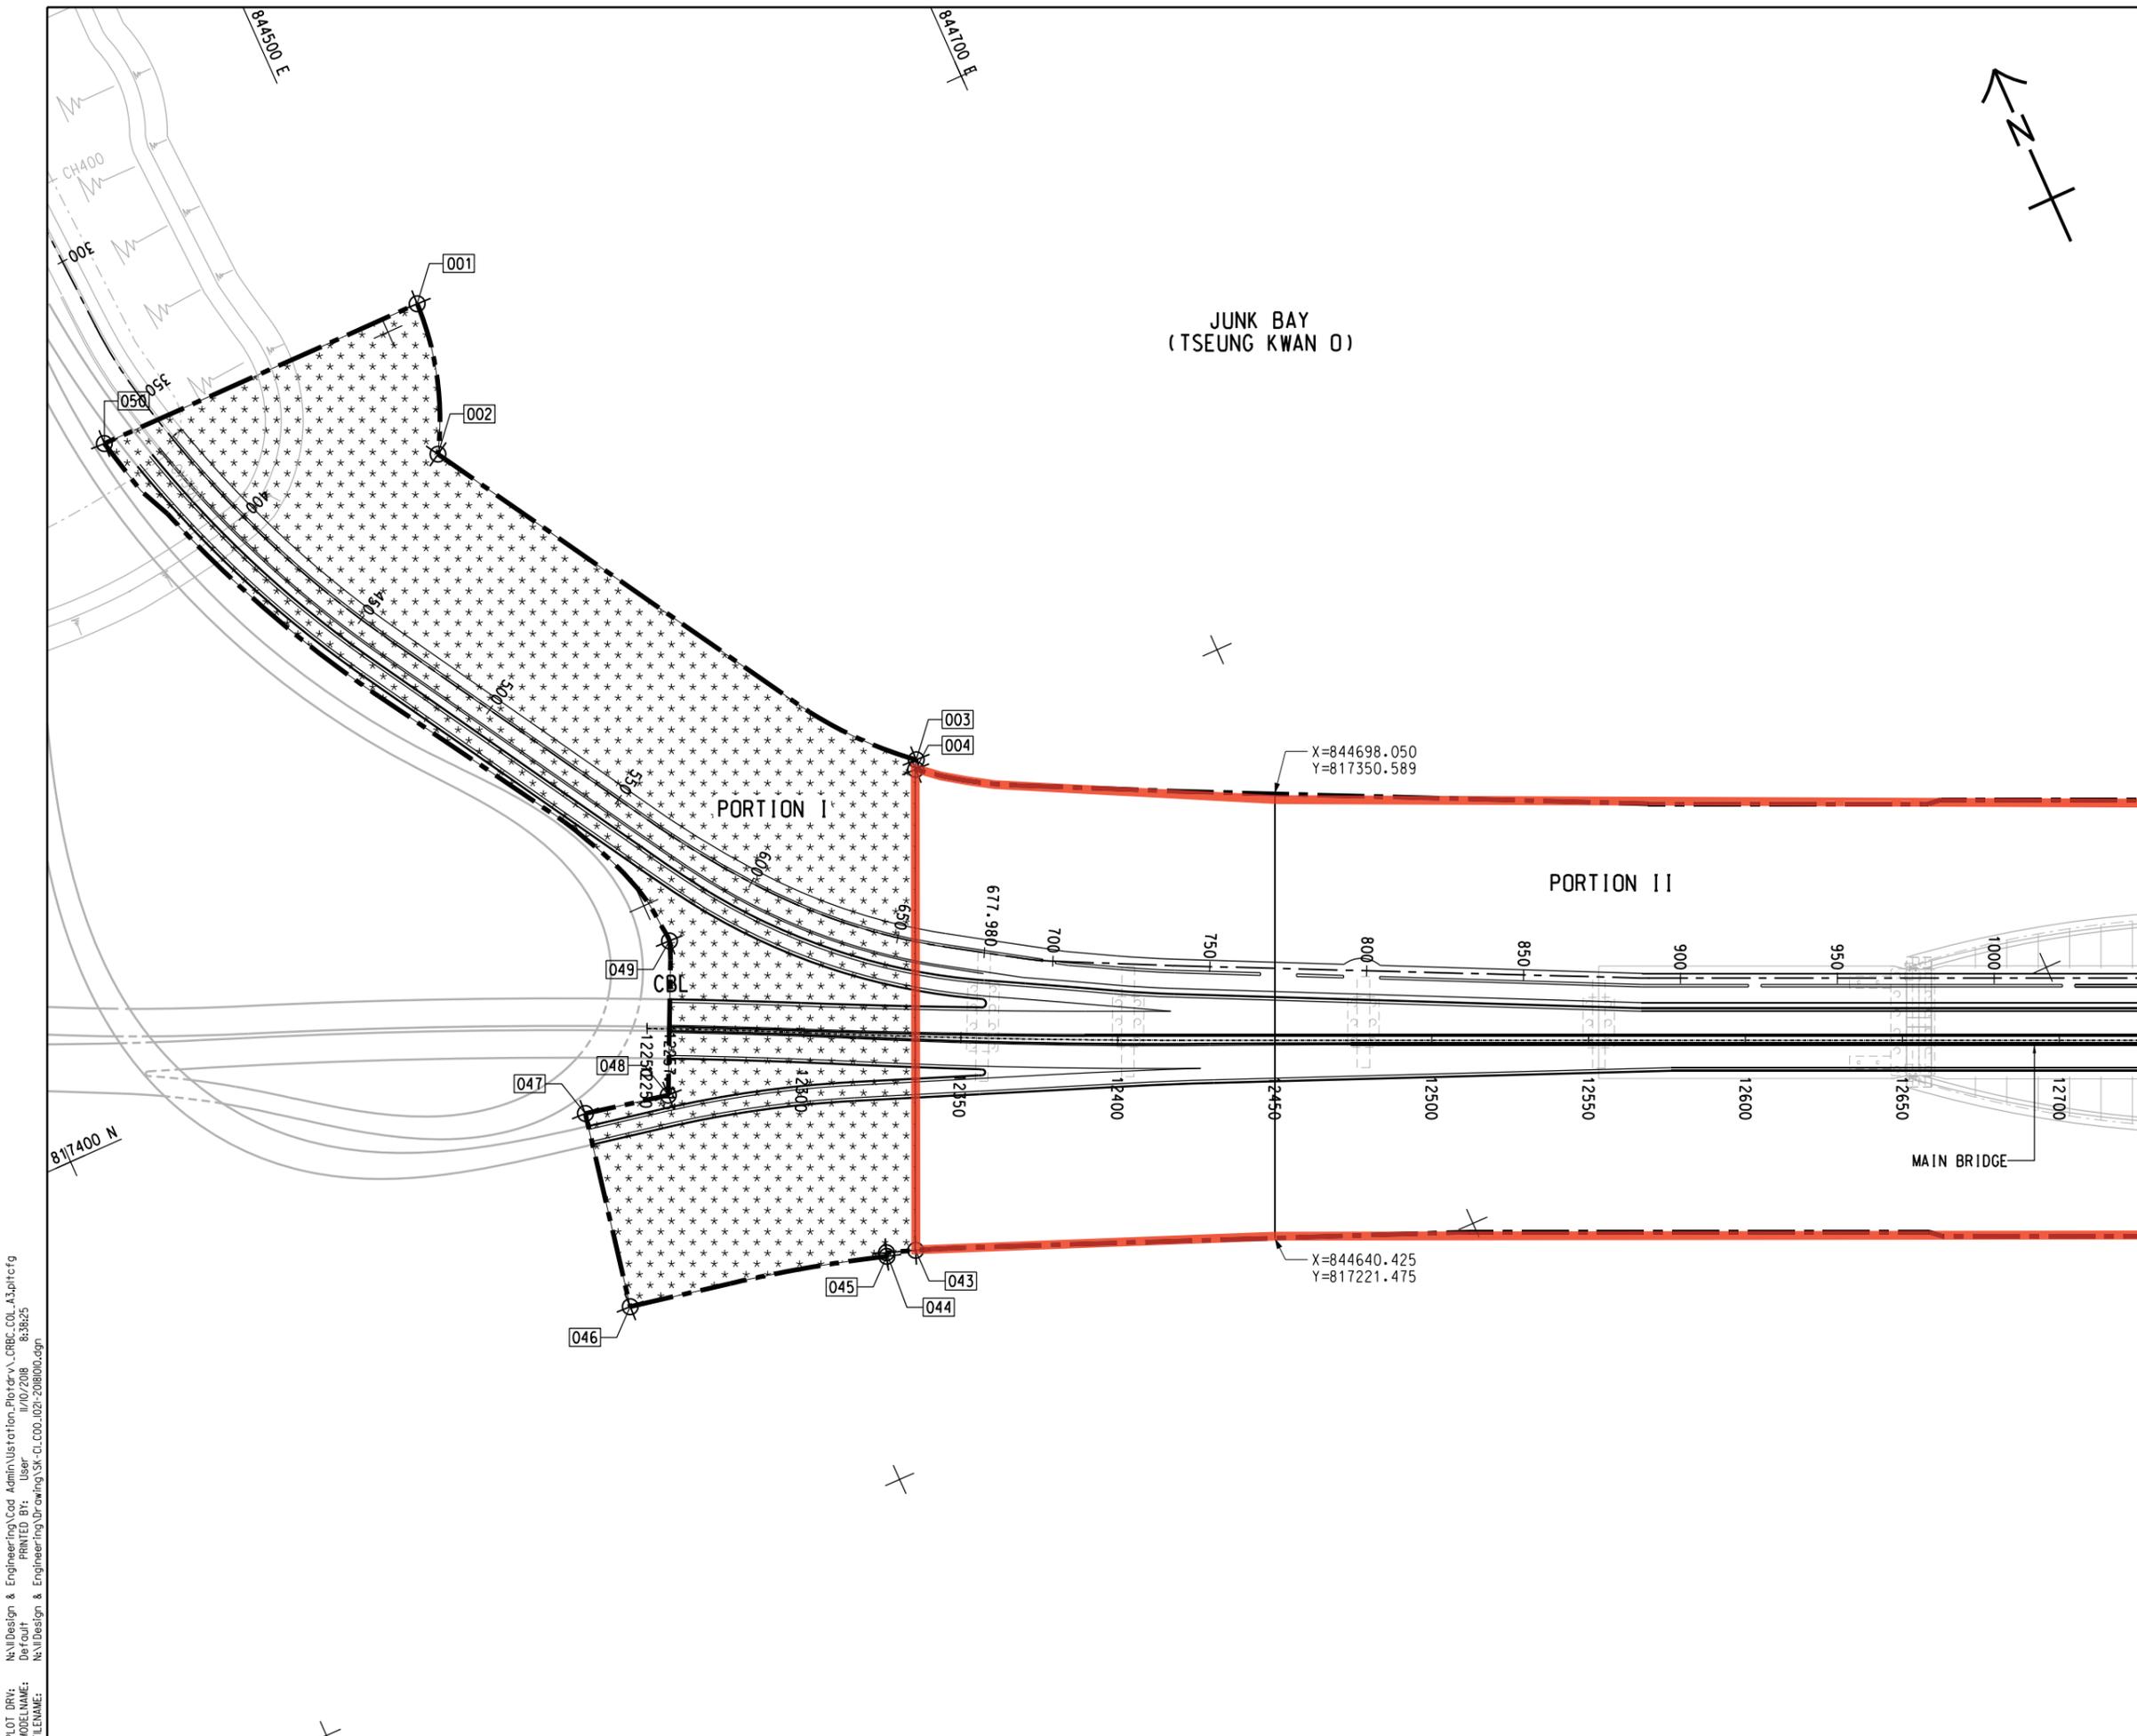

NOTES:

1. ALL SETTING OUT POINTS SHOWN ON THIS SET OF DRAWINGS ARE FOR REFERENCE ONLY. THE EXACT LIMIT OF SITE BOUNDARY SHALL BE VERIFIED AND DETERMINED BY THE CONTRACTOR ON SITE.
2. THIS DRAWING SHALL BE READ IN CONJUNCTION WITH DRAWING NOS. 60329339/C1/COO/1022 AND 1023.

LEGEND:

- SITE BOUNDARY
- PORTION I
- PORTION II
- PORTION III
- PORTION IV
- PORTION V
- PORTION VI
- PORTION VII
- WORKS AREA A
- WORKS AREA B

Works area under Contract 1

A	FIRST ISSUE	HK	KN	AC	19/09/18
Rev	Amendment	By	Chk.	App.	Date

PROJECT MANAGER: PROJECT MANAGER:
 土木工程拓展署
 Civil Engineering and Development Department

SUPERVISOR:

CONTRACTOR:
 中國路橋工程有限責任公司
 China Road and Bridge Corp.

CONTRACT NO. AND TITLE:
 Contract No. NE/2017/07
 CROSS BAY LINK, TSEUNG KWAN O - MAIN BRIDGE AND ASSOCIATED WORKS


DRAWING TITLE:

SCALE @ A1: 1:1000
 DRAWING NO:
 Copyright Reserved
 版權所有 不得翻印

PLOT DRW: N:\I\Design & Engineering\Cad Administration\Pictor-v\CRBC.COL_A3.pltcf9
 MODELNAME: Default PRINTED BY: User 11/10/2018 8:38:25
 FILENAME: N:\I\Design & Engineering\Drawing\SK-C1.C00.021-20181010.dgn

SETTING OUT POINTS		
POINTS	EASTING	NORTHING
001	844512.175	817604.422
002	844498.695	817557.993
003	844598.186	817407.065
004	844596.769	817404.339
005	845132.374	817153.641
006	845500.00	817088.580
007	845524.969	817088.226
008	845524.909	817236.307
009	845558.095	817236.307
010	845558.095	817195.885
011	845550.234	817174.288
012	845550.219	817158.042
013	845562.850	817139.744
014	845562.850	817035.700
015	845550.850	817035.670
016	845524.969	817035.670
017	846030.606	817036.089
018	846030.604	817038.387
019	846200.700	817038.418
020	846200.700	817038.796
021	846205.200	817042.796
022	846205.200	817138.796
023	846245.180	817138.796
024	846246.698	816900.099
025	846206.155	816900.099

SETTING OUT POINTS		
POINTS	EASTING	NORTHING
026	846204.700	816926.589
027	846199.263	816926.590
028	846144.269	816926.589
029	846091.080	816926.744
030	845969.970	816926.504
031	846199.197	816975.364
032	846188.983	816993.582
033	846144.274	816999.997
034	846144.274	817000.722
035	846091.204	817000.679
036	845970.070	817000.581
037	845970.069	817000.099
038	845550.850	817000.099
039	845524.969	817000.099
040	845550.850	816953.291
041	845500.00	816952.636
042	845076.990	817029.022
043	844534.373	817264.536
044	844525.572	817267.627
045	844525.199	817266.527
046	844444.018	817285.203
047	844456.043	817347.194
048	844482.530	817341.743
049	844502.889	817386.445
050	844403.015	817604.422

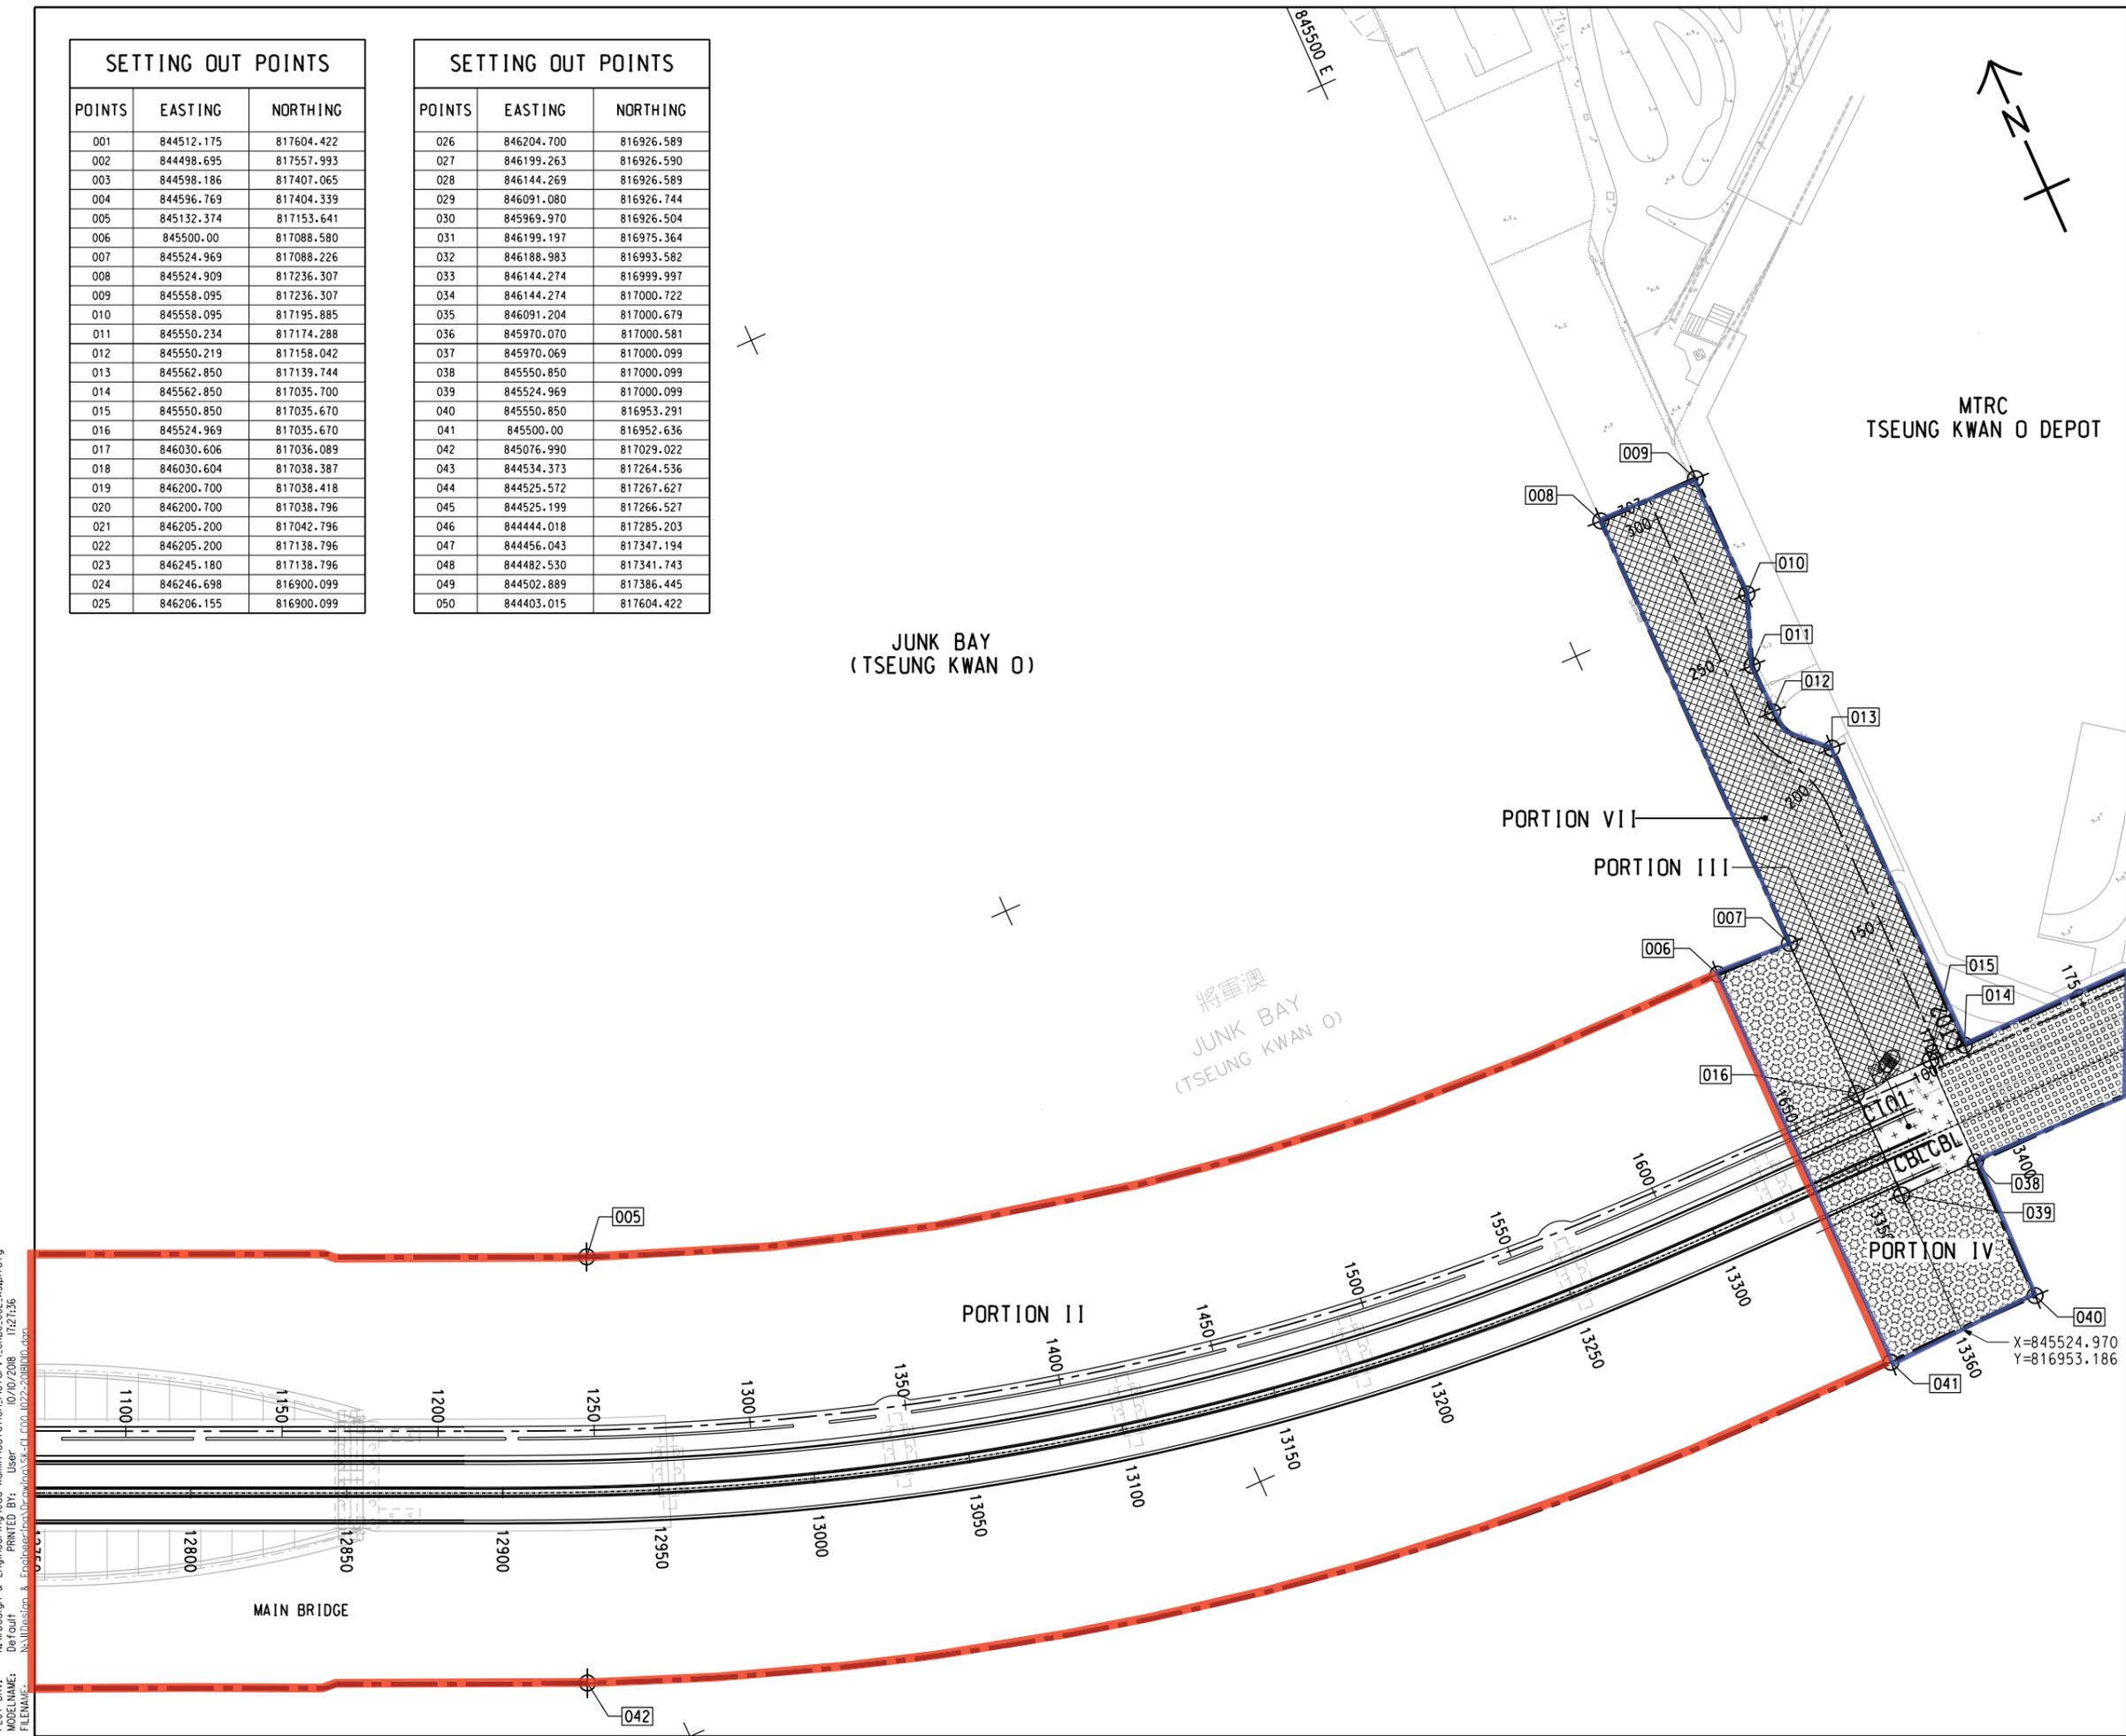


NOTE:
 1. THIS DRAWING SHALL BE READ IN CONJUNCTION WITH DRAWING NOS. 60329339/C1/COO/1021 AND 1023.

LEGEND:
 Works area under Contract 1
 Works area under Contract 2

N:\I\Design & Engineering\Cad Administration\Pictor\A3\CRBC_COL_A3.plt\cfp
 10/10/2018 10:07:20 User
 MODELNAME: C:\Users\user\Documents\172136
 FILENAME: N:\I\Design & Engineering\Cad Administration\SR-C1\000_02252481011.dwg

Rev	Amendment	By	Chk.	App.	Date
PROJECT MANAGER:		PROJECT MANAGER:			
 土木工程拓展署 Civil Engineering and Development Department					
SUPERVISOR:					
CONTRACTOR:		 中國路橋工程有限責任公司 China Road and Bridge Corp.			
CONTRACT NO. AND TITLE: Contract No. NE/2017/07 CROSS BAY LINK, TSEUNG KWAN O - MAIN BRIDGE AND ASSOCIATED WORKS					
DRAWING TITLE:					
SCALE @ A1		DRAWING NO:			
Copyright Reserved 版權所有 不得翻印					

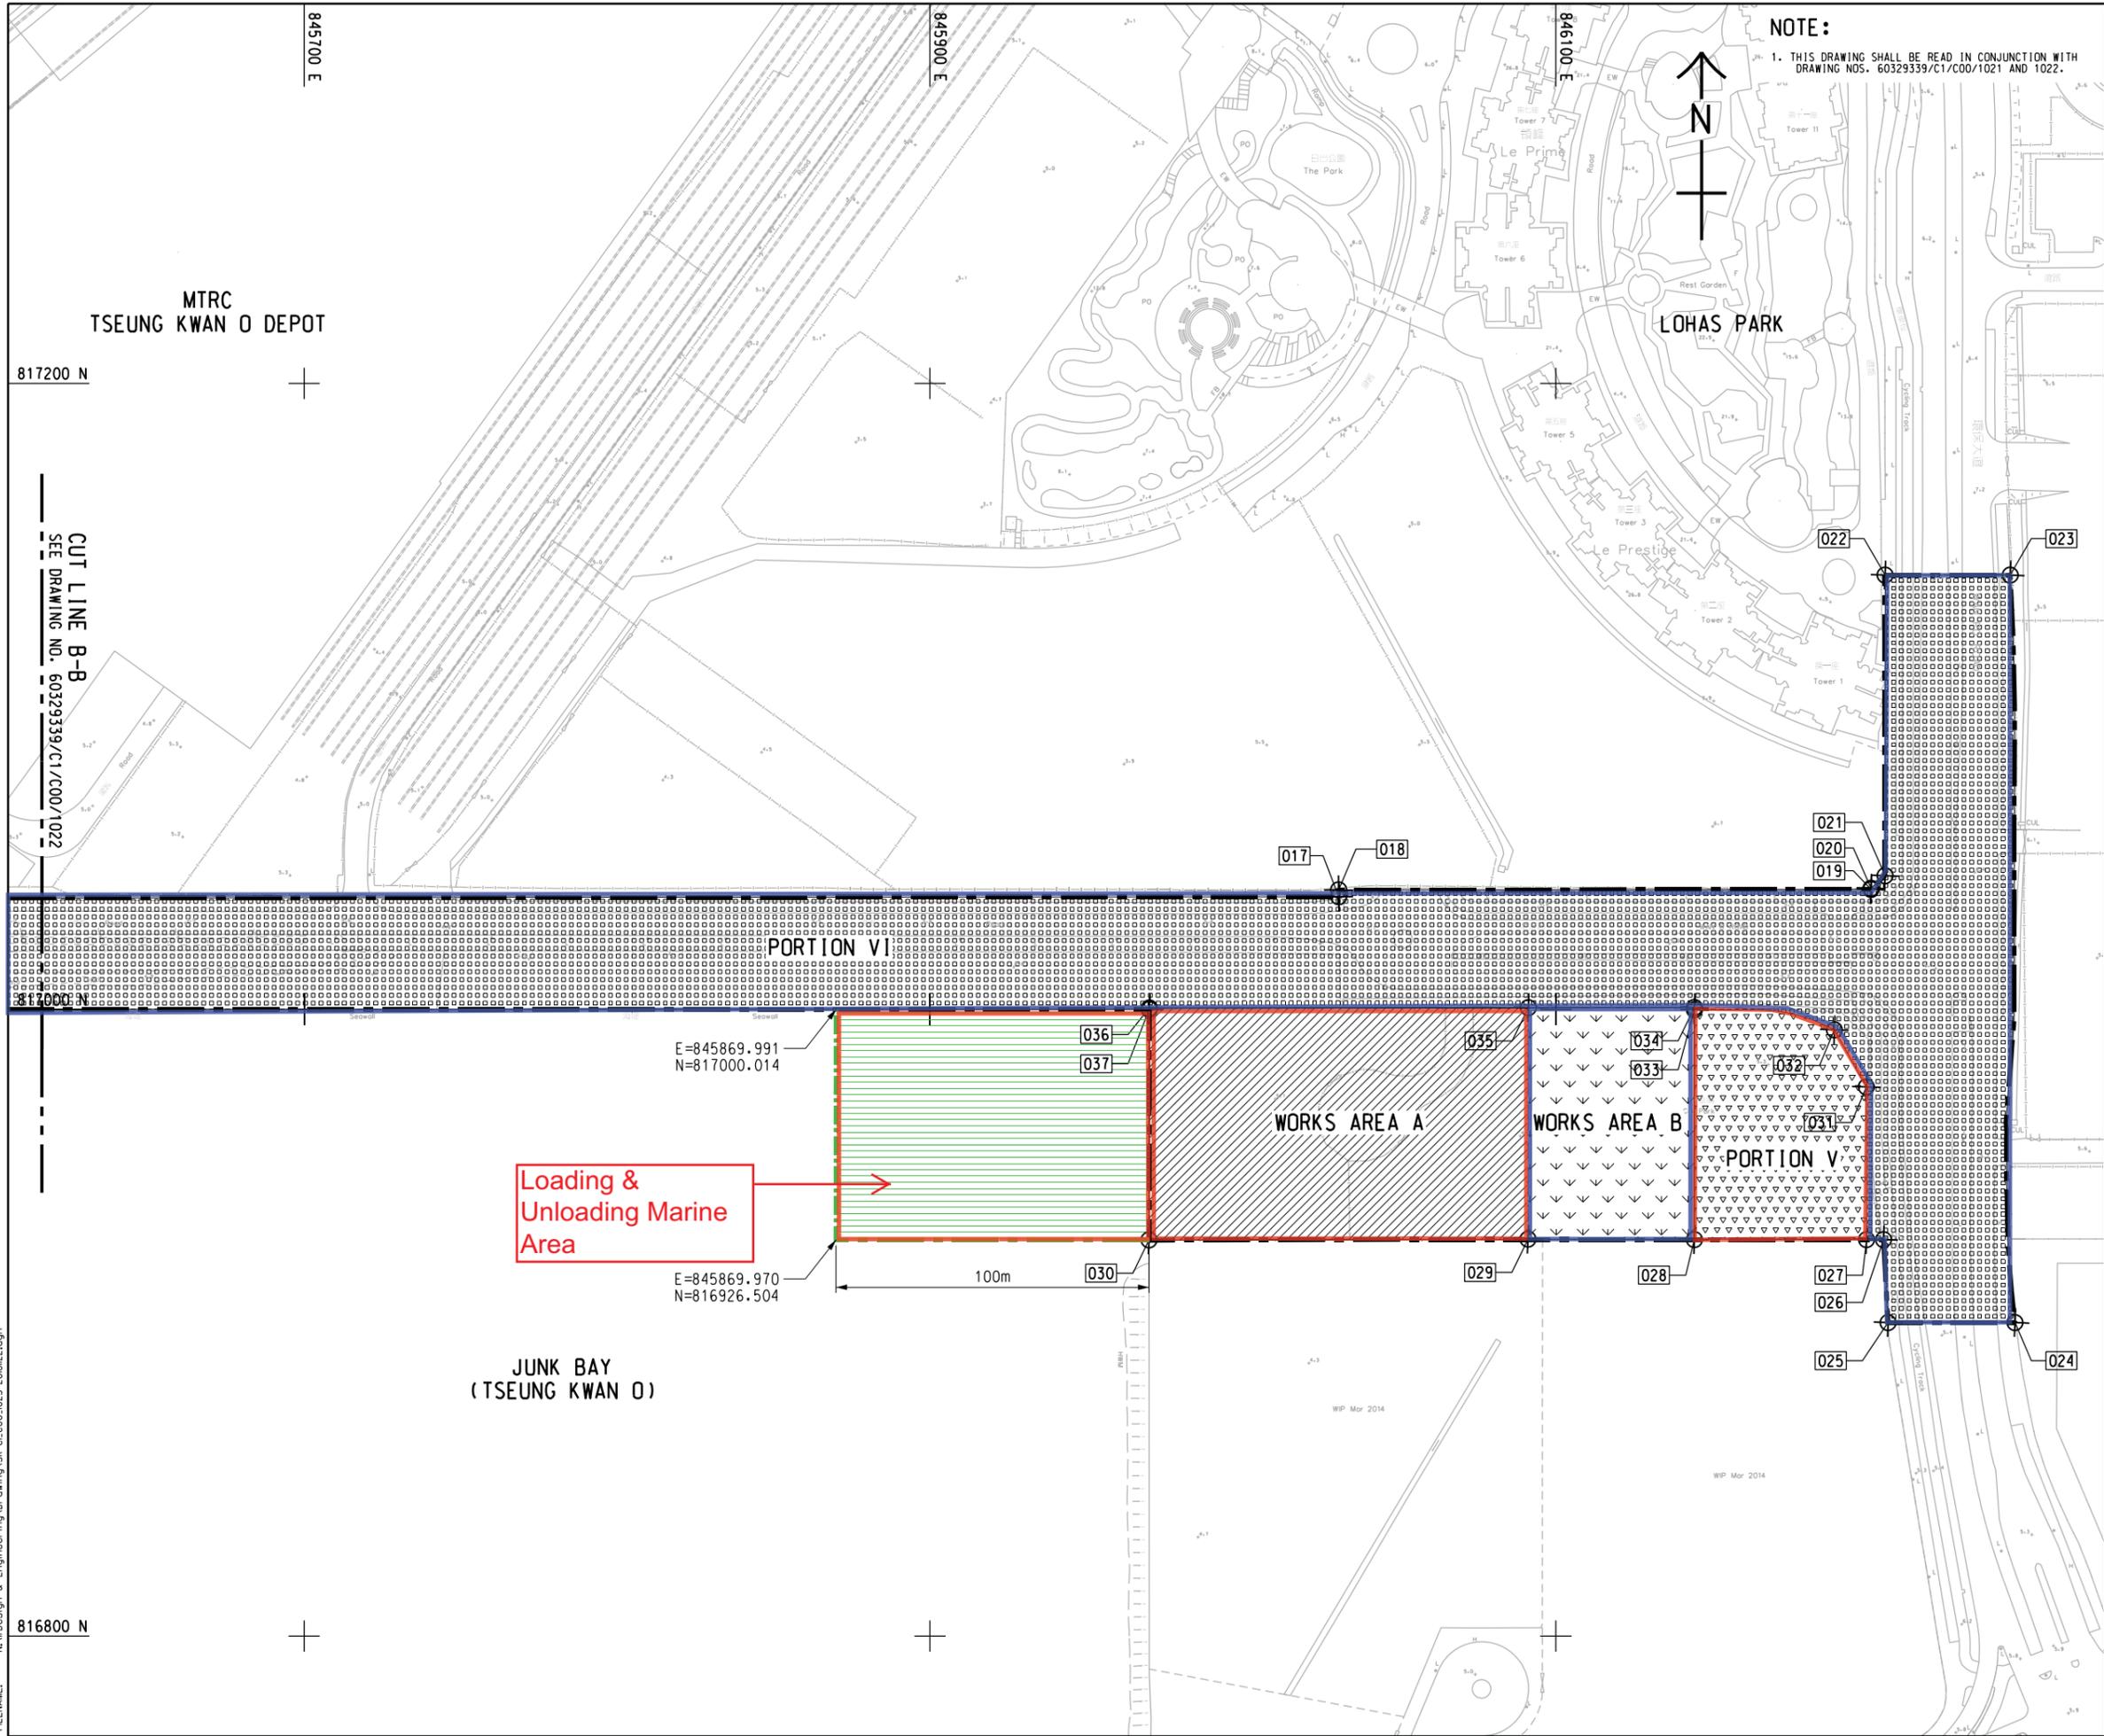

NOTE:
1. THIS DRAWING SHALL BE READ IN CONJUNCTION WITH
DRAWING NOS. 60329339/C1/COO/1021 AND 1022.

- LEGEND:
- Works area under Contract 1
 - Works area under Contract 2

MTRC
TSEUNG KWAN O DEPOT

LOHAS PARK

CUT LINE B-B
SEE DRAWING NO. 60329339/C1/COO/1022

Loading & Unloading Marine Area

WORKS AREA A

WORKS AREA B

PORTION V

JUNK BAY
(TSEUNG KWAN O)


Rev	Amendment	By	Chk.	App.	Date
PROJECT MANAGER: PROJECT MANAGER:					
土木工程拓展署 Civil Engineering and Development Department					
SUPERVISOR: AECOM					
CONTRACTOR: 中國路橋工程有限責任公司 China Road and Bridge Corp.					
CONTRACT NO. AND TITLE: Contract No. NE/2017/07 CROSS BAY LINK, TSEUNG KWAN O - MAIN BRIDGE AND ASSOCIATED WORKS					
DRAWING TITLE:					
SCALE @ A1			DRAWING NO:		
Copyright Reserved 版權所有 不得翻印					

N:\I\Design & Engineering\Cad Administration\Pictor.vv_CRBC_COL_A3.pltcf9
 MODELNAME: Default PRINTED BY: User 22/11/2018 10:00:59
 FILENAME: N:\I\Design & Engineering\Drawing\SK-CI-COO_025_2018122.dgn

Appendix B

Project Organization Chart & Contact Details of Key Personnel for the Project

Project Organization Structure

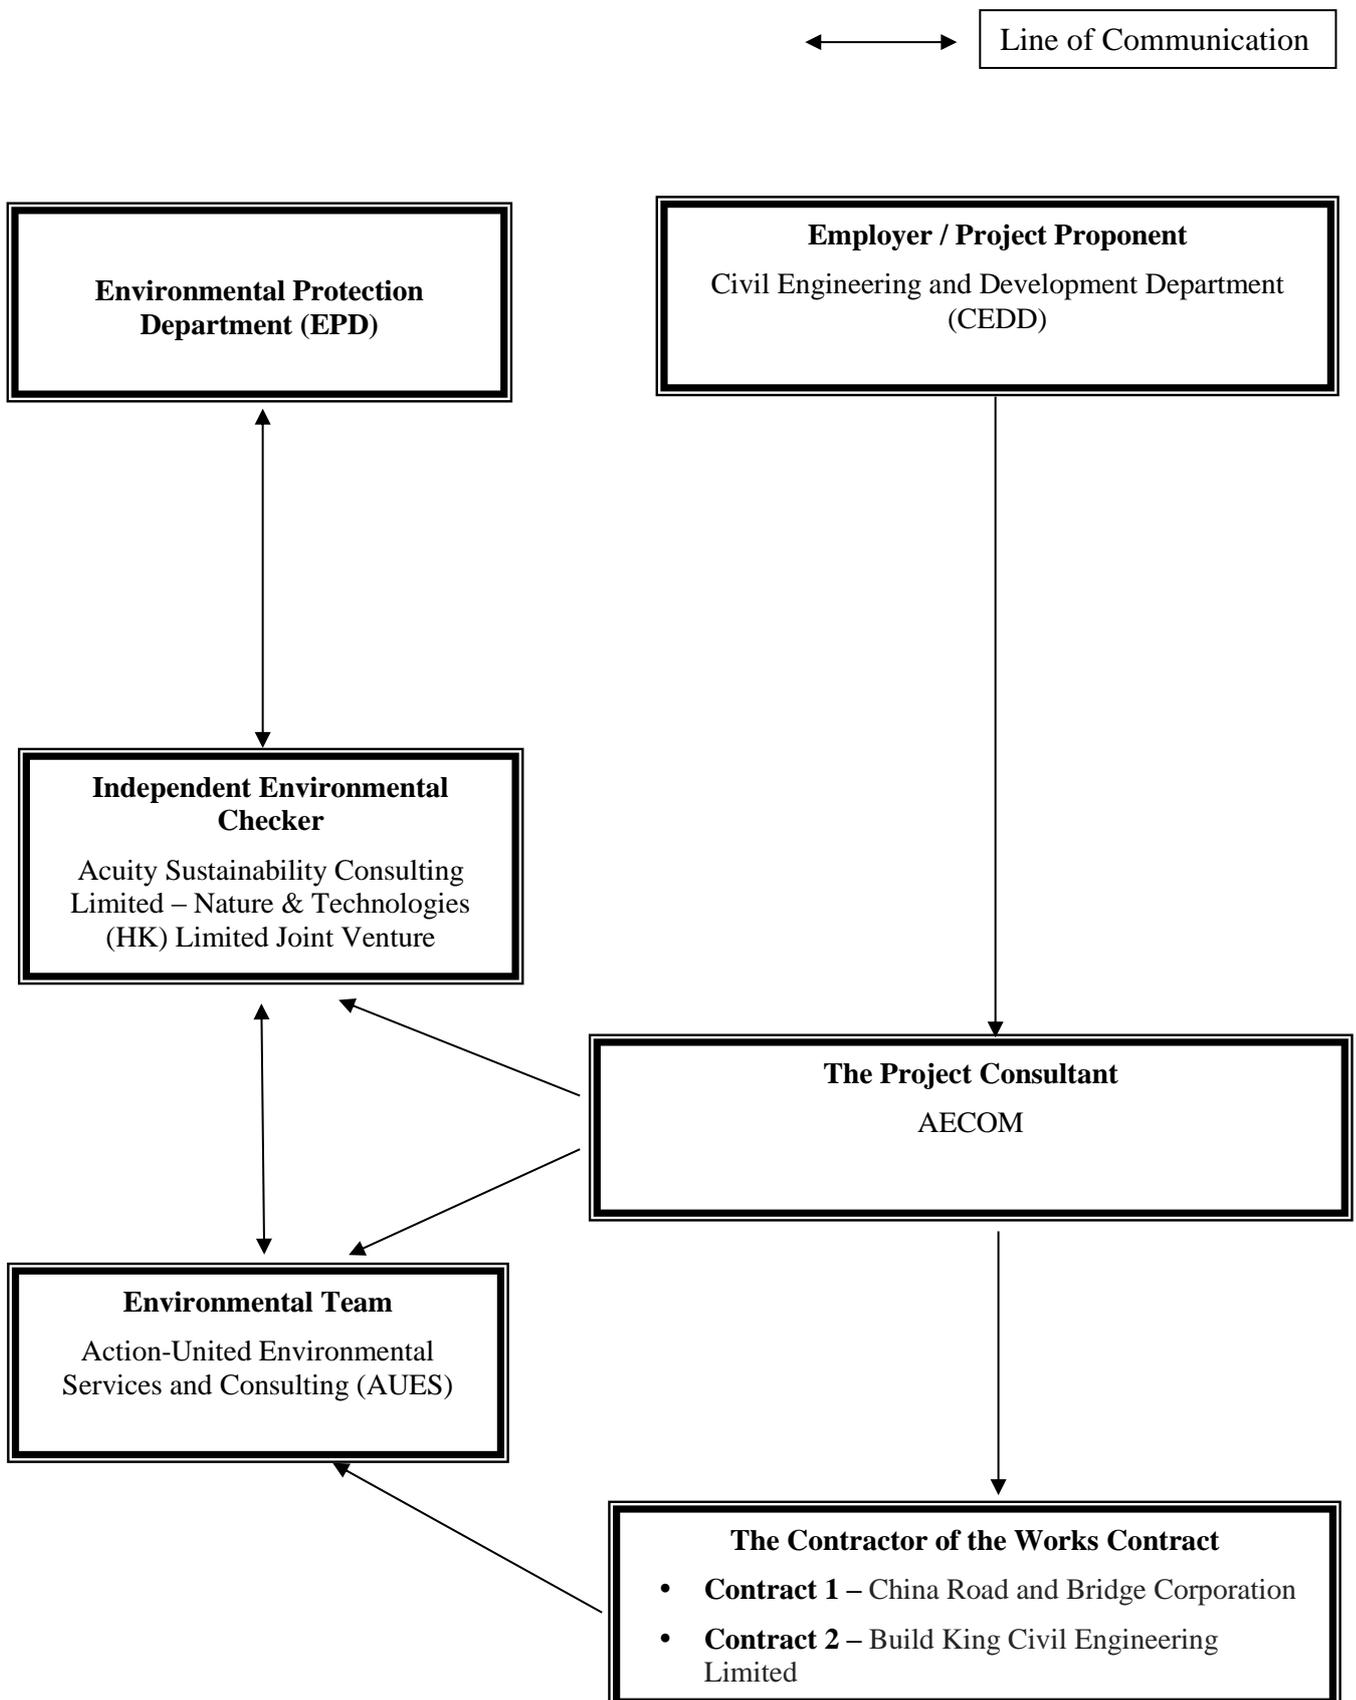

Contact Details of Key Personnel for the Project

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Project Proponent	CK Lam	2301 1398	2714 5174
CEDD	Project Proponent	Simon Wong	2301 1398	2714 5174
AECOM	Senior Resident Engineer	Jackie Chan	3595 8045	3596 6118
AECOM	Resident Engineer	Kingman Chan	3595 8045	3596 6118
ASC – N&T JV	Independent Environmental Checker	Kevin Li	2698 6833	2698 9383
ASC – N&T JV	Principal Environmental Consultant	Pan Fong	2698 6833	2698 9383
ASC – N&T JV	Senior Environmental Consultant	Tandy Tse	2698 6833	2698 9383
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Martin Li	2959 6059	2959 6079
CRBC	Site Agent	Raymond Cheng	6026 5971	2283 1689
CRBC	Environmental Officer	Calvin So	9724 6254	2283 1689
CRBC	Environmental Supervisor	Lila Lui	9790 5433	2283 1689
Build King	Site Agent	Stephen Leung	9071 7657	TBA
Build King	Environmental Officer	Stephen Leung	9071 7657	TBA
Build King	Environmental Supervisor	Walter Wong	6584 7065	TBA

Legend:

CEDD (Employer) – Civil Engineering and Development Department

AECOM (Project Consultant) – AECOM Asia Co. Ltd.

ASC – N&T JV (IEC) – Acuity Sustainability Consulting Limited – Nature & Technologies (HK) Limited Joint Venture

AUES (ET) – Action-United Environmental Services & Consulting

CRBC (the Main Contractor of the Works Contract 1) – China Road and Bridge Corporation

Build King (the Main Contractor of the Works Contract 2) - Build King Civil Engineering Limited

Appendix C

3-Month Rolling Construction Programme

Contract 1

Contract No. NE/2017/07 Cross Bay Link, Tseng Kwan O - Main Bridge and Associated Works

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Planned Start	Finish	Planned Finish	Total Cost	Activity % Complete	TRA	Variance - Finish Date	Gantt Chart (March 2019 - June 2019)											
												24	03	10	17	24	31	07	14	21	28	05	12
P-SP1790	Design, supply and installation of cable hangers system	0	0			07-Apr-19	07-Apr-19	50	0%	0	0	Design, supply and installation of cable hangers system											
Preliminaries												37											
P-P11120	Design & Erection of project manager's site office	75	0	19-Nov-18 A	08-May-19	15-Feb-19 A	06-Aug-19		100%	0	139												
P-P11140	Design & Erection of contractor's site office	85	0	19-Nov-18 A	08-May-19	02-Feb-19 A	17-Aug-19		100%	0	157												
P-P11160	Design & Erection of Community liaison centre (PMI 001)	95	95	08-Mar-19	08-Feb-19	05-Jul-19	05-Jun-19	775	0%	0	-24												
P-P11220	Physical Model for the marine viaducts of Cross Bay Link	5	5	08-Mar-19	08-Feb-19	13-Mar-19	13-Feb-19	1161	0%	0	-24	Physical Model for the marine viaducts of Cross Bay Link											
Precasting & Fabrication Works												16											
P-PS9000	Information of TCSS for Cast-in Items (provide by others)	0	0			08-Mar-19	08-Feb-19	-21	0%	7	-28	Information of TCSS for Cast-in Items (provide by others)											
Fabrication of Precast Shell and Precast Segments												12											
Precast Shell												12											
P-PS1020	Setting up precasting yard for precast shell (incl. 21 days TRA)	90	30	08-Nov-18 A	28-Apr-19	06-Apr-19	26-Jul-19	26	66.67%	21	111												
P-PS3080	Fabrication of Precast shell for pile cap of Marine viaduct and main bridge(1st batch 4 nos)	99	99	07-Apr-19	10-Mar-19	14-Jul-19	26-Jun-19	26	0%	21	-18												
Fabrication of Precast Box Girder												25											
P-BG1375	Setting Up Precasting Yard for Box Girder (incl. 14 days TRA)	120	60	10-Nov-18 A	13-May-19	06-May-19	09-Sep-19	59	50%	14	126												
P-BG1376	Procurement and Delivery of Prestress Tendons & Anchorage (incl. 20 days TRA)	89	61	25-Jan-19 A	08-Feb-19	07-May-19	07-May-19	59	31.46%	21	0	Procurement and Delivery of Prestress Tendons & Anchorage (incl. 20 days TRA)											
Box Girder Fabrication - 1st Batch 7 Pieces												0											
P-BG1380	Fabrication of Precast box girder, Cast-in Items and Prestressing -SE4-5	75	75	08-May-19	08-May-19	21-Jul-19	21-Jul-19	59	0%	21	0												
P-BG1381	Fabrication of Precast box girder, Cast-in Items and Prestressing -NW5-4	75	75	02-Jun-19	02-Jun-19	15-Aug-19	15-Aug-19	59	0%	0	0												
Fabrication of Precast Pier												-43											
P-PF1220	Setting up precasting yard for precast pier (incl. 18 days TRA)	87	87	01-Jun-19	16-Apr-19	26-Aug-19	14-Jul-19	27	0%	21	-43												
Fabrication of Steel Arch Bridge and Side Spans												-12											
Fabrication of Steel Arch Bridge												-12											
P-PF1035	1st batch of shop drawing submission & approval	50	50	16-Mar-19	04-Mar-19	13-May-19	30-Apr-19	-69	0%	0	-11	1st batch of shop drawing submission & approval											
P-PF1040	Setting up steel work fabrication yard	60	60	26-Apr-19	14-Apr-19	24-Jun-19	12-Jun-19	-93	0%	0	-12	Setting up steel work fabrication yard											
P-PF1045	Remaining shop drawing submission & approval	120	120	16-Mar-19	04-Mar-19	02-Aug-19	20-Jul-19	11	0%	0	-11												
P-PF1050	Procurement and delivery of steel material (incl. 35 days TRA)	125	125	26-May-19	14-May-19	27-Sep-19	15-Sep-19	-93	0%	35	-12												
Section 1 of the Works- All Works within Portion I of the Site (Entrusted Works of TKOI Viaduct)												557											
Pre-drilling Works												557											
Pre-drilling Works for Pier 5B (Bridge S400, 33.13m length, 5m socket)												531											
S1-PD0010	Installation of Temporary Sleeve Casings at Pier 5B	7	7	29-Mar-19	06-Apr-19	06-Apr-19	06-Apr-19	531	0%			Installation of Temporary Sleeve Casings at Pier 5B											
Pre-drilling Works for Pier 9B (Bridge CT, 32.63m length, 4.5m socket)												557											
S1-PD1054	Installation of Temporary Sleeve Casings at Pier 5B	7	7	29-Mar-19	06-Apr-19	06-Apr-19	06-Apr-19	557	0%			Installation of Temporary Sleeve Casings at Pier 5B											
Section 2 of Works-All Works within Portion II,III,IV and VI												1331											
CBL Main Bridge and Marine Viaduct												1331											
Pre-drilling Works												1088											
Pre-drilling Works for Pier W2 (55m length, 4m socket)												80											
S2-PD200	Deploy silt curtain	7	0	01-Dec-18 A	06-Mar-19	12-Dec-18 A	22-Mar-19		100%	0	81	Deploy silt curtain											
S2-PD230	Pre-drilling Works for W2- P4 (55m length, 4m socket) - rig No.1	4	0	08-Dec-18 A	09-Mar-19	12-Dec-18 A	13-Mar-19		100%	0	72	Pre-drilling Works for W2- P4 (55m length, 4m socket) - rig No.1											
S2-PD230	Pre-drilling Works for W2- P5 (55m length, 4m socket) - rig No.1	4	0	04-Dec-18 A	14-Mar-19	07-Dec-18 A	18-Mar-19		100%	0	80	Pre-drilling Works for W2- P5 (55m length, 4m socket) - rig No.1											
S2-PD230	Pre-drilling Works for W2- P6 (55m length, 4m socket) - rig No.1	4	0	08-Dec-18 A	19-Mar-19	12-Dec-18 A	22-Mar-19		100%	0	80	Pre-drilling Works for W2- P6 (55m length, 4m socket) - rig No.1											
Pre-drilling Works for Pier E1 (54-55m length, 4m socket)												117											
S2-PD220	Mobilization of Jack up barge/ working platform	2	0	09-Oct-18 A	21-May-19	10-Oct-18 A	22-May-19		100%	0	179	Mobilization of Jack up barge/ working platform											
S2-PD220	Deploy silt curtain	2	0	11-Oct-18 A	23-May-19	12-Oct-18 A	24-May-19		100%	0	179	Deploy silt curtain											
S2-PD220	Pre-drilling Works for E1- P1 (54-55m length, 4m socket) - rig No.2 (NCE 006)	4	0	15-Oct-18 A	08-Mar-19	31-Oct-18 A	12-Mar-19		100%	0	107	Pre-drilling Works for E1- P1 (54-55m length, 4m socket) - rig No.2 (NCE 006)											
S2-PD360	Pre-drilling Works for E1- P2 (54-55m length, 4m socket) - rig No.2	4	0	13-Oct-18 A	13-Mar-19	03-Nov-18 A	16-Mar-19		100%	0	108	Pre-drilling Works for E1- P2 (54-55m length, 4m socket) - rig No.2											
S2-PD360	Pre-drilling Works for E1- P3 (54-55m length, 4m socket) - rig No.2	4	0	12-Nov-18 A	16-May-19	17-Nov-18 A	20-May-19		100%	0	145	Pre-drilling Works for E1- P3 (54-55m length, 4m socket) - rig No.2											
S2-PD360	Pre-drilling Works for E1- P4 (54-55m length, 4m socket) - rig No.2	4	0	23-Nov-18 A	10-Jun-19	28-Nov-18 A	13-Jun-19		100%	0	156	Pre-drilling Works for E1- P4 (54-55m length, 4m socket) - rig No.2											
S2-PD370	Pre-drilling Works for E1- P7 (54-55m length, 4m socket) - rig No.2	4	0	27-Nov-18 A	16-May-19	05-Dec-18 A	20-May-19		100%	0	130	Pre-drilling Works for E1- P7 (54-55m length, 4m socket) - rig No.2											
S2-PD370	Pre-drilling Works for E1- P8 (54-55m length, 4m socket) - rig No.2	4	0	19-Nov-18 A	21-May-19	24-Nov-18 A	24-May-19		100%	0	143	Pre-drilling Works for E1- P8 (54-55m length, 4m socket) - rig No.2											
S2-PD370	Pre-drilling Works for E1- P9 (54-55m length, 4m socket) - rig No.2	4	0	21-Nov-18 A	30-May-19	26-Nov-18 A	03-Jun-19		100%	0	150	Pre-drilling Works for E1- P9 (54-55m length, 4m socket) - rig No.2											
S2-PD370	Pre-drilling Works for E1- P10 (54-55m length, 4m socket) - rig No.2	4	0	15-Nov-18 A	04-Jun-19	20-Nov-18 A	08-Jun-19		100%	0	159	Pre-drilling Works for E1- P10 (54-55m length, 4m socket) - rig No.2											
S2-PD370	Pre-drilling Works for E1- P11 (54-55m length, 4m socket) - rig No.2	4	0	10-Nov-18 A	10-Jun-19	14-Nov-18 A	13-Jun-19		100%	0	168	Pre-drilling Works for E1- P11 (54-55m length, 4m socket) - rig No.2											
S2-PD380	Pre-drilling Works for E1- P12 (54-55m length, 4m socket) - rig No.2	4	0	27-Nov-18 A	30-May-19	03-Dec-18 A	03-Jun-19		100%	0	144	Pre-drilling Works for E1- P12 (54-55m length, 4m socket) - rig No.2											
S2-PD380	Pre-drilling Works for E1- P13 (54-55m length, 4m socket) - rig No.2	4	0	28-Dec-18 A	18-Mar-19	02-Jan-19 A	21-Mar-19		100%	0	64	Pre-drilling Works for E1- P13 (54-55m length, 4m socket) - rig No.2											
S2-PD380	Pre-drilling Works for E1- P14 (54-55m length, 4m socket) - rig No.2	4	0	03-Jan-19 A	22-Mar-19	07-Jan-19 A	26-Mar-19		100%	0	64	Pre-drilling Works for E1- P14 (54-55m length, 4m socket) - rig No.2											
S2-PD380	Pre-drilling Works for E1- P15 (54-55m length, 4m socket) - rig No.2	4	0	14-Dec-18 A	10-Jun-19	27-Dec-18 A	13-Jun-19		100%	0	133	Pre-drilling Works for E1- P15 (54-55m length, 4m socket) - rig No.2											
S2-PD380	Pre-drilling Works for E1- P16 (54-55m length, 4m socket) - rig No.2	4	0	28-Dec-18 A	10-Jun-19	16-Jan-19 A	13-Jun-19		100%	0	117	Pre-drilling Works for E1- P16 (54-55m length, 4m socket) - rig No.2											
Pre-drilling Works for Pier E2 (51m length, 4m socket)												4											
S2-PD220	Mobilization of Jack up barge/ working platform	28	12	18-Dec-18 A	04-Mar-19	30-Mar-19	04-Apr-19	350	0%		4	Mobilization of Jack up barge/ working platform											
S2-PD220	Deploy silt curtain	2	0	18-Dec-18 A	04-Mar-19	19-Dec-18 A	05-Mar-19		100%	0	59	Deploy silt curtain											
S2-PD390	Pre-drilling Works for E2- P2 (51m length, 4m socket) - rig No.2	4	0	20-Dec-18 A	06-Mar-19	21-Dec-18 A	07-Mar-19		100%	0	59	Pre-drilling Works for E2- P2 (51m length, 4m socket) - rig No.2											
S2-PD390	Pre-drilling Works for E2- P3 (51m length, 4m socket) - rig No.2	4	0	22-Jan-19 A	01-Apr-19	05-Mar-19 A	04-Apr-19		100%	0	26	Pre-drilling Works for E2- P3 (51m length, 4m socket) - rig No.2											
S2-PD390	Pre-drilling Works for E2- P4 (51m length, 4m socket) - rig No.2 (PMI 005)	4	0	05-Jan-19 A	27-Mar-19	10-Jan-19 A	30-Mar-19	350	0%		-4	Pre-drilling Works for E2- P4 (51m length, 4m socket) - rig No.2 (PMI 005)											
S2-PD390	Pre-drilling Works for E2- P5 (51m length, 4m socket) - rig No.2	4	0	22-Mar-19	18-Mar-19	26-Mar-19	21-Mar-19	350	0%		-4	Pre-drilling Works for E2- P5 (51m length, 4m socket) - rig No.2											
S2-PD390	Pre-drilling Works for E2- P6 (51m length, 4m socket) - rig No.2	4	0	27-Mar-19	22-Mar-19	30-Mar-19	26-Mar-19	350	0%		-4	Pre-drilling Works for E2- P6 (51m length, 4m socket) - rig No.2											
Pre-drilling Works for Pier E3 (52m length, 4m socket)												71											
S2-PD400	Pre-drilling Works for E3- P3 (52m length, 4m socket) - rig No.2 - Relocated	4	0	09-Jan-19 A	27-Mar-19	14-Jan-19 A	30-Mar-19		100%	0	62	Pre-drilling Works for E3- P3 (52m length, 4m socket) - rig No.2 - Relocated											
S2-PD400	Pre-drilling Works for E3- P4 (52m length, 4m socket) - rig No.2	4	0	01-Feb-19 A	29-Apr-19	13-Feb-19 A	03-May-19		100%	0	63	Pre-drilling Works for E3- P4 (52m length, 4m socket) - rig No.2											
S2-PD400	Pre-drilling Works for E3- P5 (52m length, 4m socket) - rig No.2	4	0	26-Jan-19 A	04-May-19	31-Jan-19 A	08-May-19		100%	0	75	Pre-drilling Works for E3- P5 (52m length, 4m socket) - rig No.2											
S2-PD400	Pre-drilling Works for E3- P6 (52m length, 4m socket) - rig No.2	4	0	16-Jan-19 A	09-May-19	23-Jan-19 A	14-May-19		100%	0	86	Pre-drilling Works for E3- P6 (52m length, 4m socket) - rig No.2											
Pre-drilling Works for Pier W3 (57m length, 4m socket)												226											
S2-PD200	Mobilization of Jack up barge/ working platform	2	0	15-Dec-18 A	13-Mar-19	17-Dec-18 A	14-Mar-19		100%	0	69	Mobilization of Jack up barge/ working platform											
S2-PD200	Deploy silt curtain	2	0	18-Dec-18 A	15-Mar-19	19-Dec-18 A	16-Mar-19		100%	0	69	Deploy silt curtain											
S2-PD230	Pre-drilling Works for W3- P2 (57m length, 4m socket) - rig No.1	4	0	14-Feb-19 A	11-Apr-19	21-Feb-19 A	15-Apr-19		100%	0	44	Pre-drilling Works for W3- P2 (57m length, 4m socket) - rig No.1											
S2-PD240	Pre-drilling Works for W3- P3 (57m length, 4m socket) - rig No.1	4	0	03-Apr-19	16-Apr-19	08-Apr-19	23-Apr-19	226	0%		10	Pre-drilling Works for W3- P3 (57m length, 4m socket) - rig No.1											
S2-PD240	Pre-drilling Works for W3- P5 (57m length, 4m socket) - rig No.1	4	0	09-Apr-19	29-Apr-19	12-Apr-19	03-May-19	226	0%		14	Pre-drilling Works for W3- P5 (57m length, 4m socket) - rig No.1											
S2-PD240	Pre-drilling Works for W3- P6 (57m length, 4m socket) - rig No.1	4	0	13-Apr-19	29-Apr-19	17-Apr-19	03-May-19	226	0%		10	Pre-drilling Works for W3- P6 (57m length, 4m socket) - rig No.1											
Pre-drilling Works for Pier W1 (56-57m length, 4m socket)												1144											
S2-PD200	Pre-drilling Works for W1- P1 (56-57m length, 4m socket) - rig No.1	4	0	27-Feb-19 A	08-Feb-19	07-Mar-19 A	12-Feb-19		100%	0	-20	Pre-drilling Works for W1- P1 (56-57m length, 4m socket) - rig No.1											
S2-PD250	Pre-drilling Works for W1- P2 (56-57m length, 4m socket) - rig No.1	4	0	08-Mar-19 A	13-Feb-19	12-Mar-19	16-Feb-19	1153	0%		-20	Pre-drilling Works for W1- P2 (56-57m length, 4m socket) - rig No.1											
S2-PD250	Pre-drilling Works for W1- P3 (56-57m length, 4m socket) - rig No.1	4	0	01-Mar-19 A	18-Feb-19	07-Mar-19 A	21-Feb-19		100%	0	-12	Pre-drilling Works for W1- P3 (56-57m length, 4m socket) - rig No.1											
S2-PD250	Pre-drilling Works for W1- P4 (56-57m length, 4m socket) - rig No.1	4	0	08-Mar-19 A	22-Feb-19	16-Mar-19	26-Feb-19	1153	0%		-16	Pre-drilling Works for W1- P4 (56-57m length, 4m socket) - rig No.1											

█ Remaining Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ◆ Baseline Milestone
 — Primary Baseline
 — Summary
 — Actual Work
 ◆ Baseline Milestone

CRBC
Three Month Rolling Programme

Date	Revision	Checked	Approved
08-Mar-19	Monthly updated on 8 Mar 2019		

Contract No. NE/2017/07 Cross Bay Link, Tseng Kwan O - Main Bridge and Associated Works

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Planned Start	Finish	Planned Finish	Total Pile	Activity % Complete	TRA	Variance - Finish Date	Gantt Chart (March 2019 to June 2019)											
												24	03	10	17	24	31	07	14	21	28	05	12
Piling Works for Pier E4												Piling Works for Pier E4											
S2-PW12	Piling platform installation -E4	4	0	19-Dec-18 A	03-Jun-19	20-Dec-18 A	06-Jun-19	406	100%	0	77	Piling platform installation -E4											
Pile E4 -P1	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P1	5	0	21-Dec-18 A	08-Jun-19	07-Jan-19 A	13-Jun-19		100%	0	126	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P1											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P1	5	0	21-Dec-18 A	08-Jun-19	07-Jan-19 A	13-Jun-19		100%	0	126	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P1											
S2-PW1	Install steel cage and concreting -E4-P1	3	0	12-Feb-19 A	18-Feb-19	15-Feb-19 A	12-Jun-19		100%	0	94	Install steel cage and concreting -E4-P1											
Pile E4 -P6	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P6	8	0	21-Dec-18 A	03-Jun-19	07-Jan-19 A	12-Jun-19		100%	0	125	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P6											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P6	3	0	12-Feb-19 A	18-Feb-19	15-Feb-19 A	20-Feb-19		100%	0	5	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P6											
S2-PW1	Install steel cage and concreting -E4-P6	3	0	12-Feb-19 A	18-Feb-19	15-Feb-19 A	20-Feb-19		100%	0	5	Install steel cage and concreting -E4-P6											
Pile E4 -P3	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P3	8	0	21-Dec-18 A	03-Jun-19	07-Jan-19 A	12-Jun-19		100%	0	125	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P3											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P3	4	0	08-Feb-19 A	18-Feb-19	23-Feb-19 A	21-Jun-19		100%	0	1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P3											
S2-PW1	Install steel cage and concreting -E4-P3	3	0	25-Feb-19 A	22-Feb-19	26-Feb-19 A	25-Feb-19		100%	0	0	Install steel cage and concreting -E4-P3											
Pile E4 -P4	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P4	8	0	21-Dec-18 A	13-Jun-19	07-Jan-19 A	21-Jun-19		100%	0	133	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P4											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P4	4	0	08-Feb-19 A	22-Feb-19	18-Feb-19 A	26-Feb-19		100%	0	8	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P4											
S2-PW1	Install steel cage and concreting -E4-P4	3	0	19-Feb-19 A	27-Feb-19	21-Feb-19 A	01-Mar-19		100%	0	8	Install steel cage and concreting -E4-P4											
Pile E4 -P5	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P5	7	0	20-Feb-19 A	27-Feb-19	04-Mar-19 A	06-Mar-19		100%	0	3	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P5											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P5	4	0	20-Feb-19 A	27-Feb-19	02-Mar-19 A	02-Mar-19		100%	0	1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P5											
S2-PW1	Install steel cage and concreting -E4-P5	3	0	04-Mar-19 A	04-Mar-19	04-Mar-19 A	06-Mar-19		100%	0	3	Install steel cage and concreting -E4-P5											
Pile E4 -P2	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P2	7	0	15-Feb-19 A	07-Mar-19	08-Mar-19 A	14-Mar-19		100%	0	6	Drive Casing & Grab to excavate the soil (40.4m length) -E4-P2											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P2	4	0	15-Feb-19 A	07-Mar-19	06-Mar-19 A	11-Mar-19		100%	0	5	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E4-P2											
S2-PW1	Install steel cage and concreting -E4-P2	3	0	07-Mar-19 A	12-Mar-19	08-Mar-19 A	14-Mar-19		100%	0	6	Install steel cage and concreting -E4-P2											
Testing	Sonic Test, interface core and full core for bored pile -E4	21	21	13-Mar-19	15-Mar-19	05-Apr-19	08-Apr-19	348	0%	0	2	Sonic Test, interface core and full core for bored pile -E4											
S2-PW1	Sonic Test, interface core and full core for bored pile -E4	21	21	13-Mar-19	15-Mar-19	05-Apr-19	08-Apr-19	348	0%	0	2	Sonic Test, interface core and full core for bored pile -E4											
Piling Works for Pier E5												Piling Works for Pier E5											
S2-PW62	Piling platform installation -E5	4	4	13-Apr-19	29-Apr-19	17-Apr-19	03-May-19	34	0%	0	10	Piling platform installation -E5											
Pile E5 -P1	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P1	12	12	18-Apr-19	04-May-19	06-May-19	18-May-19	54	0%	0	10	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P1											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P1	5	5	18-Apr-19	04-May-19	26-Apr-19	09-May-19	34	0%	0	10	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P1											
S2-PW1	Install steel cage and concreting -E5-P1	4	4	27-Apr-19	10-May-19	02-May-19	15-May-19	50	0%	0	10	Install steel cage and concreting -E5-P1											
Pile E5 -P2	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P2	15	15	27-Apr-19	10-May-19	16-May-19	28-May-19	49	0%	0	10	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P2											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P2	8	8	27-Apr-19	10-May-19	07-May-19	20-May-19	34	0%	0	10	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P2											
S2-PW1	Install steel cage and concreting -E5-P2	4	4	08-May-19	21-May-19	11-May-19	24-May-19	46	0%	0	10	Install steel cage and concreting -E5-P2											
Pile E5 -P3	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P3	15	15	08-May-19	21-May-19	25-May-19	06-Jun-19	49	0%	0	10	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P3											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P3	8	8	08-May-19	21-May-19	17-May-19	29-May-19	34	0%	0	10	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P3											
S2-PW1	Install steel cage and concreting -E5-P3	4	4	18-May-19	30-May-19	22-May-19	03-Jun-19	42	0%	0	10	Install steel cage and concreting -E5-P3											
Pile E5 -P4	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P4	15	15	18-May-19	30-May-19	30-May-19	17-Jun-19	39	0%	0	10	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P4											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P4	8	8	18-May-19	30-May-19	27-May-19	08-Jun-19	34	0%	0	10	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P4											
S2-PW1	Install steel cage and concreting -E5-P4	4	4	28-May-19	10-Jun-19	31-May-19	13-Jun-19	38	0%	0	10	Install steel cage and concreting -E5-P4											
Pile E5 -P5	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P5	15	15	28-May-19	10-Jun-19	14-Jun-19	26-Jun-19	34	0%	0	10	Drive Casing & Grab to excavate the soil (40.4m length) -E5-P5											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P5	8	8	28-May-19	10-Jun-19	05-Jun-19	18-Jun-19	34	0%	0	10	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E5-P5											
S2-PW1	Install steel cage and concreting -E5-P5	4	4	06-Jun-19	19-Jun-19	11-Jun-19	22-Jun-19	34	0%	0	10	Install steel cage and concreting -E5-P5											
Piling Works for Pier E7												Piling Works for Pier E7											
S2-PW70	Piling platform installation -E7	4	4	13-Mar-19	15-Mar-19	16-Mar-19	19-Mar-19	53	0%	0	2	Piling platform installation -E7											
Pile E7 -P1	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P1	12	12	16-Mar-19	20-Mar-19	30-Mar-19	02-Apr-19	73	0%	0	2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P1											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P1	5	5	16-Mar-19	20-Mar-19	22-Mar-19	25-Mar-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P1											
S2-PW1	Install steel cage and concreting -E7-P1	4	4	22-Mar-19	26-Mar-19	27-Mar-19	29-Mar-19	69	0%	0	2	Install steel cage and concreting -E7-P1											
Pile E7 -P2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P2	15	15	22-Mar-19	26-Mar-19	10-Apr-19	12-Apr-19	68	0%	0	2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P2											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P2	8	8	22-Mar-19	26-Mar-19	01-Apr-19	03-Apr-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P2											
S2-PW1	Install steel cage and concreting -E7-P2	4	4	01-Apr-19	04-Apr-19	06-Apr-19	09-Apr-19	65	0%	0	2	Install steel cage and concreting -E7-P2											
Pile E7 -P3	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P3	15	15	01-Apr-19	04-Apr-19	23-Apr-19	25-Apr-19	63	0%	0	2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P3											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P3	8	8	01-Apr-19	04-Apr-19	11-Apr-19	13-Apr-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P3											
S2-PW1	Install steel cage and concreting -E7-P3	4	4	11-Apr-19	15-Apr-19	16-Apr-19	18-Apr-19	61	0%	0	2	Install steel cage and concreting -E7-P3											
Pile E7 -P4	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P4	15	15	11-Apr-19	15-Apr-19	03-May-19	06-May-19	58	0%	0	2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P4											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P4	8	8	11-Apr-19	15-Apr-19	24-Apr-19	26-Apr-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P4											
S2-PW1	Install steel cage and concreting -E7-P4	4	4	24-Apr-19	27-Apr-19	29-Apr-19	02-May-19	57	0%	0	2	Install steel cage and concreting -E7-P4											
Pile E7 -P5	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P5	15	15	24-Apr-19	27-Apr-19	14-May-19	16-May-19	53	0%	0	2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P5											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P5	8	8	24-Apr-19	27-Apr-19	04-May-19	07-May-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P5											
S2-PW1	Install steel cage and concreting -E7-P5	4	4	04-May-19	08-May-19	09-May-19	11-May-19	53	0%	0	2	Install steel cage and concreting -E7-P5											
Pile E7 -P6	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P6	12	12	14-May-19	17-May-19	28-May-19	30-May-19	53	0%	0	2	Drive Casing & Grab to excavate the soil (40.4m length) -E7-P6											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P6	5	5	14-May-19	17-May-19	20-May-19	22-May-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E7-P6											
S2-PW1	Install steel cage and concreting -E7-P6	4	4	20-May-19	23-May-19	24-May-19	27-May-19	53	0%	0	2	Install steel cage and concreting -E7-P6											
Testing	Sonic Test, interface core and full core for bored pile -E7	21	21	28-May-19	31-May-19	21-Jun-19	24-Jun-19	387	0%	0	2	Sonic Test, interface core and full core for bored pile -E7											
S2-PW1	Sonic Test, interface core and full core for bored pile -E7	21	21	28-May-19	31-May-19	21-Jun-19	24-Jun-19	387	0%	0	2	Sonic Test, interface core and full core for bored pile -E7											
Piling Works for Pier E1												Piling Works for Pier E1											
S2-PW75	Piling platform installation -E1	4	4	28-May-19	31-May-19	01-Jun-19	04-Jun-19	53	0%	0	2	Piling platform installation -E1											
Pile E1 -P1	Drive Casing & Grab to excavate the soil (42.4m length) -E1-P1	12	12	01-Jun-19	05-Jun-19	17-Jun-19	19-Jun-19	128	0%	0	2	Drive Casing & Grab to excavate the soil (42.4m length) -E1-P1											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E1-P1 (N)	5	5	01-Jun-19	05-Jun-19	08-Jun-19	11-Jun-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E1-P1 (N)											
S2-PW1	Install steel cage and concreting -E1-P1	4	4	08-Jun-19	12-Jun-19	13-Jun-19	15-Jun-19	113	0%	0	2	Install steel cage and concreting -E1-P1											
Pile E1 -P2	Drive Casing & Grab to excavate the soil (42.4m length) -E1-P2	8	8	08-Jun-19	12-Jun-19	18-Jun-19	20-Jun-19	53	0%	0	2	Drive Casing & Grab to excavate the soil (42.4m length) -E1-P2											
S2-PW1	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E1-P2	4	4	08-Jun-19	12-Jun-19	18-Jun-19	20-Jun-19	53	0%	0	2	Install RCD and excavate the rock under rockhead level to founding level (4m socket) - rig No.2 & air lifting -E1-P2											
Section 5 of the Works-All Works within Portion V (CBL E&M Plantroom)												Section 5 of the Works-All Works within Portion V (CBL E&M Plantroom)											
S5-PR1995	Installation of Sheet Pile	21	21	02-Apr-19	02-Apr-19	30-Apr-19	30-Apr-19	13	0%	0	0	Installation of Sheet Pile											
S5-PR2000	Excavation Works	28	28	02-May-19	02-May-19	04-Jun-19	04-Jun-19	13	0%	0	0	Excavation Works											

█ Remaining Level of Effort
 █ Remaining Work
 █ Critical Remaining Work
 ◆ Milestone
 ◆ Baseline Milestone
 ◆ Summary

CRBC
Three Month Rolling Programme

Date	Revision	Checked	Approved
08-Mar-19	Monthly updated on 8 Mar 2019		

Contract 2

Activity ID	Activity Name	Original Duration	Actual Duration	Remaining Float	Start	Finish	Calendar	Total Float	Activity % Complete	2019					
										Feb	Mar	Apr	May	Jun	
NE/2017/08-6 NE/2017/08 Three Months Rolling (data date 20190306)		240	24	982	08-Feb-19 A	28-Nov-19		982							
NE/2017/08-6.1 Project Key Dates		0	0	0				0							
NE/2017/08-6.1.1 Access Dates		0	0	0				0							
NE/2017/08-6.1.2 Key Dates		0	0	0				0							
NE/2017/08-6.1.3 Sectional Completion Dates		0	0	0				0							
NE/2017/08-6.1.4 Planned Completion		0	0	0				0							
NE/2017/08-6.2 Design and Method Statement, Material Submissions		172	28	1312	08-Feb-19 A	30-Jul-19	NE/2017/08(7days)	1312							
NE/2017/08-6.2.1 Contractor's Design		36	0	89	12-Mar-19	16-Apr-19	NE/2017/08(7days)	89							
AD1030 Alternative Designs - Prepare DDA Submission to Relevant Authorities		8	0	89	12-Mar-19	19-Mar-19	NE/2017/08(7days)	89	0%						
AD1040 Alternative Designs - Review and Acceptance of DDA (7D for PM and 21D for H)		28	0	89	20-Mar-19	16-Apr-19	NE/2017/08(7days)	89	0%						
NE/2017/08-6.2.2 Temporary Works Design		112	0	233	12-Mar-19	01-Jul-19	NE/2017/08(7days)	233							
TW1010 ELS for Excavation of Pile Caps, Raft Footings & Pad Footings (with 5D for ICE)		13	0	0	12-Mar-19	24-Mar-19	NE/2017/08(7days)	0	0%						
TW1050 Falsework & Formwork Design for Construction of Cycle Track Ramp (With 7D for ICE Certified and 21D for PM acceptance)		35	0	233	28-May-19	01-Jul-19	NE/2017/08(7days)	233	0%						
NE/2017/08-6.2.3 Method Statement for Major Construction Works		35	0	233	28-May-19	01-Jul-19	NE/2017/08(7days)	233							
MS1090 Method Statement for Construction of Cycle Track Ramp (With 7D for ICE Certified and 21D for PM acceptance)		35	0	233	28-May-19*	01-Jul-19	NE/2017/08(7days)	233	0%						
NE/2017/08-6.2.4 General Submissions		168	24	121	13-Feb-19 A	30-Jul-19	NE/2017/08(7days)	121							
GS1024 Review and Comment of Revised First Programme by AACL		14	14		13-Feb-19 A	26-Feb-19 A	NE/2017/08(7days)		100%						
GS1030 Preparation & Submission of Detailed Programme (with 21D for PM acceptance)		50	0	0	09-Mar-19	27-Apr-19*	NE/2017/08(7days)	0	0%						
GS1190 Preparation & Submission of SQR for Env. Boreholes EBH7 & EBH8		70	0	121	22-May-19	30-Jul-19	NE/2017/08(7days)	121	0%						
GS1220 Submission of Traffic Management Contingency Plan (with 21D for PM and 21D for HD acceptance)		56	7	48	02-Mar-19 A	26-Apr-19	NE/2017/08(7days)	48	12.5%						
GS1230 Submission of Comprehensive Construction Traffic Impact Assessment Report (with 21D for PM and 21D for HyD acceptance)		56	7	48	02-Mar-19 A	26-Apr-19	NE/2017/08(7days)	48	12.5%						
GS1330 Submission of Contingency Plan to Deal with Flooding during Wet Season (with 21D for PM acceptance)		35	0	18	09-Mar-19	12-Apr-19*	NE/2017/08(7days)	18	0%						
GS1410 Review and Acceptance of TTMS in TMLG		48	23	0	14-Feb-19 A	02-Apr-19	NE/2017/08(7days)	0	47.92%						
GS1420 Application and Acceptance of Road Work Advice		10	0	0	17-Apr-19	26-Apr-19	NE/2017/08(7days)	0	0%						
GS1450 Submission of Interface Management Plan (MTRC, C1 to C4) (with 21D PM and 21D MTRC Acceptance)		49	0	27	09-Mar-19	26-Apr-19	NE/2017/08(7days)	27	0%						
GS1460 Submission of Crisis Management Plan (with 21D PM acceptance)		28	0	21	09-Mar-19	05-Apr-19	NE/2017/08(7days)	21	0%						
NE/2017/08-6.2.5 Project Manager Acceptance of Sub-Contractors		108	17	1376	08-Feb-19 A	27-May-19	NE/2017/08(7days)	1376							
SC1100 Construction Video Film & Photographer		0	0			08-Feb-19 A	NE/2017/08(7days)		100%						
SC1150 Bored Piling Works		0	0			25-Feb-19 A	NE/2017/08(7days)		100%						
SC1170 Excavation, Lateral Supports & Earthworks		0	0	0		24-Mar-19*	NE/2017/08(7days)	0	0%						
SC1180 RC Structures for Elevated Deck, U-trough & Pad Footings		0	0	0		27-May-19*	NE/2017/08(7days)	0	0%						
NE/2017/08-6.3 NCE		26	26	251	11-Feb-19 A	09-Mar-19	NE/2017/08(7days)	251							
NCE110 Trees to be Transplanted outside LOHAS Park Package 4		26	26	251	11-Feb-19 A	09-Mar-19	NE/2017/08(7days)	251	100%						
NCE1120 Unexpected Gas Main at Extent of Elevated Deck, U Trough		26	26	3	11-Feb-19 A	09-Mar-19	NE/2017/08(7days)	3	100%						
NE/2017/08-6.4 Construction Works		230	14	76	21-Feb-19 A	28-Nov-19		76							
NE/2017/08-6.4.1 Preliminaries		39	14	18	21-Feb-19 A	08-Apr-19	NE/2017/08(6days)	18							
PREL1035 Installation of Utilities/ Ground Settlement Monitoring Points at MTRC's Development Area		6	6		21-Feb-19 A	27-Feb-19 A	NE/2017/08(6days)		100%						
PREL1037 Installation of Ground Settlement Monitoring Points at MTRC Development Phase 6 (Initial Reading on 14 Mar 2019)		17	12	8	23-Feb-19 A	14-Mar-19	NE/2017/08(6days)	8	70.59%						
PREL1120 Construction of Temporary Wheel Washing Facilities		6	0	0	18-Mar-19*	23-Mar-19	NE/2017/08(6days)	0	0%						
PREL1125 Construction of Wheel Washing Bay		12	0	18	25-Mar-19	08-Apr-19	NE/2017/08(6days)	18	0%						
PREL1180 Removal of Existing Lighting Columns (by others)		18	0	5	09-Mar-19	29-Mar-19	NE/2017/08(6days)	5	0%						
NE/2017/08-6.4.2 Construction Works of Portion I		0	0	0				0							
NE/2017/08-6.4.2.1 U-trough at Cycle Track		0	0	0				0							
NE/2017/08-6.4.2.2 Elevated Cycle Track		0	0	0				0							
NE/2017/08-6.4.2.3 Lift and Staircase		0	0	0				0							
NE/2017/08-6.4.3 Construction Works of Portion II		165	0	0	16-Mar-19	05-Oct-19	NE/2017/08(6days)	0							
NE/2017/08-6.4.3.1 Abutment 2A		20	0	0	21-May-19	13-Jun-19	NE/2017/08(6days)	0							
PORII.AB.1010 Pre-drilling Works for Alternative Bored Pile at Abutment 2A (8nos,10D/no,6rigs for 1st cycle,2rigs for 2nd cycle)		20	0	0	21-May-19	13-Jun-19	NE/2017/08(6days)	0	0%						
NE/2017/08-6.4.3.2 Elevated Deck		165	0	0	16-Mar-19	05-Oct-19	NE/2017/08(6days)	0							
PORII.ED.1010 Pre-drilling Works for Conforming Bored Pile (Elevated Deck) (1nos.,10D/no.,3rig on16/3,6rig for 8/5 for ED+UT)		50	0	0	16-Mar-19	20-May-19	NE/2017/08(6days)	0	0%						
PORII.ED.1020 Lower GL(+5.0 to 4.5mPD)and BP Construction(ED)(1nos,21D/pile,4tm for ED+UT,1st on3/25,2nd on 9/4,3rd+4th on 15/4)		109	0	0	25-Mar-19	07-Aug-19	NE/2017/08(6days)	0	0%						
PORII.ED.1055 Sheet Piling Works for Construction of Footing/ Pile Cap Along Northern Footpat		158	0	0	25-Mar-19	05-Oct-19	NE/2017/08(6days)	0	0%						
NE/2017/08-6.4.4 Construction Works of Portion III		180	9	0	27-Feb-19 A	05-Oct-19	NE/2017/08(6days)	0							
NE/2017/08-6.4.4.1 Construction of Elevated Deck and Abutment 2B		180	9	0	27-Feb-19 A	05-Oct-19	NE/2017/08(6days)	0							
PORIII.ED1010 Pre-drilling Works for Conforming Bored Pile (Abutment 2B) (3nos.,10D/no.,3rig		15	9	0	27-Feb-19 A	15-Mar-19	NE/2017/08(6days)	0	60%						
PORIII.ED1015 Pre-drilling Works for Conforming Bored Pile (Elevated Deck)(9nos,10D/no,3rig on16/3,6rig for 8/5 for ED+UT)		50	0	0	16-Mar-19	20-May-19	NE/2017/08(6days)	0	0%						
PORIII.ED1020 Lower GL(+5.0 to 4.5mPD)and BP Construction(ED+AB2B)(12nos,21D/pile,4tm for ED+UT,1st on25/3,2nd on 9/4,3rd+4th on 15/4)		109	0	0	25-Mar-19	07-Aug-19	NE/2017/08(6days)	0	0%						
PORIII.ED1055 Sheet Piling Works for Construction of Footing/ Pile Cap Along Northern Footpat		158	0	0	25-Mar-19	05-Oct-19	NE/2017/08(6days)	0	0%						
NE/2017/08-6.4.4.2 Construction of U-trough Structure		165	0	0	16-Mar-19	05-Oct-19	NE/2017/08(6days)	0							
PORIII.UT1010 Pre-drilling Works for Conforming Bored Pile (U-trough) (8nos,10D/no,3rig on16/3,6rig for 8/5 for ED+UT)		50	0	0	16-Mar-19	20-May-19	NE/2017/08(6days)	0	0%						
PORIII.UT1020 Lower GL(+5.0 to 4.5mPD)and BP Construction(UT)(8nos,21D/pile,4tm for ED+UT,1st on3/25,2nd on 9/4,3rd+4th on 15/4)		105	0	0	25-Mar-19	02-Aug-19	NE/2017/08(6days)	0	0%						

■ Actual Level of Effort ◆ Milestone
■ Actual Work ◆ summary
■ Remaining Work
■ Critical Remaining Work



Contract No.: NE/2017/08
Cross Bay Link, Tseung Kwan O
Road D9 and Associated Works
 Page 1 of 2



Date	Revision	Checked	Approved
08-Mar-19	Three Month Rolling (Feb 2019)	HY	StL

Activity ID	Activity Name	Original Duration	Actual Duration	Remaining Float	Start	Finish	Calendar	Total Float	Activity % Complete	2019					
										Feb	Mar	Apr	May	Jun	
PORIII.UT1055	Sheet Piling Works for Construction of Footing/Pile Cap along northern Footpath	158	0	0	25-Mar-19	05-Oct-19	NE/2017/08(6days)	0	0%						
NE/2017/08-6.4.5	Modification of Seawall (Portion II and III)	14	0	0	02-Apr-19	18-Apr-19	NE/2017/08(6days)	0	0%						
SW1025	Installation of 2nd layer Temporary Concrete Block Wall for Weather Protection	14	0	0	02-Apr-19	18-Apr-19*	NE/2017/08(6days)	0	0%						
NE/2017/08-6.4.6	Construction of the At-grade Noise Semi Enclosures	158	0	0	25-Mar-19	05-Oct-19	NE/2017/08(6days)	0	0%						
NSE1005	Sheet Piling/Open Excavation Works for Construction of Footing/Pile Cap along northern Footpath	158	0	0	25-Mar-19	05-Oct-19	NE/2017/08(6days)	0	0%						
NE/2017/08-6.4.7	Tree Protection Works (Portion I, II and III)	88	0	161	04-May-19	17-Aug-19	NE/2017/08(6days)	161	0%						
TP1000	Preparation Works for Tree Transplant	88	0	161	04-May-19	17-Aug-19	NE/2017/08(6days)	161	0%						
NE/2017/08-6.4.8	Wan O Road	178	0	0	27-Apr-19	28-Nov-19		0	0%						
WO1030	Implementation of TTA at FP for Construction of Environmental Borehole	5	0	0	27-Apr-19	03-May-19	NE/2017/08(6days)	0	0%						
WO1040	Construction of Environmental Borehole and Sampling (2nos, 10D/no. 2rigs)	14	0	0	04-May-19	21-May-19	NE/2017/08(6days)	0	0%						
WO1050	Chemical/Biological Testing for Environmental Borehole	191	0	0	22-May-19	28-Nov-19	NE/2017/08(7days)	0	0%						
WO1060	Utility Detection and Trial Pit at Footpath	7	0	0	04-May-19	11-May-19	NE/2017/08(6days)	0	0%						
WO1070	Installation of utility/Ground Settlement monitoring Points at Footpath	26	0	0	14-May-19	13-Jun-19	NE/2017/08(6days)	0	0%						
WO1080	Erection of Chain Link Fence and Vehicular Gate at Footpath	20	0	0	14-May-19	05-Jun-19	NE/2017/08(6days)	0	0%						
WO1090	Implementation of TTA at FP/Carriageway	6	0	0	06-Jun-19	13-Jun-19	NE/2017/08(6days)	0	0%						
NE/2017/08-6.5	Miscellaneous Works (Portion I, II and III)	0	0	0				0	0%						

█ Actual Level of Effort ◆ Milestone
█ Actual Work ◆ summary
█ Remaining Work
█ Critical Remaining Work




Contract No.: NE/2017/08
Cross Bay Link, Tseung Kwan O
Road D9 and Associated Works
 Page 2 of 2




Date	Revision	Checked	Approved
08-Mar-19	Three Month Rolling (Feb 2019)	HY	StL

Appendix D

**Monitoring Location
(Air Quality, Noise and Water Quality)**

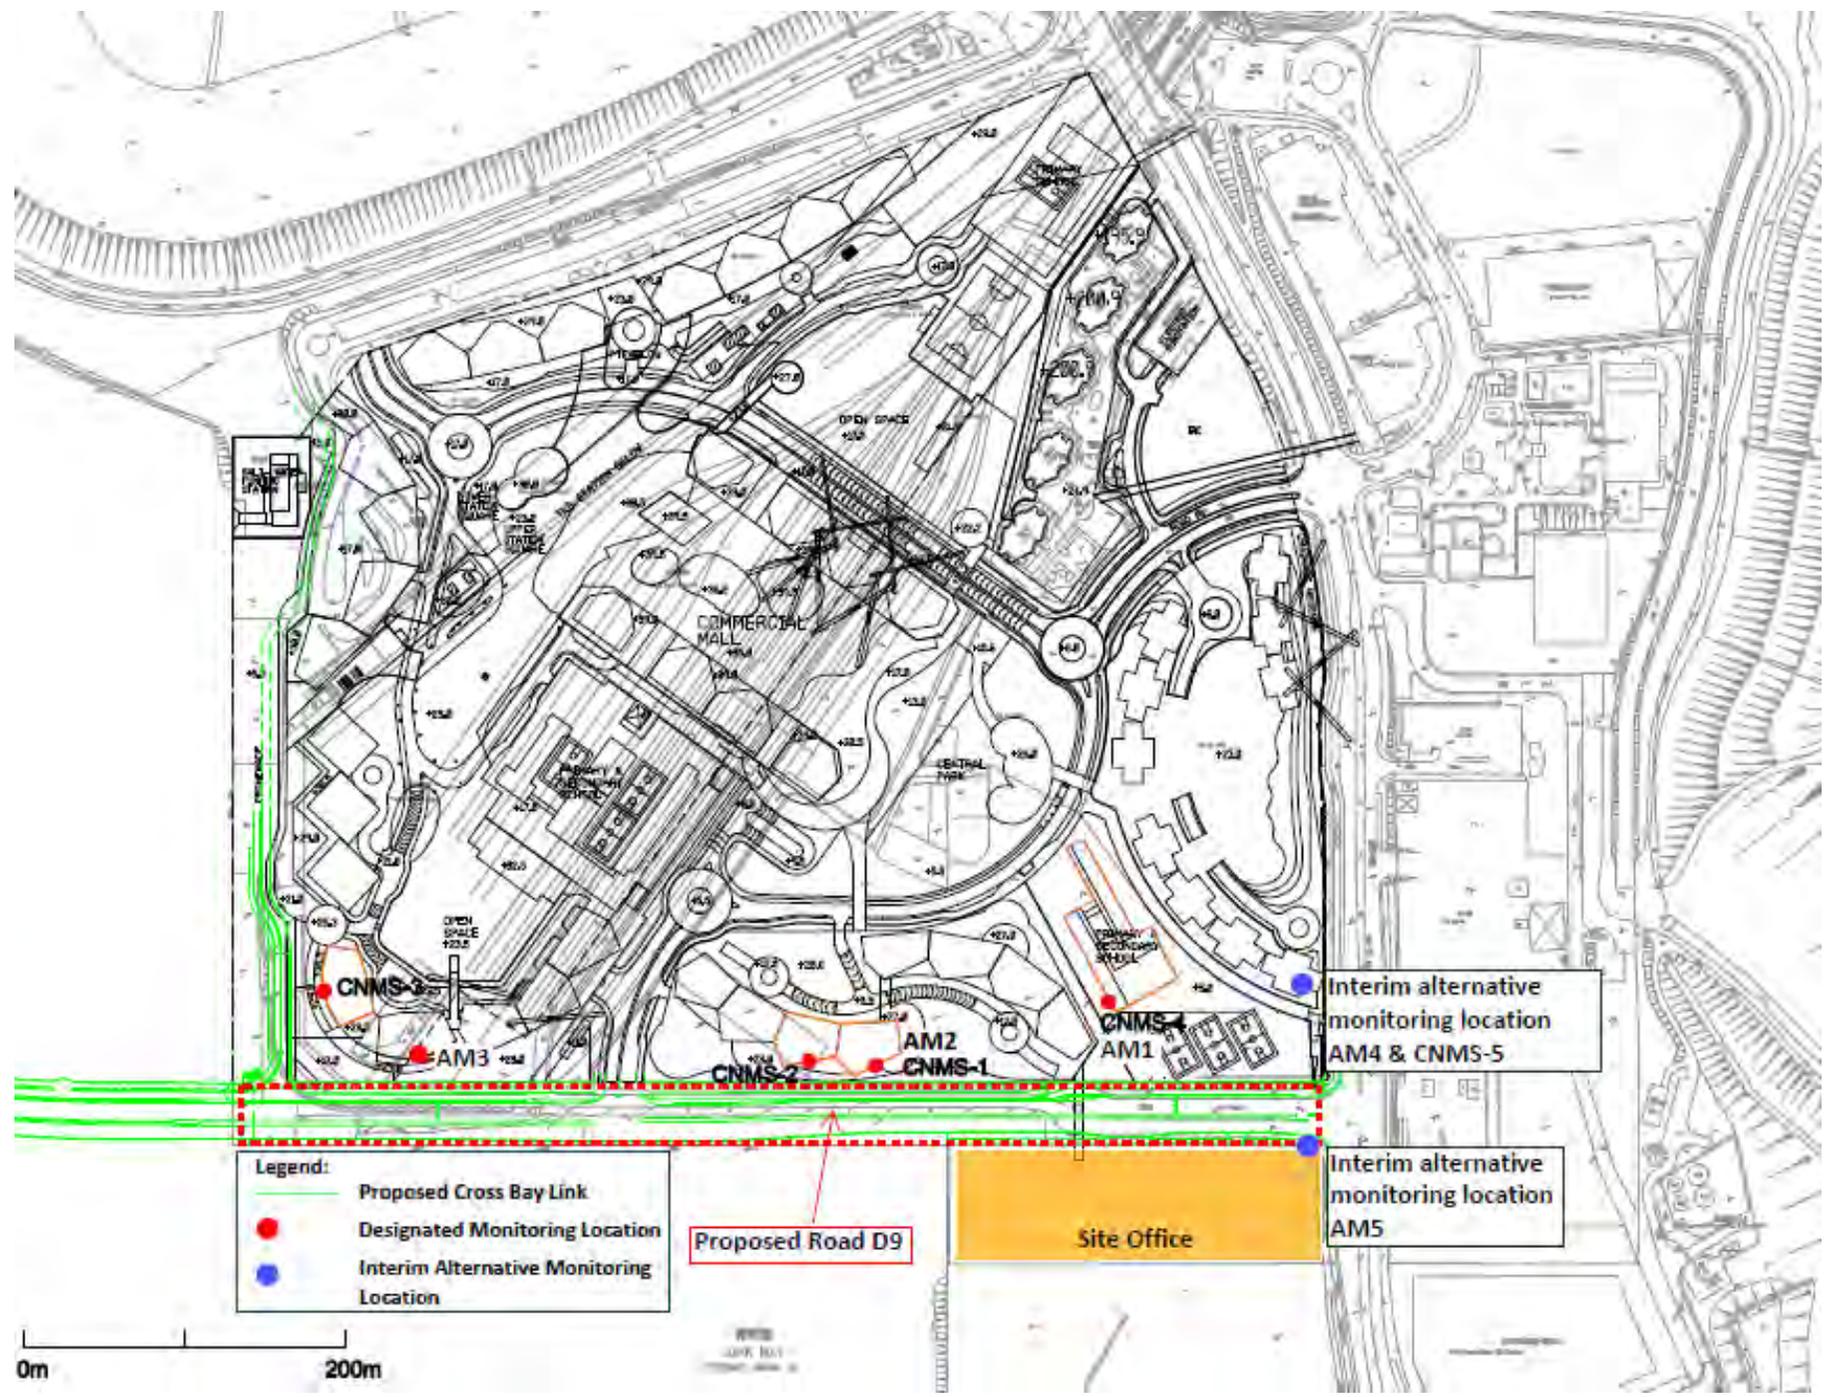

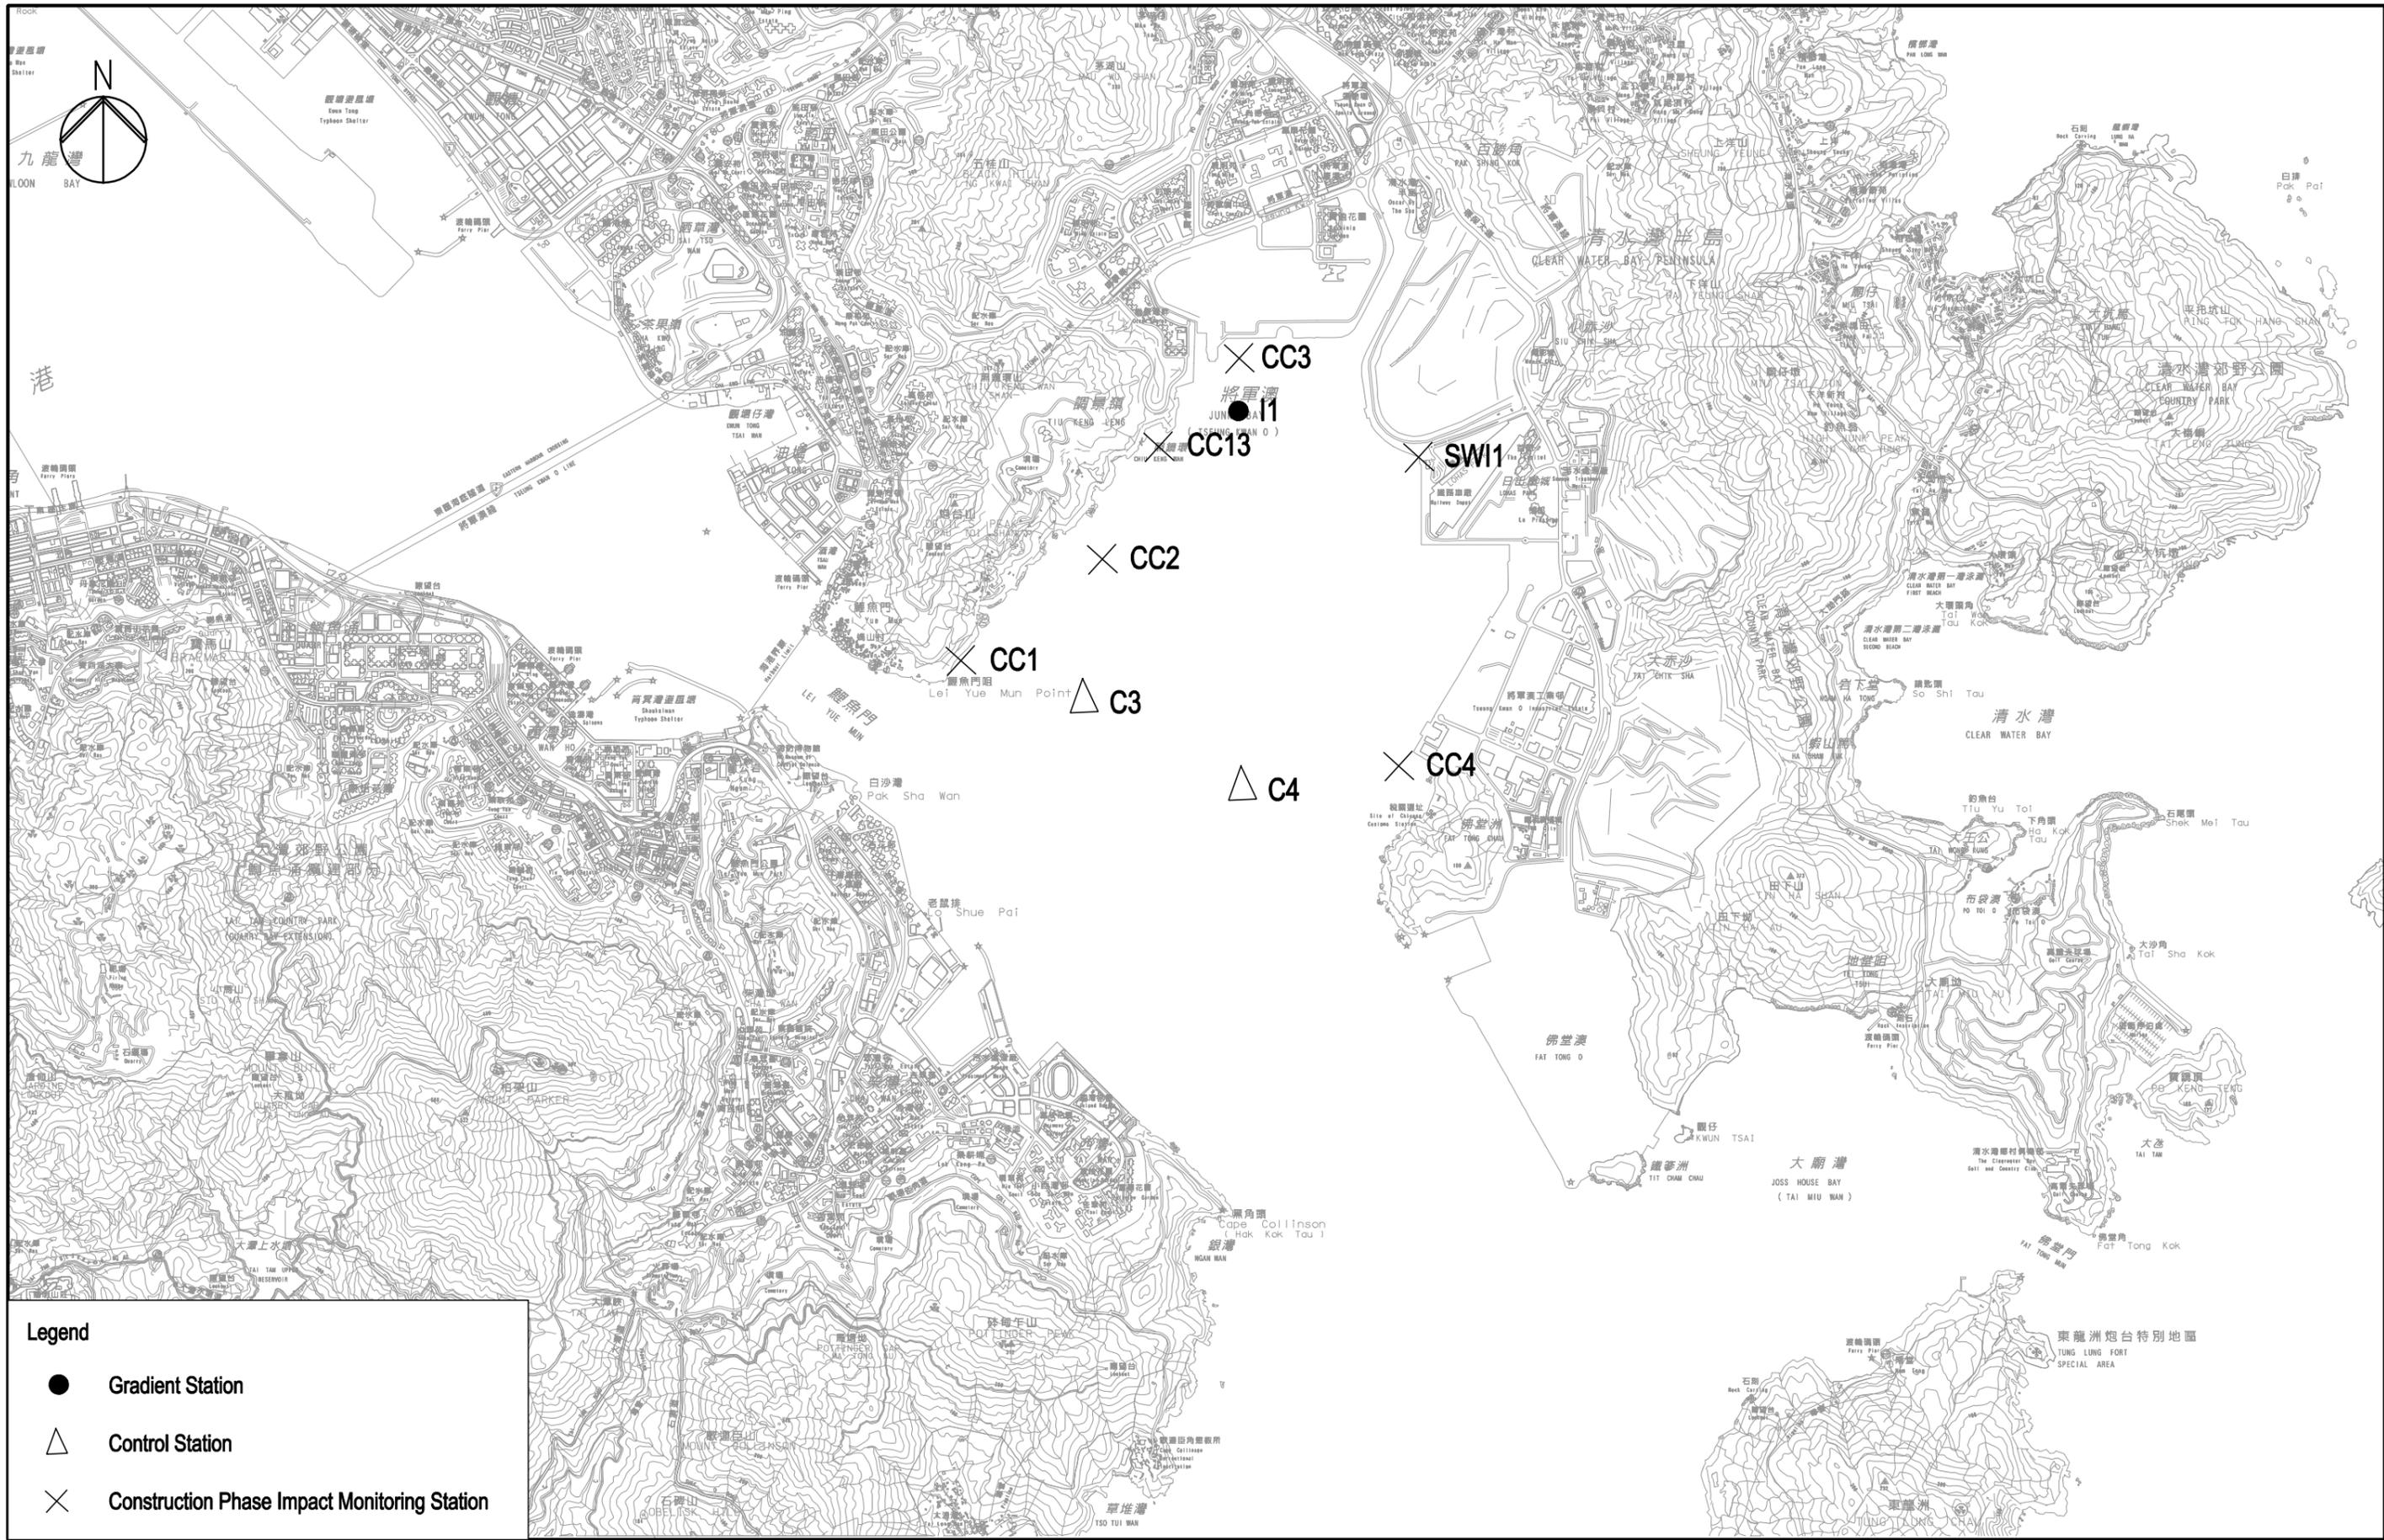

Legend

- Gradient Station
- △ Control Station
- × Construction Phase Impact Monitoring Station

3/1/2013
 H:\CDMA\4
 C:\temp\p020506-04\map\20130303_BAU\WQ_001.dwg
 Drawn by: GL
 Plotted by:



土木工程拓展署
 Civil Engineering and
 Development Department



Ove Arup & Partners
 Hong Kong Limited

Job Title
Agreement No. CE 43/2008(HY)
Cross Bay Link, Tseung Kwan O - Investigation

Drawing Title
**Locations of Water Quality
 Monitoring Stations**

Drawn	GL	Date	03/13	Drawing No.	209506/EMA/WQ/001	
C	THIRD ISSUE	03/13	Checked	JP	Approved	ST
B	SECOND ISSUE	01/13	Scale	1:30000 (A3)		
A	FIRST ISSUE	03/11	Status	FINAL		
Rev.	Description	Date	Rev.	C		

Appendix E

Event and Action Plan

**CEDD Contract Agreement No. EDO/04/2018 -
Environmental Team for Cross Bay Link, Tseung Kwan O
Event and Action Plan for Air Quality Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
ACTION LEVEL				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and Project Consultant; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and Project Consultant; 3. Advise the Project Consultant on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and Project Consultant; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.

**CEDD Contract Agreement No. EDO/04/2018 -
 Environmental Team for Cross Bay Link, Tseung Kwan O
 Event and Action Plan for Air Quality Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
LIMIT LEVEL				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform Project Consultant, Contractor, IEC and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and Project Consultant informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the Project Consultant on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; 4. Amend proposal if appropriate.

**CEDD Contract Agreement No. EDO/04/2018 -
Environmental Team for Cross Bay Link, Tseung Kwan O
Event and Action Plan for Air Quality Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
LIMIT LEVEL				
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, Project Consultant, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and Project Consultant to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and Project Consultant informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst Project Consultant, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the Project Consultant accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the Project Consultant until the exceedance is abated.

**CEDD Contract Agreement No. EDO/04/2018 -
Environmental Team for Cross Bay Link, Tseung Kwan O
Event and Action Plan for Construction Noise Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
Action Level	<ol style="list-style-type: none"> 1. Notify IEC and contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, Project Consultant and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the Project Consultant accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, Project Consultant, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, Project Consultant and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and Project Consultant informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst Project Consultant, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the Project Consultant accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the Project Consultant until the exceedance is abated.

**CEDD Contract Agreement No. EDO/04/2018 -
Environmental Team for Cross Bay Link, Tseung Kwan O
Event and Action Plan for Marine Water Quality Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
Action level being exceeded by one sampling day at water sensitive receiver(s)	<ol style="list-style-type: none"> 1. Identify the source(s) of impact by comparing the results with those collected at the gradient stations and the control stations as appropriate; 2. If exceedance is found to be caused by the marine works, repeat <i>in-situ</i> measurement to confirm findings; 3. Inform IEC and contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. If exceedance occurs at WSD salt water intake, inform WSD; 6. Discuss mitigation measures with IEC and Contractor; 7. Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss mitigation measures with ET and Contractor; 2. Review proposal on mitigation measures submitted by Contractor and advise the Project Consultant accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss proposed mitigation measures with IEC; 2. Make agreement on the mitigation proposal. 	<ol style="list-style-type: none"> 1. Inform the Project Consultant and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Amend working methods if appropriate; 5. Discuss with ET and IEC and propose mitigation measures to IEC and Project Consultant; 6. Implement the agree mitigation measures.
Action level being exceeded by two or more consecutive sampling days at water sensitive receiver(s)	<ol style="list-style-type: none"> 1. Identify the source(s) of impact by comparing the results with those collected at the gradient stations and the control stations as appropriate; 2. If exceedance is found to be caused by the marine works, repeat <i>in-situ</i> measurement to confirm findings; 3. Inform IEC and contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, and Contractor; 6. Ensure mitigation measures are 	<ol style="list-style-type: none"> 1. Discuss mitigation measures with ET and Contractor; 2. Review proposal on mitigation measures submitted by Contractor and advise the Project Consultant accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss proposed mitigation measures with IEC; 2. Make agreement on the mitigation proposal; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the Project Consultant and confirm notification of the noncompliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET, IEC and Project Consultant and propose mitigation measures to IEC and Project Consultant within 3 working

**CEDD Contract Agreement No. EDO/04/2018 -
Environmental Team for Cross Bay Link, Tseung Kwan O
Event and Action Plan for Marine Water Quality Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
	<p>implemented;</p> <p>7. Prepare to increase the monitoring frequency to daily;</p> <p>8. If exceedance occurs at WSD salt water intake, inform WSD;</p> <p>9. Repeat measurement on next day of exceedance.</p>			<p>days;</p> <p>5. Implement the agreed mitigation measures.</p>
<p>Limit level being exceeded by one sampling day at water sensitive receiver(s)</p>	<p>1. Identify the source(s) of impact by comparing the results with those collected at the gradient stations and the control stations as appropriate;</p> <p>2. If exceedance is found to be caused by the marine works, repeat <i>in-situ</i> measurement to confirm findings;</p> <p>3. Inform IEC, contractor and EPD</p> <p>4. Check monitoring data, all plant, equipment and Contractor's working methods;</p> <p>5. Discuss mitigation measures with IEC, ER and Contractor;</p> <p>6. Ensure mitigation measures are implemented;</p> <p>7. If exceedance occurs at WSD salt water intake, inform WSD.</p> <p>8. ET should contact AFCD if the limit level is exceeded by one sampling day or two or more consecutive sampling days at water sensitive receiver(s).</p>	<p>1. Discuss mitigation measures with ET and Contractor;</p> <p>2. Review proposal on mitigation measures submitted by Contractor and advise the Project Consultant accordingly;</p> <p>3. Assess the effectiveness of the implemented mitigation measures.</p>	<p>1. Discuss proposed mitigation measures with IEC, ET and Contractor;</p> <p>2. Request Contractor to critically review the working methods;</p> <p>3. Make agreement on the mitigation measures to be implemented;</p> <p>4. Assess the effectiveness of the implemented mitigation measures.</p>	<p>1. Inform the Project Consultant and confirm notification of the noncompliance in writing;</p> <p>2. Rectify unacceptable practice;</p> <p>3. Check all plant and equipment and consider changes of working methods;</p> <p>4. Discuss with ET, IEC and Project Consultant and submit proposal of mitigation measures to IEC and Project Consultant within 3 working days of notification;</p> <p>5. Implement the agreed mitigation measures.</p>
<p>Limit level being exceeded by two or more</p>	<p>1. Identify the source(s) of impact by comparing the results with those collected at the gradient stations and the</p>	<p>1. Discuss mitigation measures with ET and Contractor;</p>	<p>1. Discuss proposed mitigation measures with IEC, ET and Contractor;</p>	<p>1. Inform the Project Consultant and confirm notification of the</p>

**CEDD Contract Agreement No. EDO/04/2018 -
Environmental Team for Cross Bay Link, Tseung Kwan O
Event and Action Plan for Marine Water Quality Monitoring**



EVENT	ACTION			
	Environmental Team (ET)	Independent Environmental Checker (IEC)	Project Consultant	Contractor
consecutive sampling days at water sensitive receiver(s)	<p>control stations as appropriate; 2. If exceedance is found to be caused by the marine works, repeat <i>in-situ</i> measurement to confirm findings; 3. Inform IEC, contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, and Contractor; 6. Ensure mitigation measures are implemented; 7. Prepare to increase the monitoring frequency to daily; 8. If exceedance occurs at WSD salt water intake, inform WSD; 9. Repeat measurement on next day of exceedance.</p>	<p>2. Review proposal on mitigation measures submitted by Contractor and advise the Project Consultant accordingly; 3. Assess the effectiveness of the implemented mitigation measures.</p>	<p>2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level.</p>	<p>noncompliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Discuss with ET, IEC and Project Consultant and submit proposal of mitigation measures to IEC and Project Consultant within 3 working days of notification; 5. Implement the agreed mitigation measures; 6. As directed by the Engineer, to slow down or to stop all or part of the construction activities.</p>

Appendix F

Impact Monitoring Schedule of the Reporting Month and Coming Month

Impact Monitoring Schedule for coming month – March 2019

Date	Noise Monitoring ($L_{eq}30min$)	Air Quality Monitoring		Water Quality
		1-Hour TSP	24-Hour TSP	
Fri	1-Mar-19			
Sat	2-Mar-19		✓	✓
Sun	3-Mar-19			
Mon	4-Mar-19			✓
Tue	5-Mar-19			
Wed	6-Mar-19			*
Thu	7-Mar-19			✓
Fri	8-Mar-19	✓	✓	
Sat	9-Mar-19			✓
Sun	10-Mar-19			
Mon	11-Mar-19			✓
Tue	12-Mar-19			
Wed	13-Mar-19			✓
Thu	14-Mar-19	✓	✓	
Fri	15-Mar-19			✓
Sat	16-Mar-19			
Sun	17-Mar-19			
Mon	18-Mar-19			✓
Tue	19-Mar-19			
Wed	20-Mar-19	✓	✓	✓
Thu	21-Mar-19			✓
Fri	22-Mar-19			✓
Sat	23-Mar-19			
Sun	24-Mar-19			
Mon	25-Mar-19			✓
Tue	26-Mar-19	✓	✓	
Wed	27-Mar-19			✓
Thu	28-Mar-19			
Fri	29-Mar-19			
Sat	30-Mar-19			✓
Sun	31-Mar-19			

✓	Monitoring Day
	Sunday or Public Holiday

* Cancelled due to adverse weather condition

Marine Water Quality Monitoring Schedule

Scheduled Monitoring Day		Tides of Tai Miu Wan		Proposed Sampling Time (#)	
		Mid-Ebb	Mid-Flood	Mid-Ebb	Mid-Flood
2-Mar-19	Sat	10:14	15:07	08:29 – 11:59	13:22 – 16:52
4-Mar-19	Mon	11:34	16:44	09:49 – 13:19	14:59 – 18:29
7-Mar-19	Thu	13:05	18:43*	11:20 – 14:50	16:30 – 20:28*
9-Mar-19	Sat	14:05	08:08*	12:20 – 15:50	08:00 – 09:53*
11-Mar-19	Mon	15:18	09:02*	13:33 – 17:03	08:00 – 10:47*
13-Mar-19	Wed	16:53	09:59	15:08 – 18:38	08:14 – 11:44
15-Mar-19	Fri	19:31*	11:31	16:30 – 21:16*	09:46 – 13:16
18-Mar-19	Mon	10:25	15:41	08:40 – 12:10	13:56 – 17:26
20-Mar-19	Wed	17:43	11:56	15:58 – 19:28	10:11 – 13:46
22-Mar-19	Fri	13:17	07:20*	11:32 – 15:02	08:00 – 09:05*
25-Mar-19	Mon	15:19	08:58*	13:34 – 17:04	08:00 – 10:43*
27-Mar-19	Wed	17:11	09:59	15:26 – 18:56	08:14 – 11:44
30-Mar-19	Sat	20:44*	08:22*	16:30 – 22:29*	08:00 – 10:09*

Remark: The water quality sampling will be undertaken within a three and half hour window of 1.75 hour before and 1.75 hour after mid flood and mid-ebb tides.

(*) Due to safety reason, the sampling time will be started at 08:00 or 16:30

Impact Monitoring Schedule for coming month – April 2019

Date		Noise Monitoring (L _{eq} 30min)	Air Quality Monitoring		Water Quality
			1-Hour TSP	24-Hour TSP	
Mon	1-Apr-19	✓	✓		✓
Tue	2-Apr-19			✓	
Wed	3-Apr-19				✓
Thu	4-Apr-19				
Fri	5-Apr-19				
Sat	6-Apr-19		✓		✓
Sun	7-Apr-19				
Mon	8-Apr-19			✓	✓
Tue	9-Apr-19				
Wed	10-Apr-19				✓
Thu	11-Apr-19				
Fri	12-Apr-19	✓	✓		✓
Sat	13-Apr-19			✓	
Sun	14-Apr-19				
Mon	15-Apr-19				✓
Tue	16-Apr-19				
Wed	17-Apr-19	✓	✓		✓
Thu	18-Apr-19			✓	
Fri	19-Apr-19				✓
Sat	20-Apr-19				
Sun	21-Apr-19				
Mon	22-Apr-19				
Tue	23-Apr-19	✓	✓		✓
Wed	24-Apr-19			✓	
Thu	25-Apr-19				✓
Fri	26-Apr-19				
Sat	27-Apr-19		✓		✓
Sun	28-Apr-19				
Mon	29-Apr-19				
Tue	30-Apr-19			✓	✓
✓		Monitoring Day			
		Sunday or Public Holiday			

Marine Water Quality Monitoring Schedule

Scheduled Monitoring Day		Tides of Tai Miu Wan		Proposed Sampling Time (#)	
		Mid-Ebb	Mid-Flood	Mid-Ebb	Mid-Flood
1-Apr-19	Mon	10:41	15:37	08:56 – 12:26	13:52 – 17:22
3-Apr-19	Wed	11:41	17:13	09:56 – 13:26	15:28 – 18:58
6-Apr-19	Sat	13:07	06:59*	11:22 – 14:52	08:00 – 08:44*
8-Apr-19	Mon	14:14	07:51*	12:29 – 15:59	08:00 – 09:36*
10-Apr-19	Wed	15:32	08:41*	13:47 – 17:17	08:00 – 09:26*
12-Apr-19	Fri	16:49	08:59	15:04 – 18:34	08:00 – 10:44*
15-Apr-19	Mon	09:14*	14:23	08:00 – 10:59*	12:38 – 16:08
17-Apr-19	Wed	10:55	16:43	09:05 – 12:35	14:58 – 18:28
19-Apr-19	Fri	12:15	06:08*	10:30 – 14:00	08:00 – 08:45*
23-Apr-19	Tue	14:53	08:14*	13:08 – 16:38	08:00 – 09:59*
25-Apr-19	Thu	16:34	09:02*	14:49 – 18:19	08:00 – 10:47*
27-Apr-19	Sat	18:47*	05:41*	16:30 – 20:32*	08:00 – 08:45*
30-Apr-19	Tue	10:10	15:01	08:25 – 11:55	13:16 – 16:46

Remark: The water quality sampling will be undertaken within a three and half hour window of 1.75 hour before and 1.75 hour after mid flood and mid-ebb tides.

(*) Due to safety reason, the sampling time will be started at 08:00 or 16:30

Appendix G

Calibration Certificates of Equipment and Accreditation Laboratory Certificate



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence
此實驗所符合ISO / IEC 17025 : 2005 - 《測試及校正實驗所能力的通用規定》所訂的要求，
of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as
獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
listed in the HOKLAS Directory of Accredited Laboratories within the test category of
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。


This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作
quality management system (see joint IAF-ILAC-ISO Communiqué).
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS 066**
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日



TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Junction of Wan Po Road and Wan O Road Date of Calibration: 2-Mar-19
 Location ID : AM5 Next Calibration Date: 2-May-19
 Name and Model: TISCH HVS Model TE-5170 Technician: Ho

CONDITIONS

Sea Level Pressure (hPa)	1012.7	Corrected Pressure (mm Hg)	759.525
Temperature (°C)	21.5	Temperature (K)	295

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.0968
Model->	5025A	Qstd Intercept ->	-0.00065
Serial # ->	1941		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	4.60	4.60	9.2	1.455	58	58.67	Slope = 27.4676 Intercept = 19.0205 Corr. coeff. = 0.9974
13	3.40	3.40	6.8	1.251	53	53.61	
10	2.30	2.30	4.6	1.029	47	47.54	
7	1.50	1.50	3.0	0.831	42	42.49	
5	1.30	1.30	2.6	0.774	39	39.45	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))]-b$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

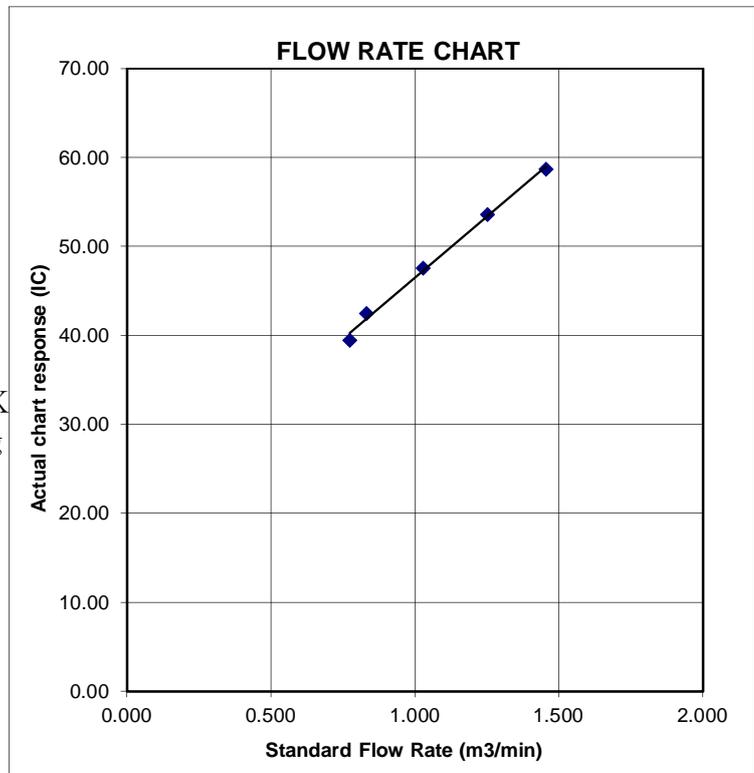

Certificate of Calibration

Calibration Certification Information			
Cal. Date: February 5, 2019	Rootsmeter S/N: 438320	Ta: 293	°K
Operator: Jim Tisch		Pa: 753.1	mm Hg
Calibration Model #: TE-5025A	Calibrator S/N: 1941		

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4830	3.2	2.00
2	3	4	1	1.0430	6.4	4.00
3	5	6	1	0.9300	7.9	5.00
4	7	8	1	0.8870	8.7	5.50
5	9	10	1	0.7320	12.7	8.00

Data Tabulation					
Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
1.0036	0.6767	1.4197	0.9958	0.6714	0.8821
0.9993	0.9581	2.0078	0.9915	0.9506	1.2475
0.9973	1.0723	2.2448	0.9895	1.0640	1.3947
0.9962	1.1231	2.3544	0.9884	1.1144	1.4628
0.9908	1.3536	2.8395	0.9831	1.3431	1.7642
QSTD	m=	2.09680	QA	m=	1.31298
	b=	-0.00065		b=	-0.00040
	r=	0.99999		r=	0.99999

Calculations	
Vstd= $\Delta Vol \left(\frac{Pa - \Delta P}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)$	Va= $\Delta Vol \left(\frac{Pa - \Delta P}{Pa} \right)$
Qstd= $Vstd / \Delta Time$	Qa= $Va / \Delta Time$
For subsequent flow rate calculations:	
Qstd= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions	
Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION
US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1908930
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 25-FEB-2019
		DATE OF ISSUE	: 4-MAR-2019
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.
- Calibration was subcontracted to and analysed by Action United Enviro Services.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung

General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F. Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1908930
SUB-BATCH : 1
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1908930-001	S/N: 3Y6503	AIR	25-Feb-2019	S/N: 3Y6503

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
 Manufacturer: Sibata LD-3B
 Serial No. 3Y6503
 Equipment Ref: EQ112
 Job Order HK1908930

Standard Equipment:

Standard Equipment: Higher Volume Sampler
 Location & Location ID: AUES office (calibration room)
 Equipment Ref: HVS 018
 Last Calibration Date: 21 December 2018

Equipment Verification Results:

Testing Date: 7 January 2019

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	09:01 ~ 11:08	18.5	1021.4	0.045	2403	19.0
2hr11min	11:13 ~ 13:24	18.5	1021.4	0.032	1577	12.1
2hr07min	13:30 ~ 15:37	18.5	1021.4	0.089	5129	40.5

Sensitivity Adjustment Scale Setting (Before Calibration) 655 (CPM)


Sensitivity Adjustment Scale Setting (After Calibration) 655 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022

Correlation Coefficient 0.9975

Date of Issue 14 January 2019

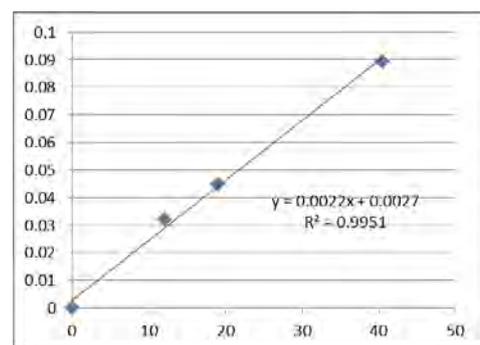

Remarks:

1. **Strong Correlation (R>0.8)**
 2. Factor 0.0022 should be apply for TSP monitoring
- *If R<0.5, repair or re-verification is required for the equipment

Operator : Martin Li Signature : [Signature] Date : 14 January 2019

QC Reviewer : Ben Tam Signature : [Signature] Date : 14 January 2019

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung Date of Calibration: 21-Dec-18
 Location ID : Calibration Room Next Calibration Date: 21-Mar-19

CONDITIONS

Sea Level Pressure (hPa)	1016.1	Corrected Pressure (mm Hg)	762.075
Temperature (°C)	22.4	Temperature (K)	295

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.02017
Model->	5025A	Qstd Intercept ->	-0.03691
Calibration Date->	13-Feb-18	Expiry Date->	13-Feb-19

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.7	5.7	11.4	1.699	56	56.32	Slope = 34.0074 Intercept = -0.4093 Corr. coeff. = 0.9972
13	4.4	4.4	8.8	1.495	51	51.29	
10	3.4	3.4	6.8	1.317	45	45.26	
8	2.3	2.3	4.6	1.086	36	36.21	
5	1.4	1.4	2.8	0.851	28	28.16	

Calculations :

$$Q_{std} = 1/m[\sqrt{H_2O(P_a/P_{std})(T_{std}/T_a)}] - b$$


$$IC = I[\sqrt{P_a/P_{std}}(T_{std}/T_a)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\sqrt{298/T_{av}}(P_{av}/760)] - b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

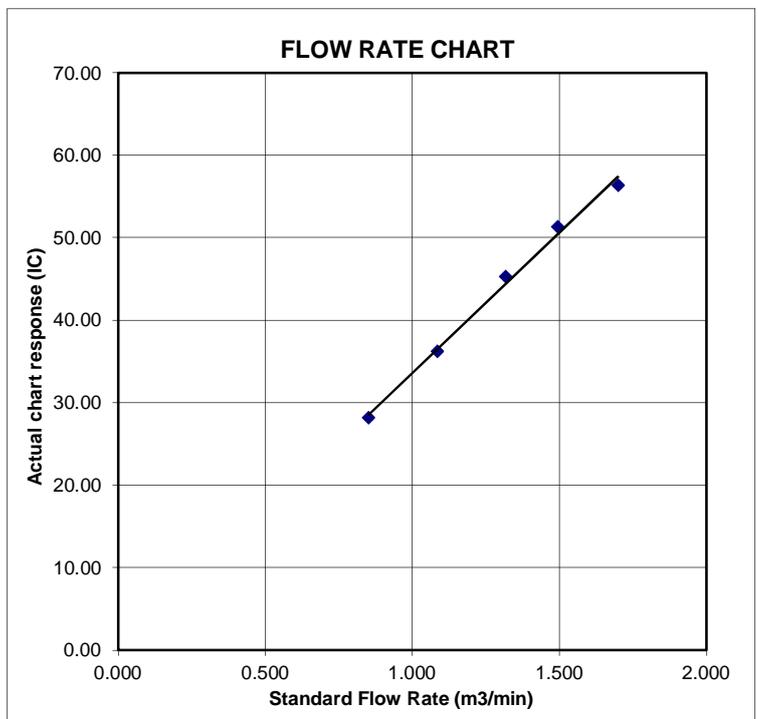



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C182472

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 26 April 2018

Description / 儀器名稱 : Sound Level Meter (EQ067)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-31

Serial No. / 編號 : 00410221

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C

Relative Humidity / 相對濕度 : (50 ± 25)%

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration

DATE OF TEST / 測試日期 : 12 May 2018

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By
測試


H T Wong
Technical Officer

Certified By
核證


K C Lee
Engineer

Date of Issue
簽發日期

15 May 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 1 of 4

Certificate of Calibration

校正證書

Certificate No. : C182472
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using the internal standard (After Adjustment) was performed before the test 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.

4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C180024
CL281	Multifunction Acoustic Calibrator	PA160023

5. Test procedure : MA101N.

6. Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Adjustment

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	92.9	± 1.1

6.1.1.2 After Adjustment

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 120	L _A	A	Fast	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.1

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C182472

證書編號

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 120	L _A	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	± 0.3

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _A	A	Fast	94.00	63 Hz	67.7	-26.2 ± 1.5
					125 Hz	77.8	-16.1 ± 1.5
					250 Hz	85.3	-8.6 ± 1.4
					500 Hz	90.7	-3.2 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	95.3	+1.2 ± 1.6
					4 kHz	95.1	+1.0 ± 1.6
					8 kHz	92.9	-1.1 (+2.1 ; -3.1)
					12.5 kHz	90.0	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 120	L _C	C	Fast	94.00	63 Hz	93.1	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.0	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.9	-0.2 ± 1.6
					4 kHz	93.3	-0.8 ± 1.6
					8 kHz	91.0	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.1	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Certificate of Calibration

校正證書

Certificate No. : C182472
證書編號

Remarks : - UUT Microphone Model No. : UC-53A & S/N : 319734

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : ± 0.35 dB
250 Hz - 500 Hz : ± 0.30 dB
1 kHz : ± 0.20 dB
2 kHz - 4 kHz : ± 0.35 dB
8 kHz : ± 0.45 dB
12.5 kHz : ± 0.70 dB
104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited

Calibration & Testing Laboratory

Certificate of Calibration

校正證書

Certificate No. : C183261
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC18-0867)

Date of Receipt / 收件日期 : 12 June 2018

Description / 儀器名稱 : Sound Calibrator (EQ086)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NC-74

Serial No. / 編號 : 34657230

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 18 June 2018

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By


測試



H T Wong
Technical Officer

Certified By

核證



K C Lee
Engineer

Date of Issue

簽發日期

20 June 2018

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 — 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C183261

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
2. The results presented are the mean of 3 measurements at each calibration point.
3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C173864
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C181288

4. Test procedure : MA100N.

5. Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.1	± 0.3	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.002	1 kHz ± 1 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



ALS Technichem (HK) Pty Ltd

11/F, Chung Shun Knitting Centre

1-3 Wing Yip Street, Kwai Chung

N.T., Hong Kong

T: +852 2610 1044 | F: +852 2610 2021

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT:	BEN TAM	WORK ORDER:	HK1906866
CLIENT:	ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS:	RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T., HONG KONG	SUB-BATCH:	0
		LABORATORY:	HONG KONG
		DATE RECEIVED:	18-Feb-2019
		DATE OF ISSUE:	26-Feb-2019

COMMENTS

The performance of the equipment stated in this report is checked with independent reference material and results compared against a calibrated secondary source.

The "Tolerance Limit" quoted is the acceptance criteria applicable for similar equipment used by the ALS Hong Kong laboratory or quoted from relevant international standards.

Scope of Test:	Conductivity, Dissolved Oxygen, pH Value, Turbidity, Salinity and Temperature
Equipment Type:	Multifunctional Meter
Brand Name:	YSI
Model No.:	Professional DSS
Serial No.:	15H102620/ 15H103928
Equipment No.:	EQW018
Date of Calibration:	25 February, 2019

NOTES

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr Chan Siu Ming, Vice
Manager - Inorganic

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1906866
 SUB-BATCH: 0
 DATE OF ISSUE: 26-Feb-2019
 CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Multifunctional Meter
 Brand Name: YSI
 Model No.: Professional DSS
 Serial No.: 15H102620/ 15H103928
 Equipment No.: EQW018
 Date of Calibration: 25 February, 2019 Date of Next Calibration: 25 May, 2019

PARAMETERS:

Conductivity Method Ref: APHA (21st edition), 2510B

Expected Reading ($\mu\text{S/cm}$)	Displayed Reading ($\mu\text{S/cm}$)	Tolerance (%)
6667	6119	-8.2
12890	11792	-8.5
58670	54356	-7.4
	Tolerance Limit (%)	± 10.0

Dissolved Oxygen Method Ref: APHA (21st edition), 4500-O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
2.63	2.54	-0.09
5.84	5.98	+0.14
8.57	8.56	-0.01
	Tolerance Limit (mg/L)	± 0.20

pH Value Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH unit)	Displayed Reading (pH unit)	Tolerance (pH unit)
4.0	3.98	-0.02
7.0	7.11	+0.11
10.0	10.05	+0.05
	Tolerance Limit (pH unit)	± 0.20

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vice
 Manager - Inorganic

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1906866
 SUB-BATCH: 0
 DATE OF ISSUE: 26-Feb-2019
 CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Multifunctional Meter
 Brand Name: YSI
 Model No.: Professional DSS
 Serial No.: 15H102620/ 15H103928
 Equipment No.: EQW018
 Date of Calibration: 25 February, 2019 Date of Next Calibration: 25 May, 2019

PARAMETERS:

Turbidity Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.02	--
4	3.75	-6.3
40	37.15	-7.1
80	83.91	+4.9
400	410.68	+2.7
800	792.16	-1.0
	Tolerance Limit (%)	±10.0

Salinity Method Ref: APHA (21st edition), 2520B

Expected Reading (ppt)	Displayed Reading (ppt)	Tolerance (%)
0	0.03	--
10	10.06	+0.6
20	20.02	+0.1
30	30.23	+0.8
	Tolerance Limit (%)	±10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr Chan Siu Ming, Vice
 Manager - Inorganic

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION



WORK ORDER: HK1906866
SUB-BATCH: 0
DATE OF ISSUE: 26-Feb-2019
CLIENT: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING

Equipment Type: Multifunctional Meter
Brand Name: YSI
Model No.: Professional DSS
Serial No.: 15H102620/ 15H103928
Equipment No.: EQW018
Date of Calibration: 25 February, 2019 Date of Next Calibration: 25 May, 2019

PARAMETERS:

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
10.5	10.9	+0.4
21.0	20.4	-0.6
39.0	38.7	-0.3
	Tolerance Limit (°C)	±2.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

A handwritten signature in black ink, appearing to read 'Chan Siu Ming'.

Mr Chan Siu Ming, Vice
Manager - Inorganic

Appendix H

Database of Monitoring Results

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-hr TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
4-Mar-19	23778	14418.62	14443.09	1468.20	49	49	49.0	20.9	1013.7	1.10	1621	2.5992	2.8672	0.2680	165
9-Mar-19	23837	14443.09	14467.57	1468.80	53	53	53.0	17.8	1012.2	1.26	1850	2.6032	2.9052	0.3020	163
15-Mar-19	23840	14467.57	14491.58	1440.60	50	51	50.5	20.2	1020	1.17	1681	2.6241	2.8376	0.2135	127
21-Mar-19	23844	14491.58	14515.48	1434.00	55	56	55.5	25.3	1011.4	1.33	1900	2.6067	2.7910	0.1843	97
27-Mar-19	23879	14515.48	14539.96	1468.80	58	59	58.5	22.3	1017.1	1.45	2131	2.6543	3.0153	0.3610	169

Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	
8-Mar-19	10:14	63.2	64.3	61.8	61.0	62.6	58.9	64.2	65.4	62.8	63.5	64.6	62.4	61.1	62.4	59.7	62.5	63.6	60.8	62.7
14-Mar-19	10:28	62.7	63.6	61.7	62.7	63.5	61.8	62.4	63.5	60.4	59.8	60.9	58.7	62.5	63.4	61.5	67.6	63.4	60.7	63.7
20-Mar-19	10:54	65.3	68.0	61.0	64.2	67.5	61.5	66.5	69.0	62.0	66.3	68.5	62.0	65.8	69.0	61.0	66.1	69.5	61.0	65.8
26-Mar-19	13:42	60.3	60.9	58.8	62.7	63.6	60.7	62.4	63.8	60.5	60.2	61.4	58.0	61.9	63.0	60.2	62.6	63.8	61.1	61.8

Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			Leq30min, dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	
15-Mar-19	19:06	59.4	63.7	52.4	59.5	61.8	52.5	58.0	61.7	50.2	59.0
21-Mar-19	19:24	63.1	65.7	55.6	62.8	65.0	54.2	60.1	62.8	53.3	62.2
28-Mar-19	19:16	61.7	65.0	54.7	61.3	65.0	54.3	61.0	64.4	53.9	61.3

Impact Water Quality Monitoring Result													
Sampling Date: 2-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
11:22	CC1	ME	843201	816416	9.51	1.00	19.2	7.12	93.5	0.54	32.59	8.45	1.2
							19.2	7.12	93.5	0.54	32.59	8.45	<1.0
						4.76	19.2	7.06	92.7	0.54	32.62	8.45	<1.0
							19.2	7.06	92.7	0.53	32.62	8.45	1
							19.2	7.04	92.4	0.60	32.63	8.45	1.1
11:30	CC2	ME	844076	817091	11.75	1.00	19.2	7.22	94.8	0.50	32.56	8.45	2.5
							19.2	7.21	94.8	0.50	32.56	8.45	1.7
						5.88	19.2	7.19	94.4	0.52	32.57	8.45	<1.0
							19.2	7.18	94.4	0.52	32.57	8.46	<1.0
							19.2	7.02	92.2	1.52	32.63	8.46	1.1
11:44	CC3	ME	844606	817941	9.14	1.00	19.2	7.10	93.2	0.78	32.53	8.45	1.8
							19.2	7.10	93.2	0.79	32.53	8.45	1.2
						4.57	19.2	7.12	93.5	0.70	32.59	8.45	1.4
							19.2	7.12	93.5	0.69	32.60	8.45	2.2
							19.2	7.08	93.0	0.81	32.62	8.46	3.1
11:05	CC4	ME	845444	815595	2.57	1.29	19.2	7.16	94.1	2.28	32.63	8.36	3.2
							19.3	7.15	93.9	1.42	32.60	8.36	2.7
11:34	CC13	ME	844200	817495	8.35	1.00	19.2	7.20	94.6	0.53	32.56	8.45	<1.0
							19.2	7.20	94.6	0.53	32.56	8.45	<1.0
						4.18	19.2	7.17	94.2	0.51	32.56	8.46	1
							19.2	7.17	94.2	0.52	32.56	8.46	1.9
							19.2	7.13	93.7	0.53	32.58	8.46	<1.0
10:57	SWI1	ME	845512	817442	3.92	1.00	19.2	7.13	93.7	0.55	32.58	8.46	1.2
							19.3	7.20	94.7	0.50	32.59	8.27	3.2
							19.3	7.21	94.7	0.50	32.59	8.27	2.4
11:18	C3	ME	843821	816211	15.29	2.92	19.2	7.21	94.7	0.56	32.61	8.30	<1.0
							19.2	7.21	94.7	0.57	32.61	8.30	<1.0
							19.2	7.22	94.8	0.55	32.61	8.45	2
							19.2	7.20	94.5	0.49	32.63	8.45	1.3
							19.2	7.20	94.5	0.46	32.63	8.45	2
11:09	C4	ME	844621	815770	16.17	1.00	19.2	7.18	94.2	0.51	32.63	8.45	1.7
							19.2	7.17	94.1	0.53	32.63	8.45	1.2
							19.2	7.17	94.1	0.53	32.63	8.45	1.1
							19.2	7.26	95.3	0.42	32.61	8.40	1.7
							19.2	7.26	95.3	0.41	32.61	8.40	1.1
11:39	II	ME	844602	817675	9.9	1.00	19.1	7.15	93.8	0.39	32.64	8.45	1.5
							19.1	7.15	93.8	0.39	32.64	8.45	1.5
							19.1	7.11	93.2	0.94	32.65	8.45	<1.0
							19.1	7.11	93.2	0.93	32.65	8.45	<1.0
							19.3	7.14	93.9	0.68	32.54	8.45	1.6
13:44	CC1	MF	843201	816416	9.17	1.00	19.2	7.13	93.8	0.39	32.64	8.45	1.5
							19.2	7.13	93.8	0.39	32.64	8.45	1.5
							19.2	7.13	93.8	0.39	32.64	8.45	1.5
							19.2	7.13	93.8	0.39	32.64	8.45	1.5
							19.2	7.13	93.8	0.39	32.64	8.45	1.5
13:50	CC2	MF	844076	817091	12.28	1.00	19.2	7.14	93.9	0.68	32.54	8.45	1.6
							19.3	7.14	93.8	0.68	32.54	8.45	1
							19.2	7.13	93.7	0.63	32.59	8.46	1.5
							19.2	7.13	93.7	0.62	32.59	8.46	2.1
							19.2	7.08	93.0	1.38	32.64	8.46	1.6
13:31	CC4	MF	845444	815595	2.54	1.00	19.2	7.07	92.8	1.54	32.64	8.46	<1.0
							19.3	7.16	94.3	0.52	32.57	8.44	1.2
							19.3	7.17	94.3	0.51	32.57	8.45	<1.0
							19.3	7.15	93.9	0.53	32.59	8.47	<1.0
							19.2	7.14	93.8	0.51	32.60	8.47	1.3
13:40	C3	MF	843821	816211	15.47	1.00	19.2	7.07	92.8	0.52	32.62	8.47	1.5
							19.2	7.06	92.7	0.53	32.62	8.47	1
							19.3	7.21	94.8	0.49	32.61	8.46	2.1
							19.3	7.25	95.4	0.51	32.57	8.46	1.7
							19.2	7.18	94.3	0.53	32.60	8.47	1.7
13:35	C4	MF	844621	815770	16.08	1.00	19.2	7.17	94.3	0.52	32.60	8.47	2.4
							19.2	7.1	93.1	0.68	32.63	8.47	2.8
							19.2	7.09	93.1	0.68	32.63	8.47	2.3
							19.3	7.13	93.7	0.65	32.47	8.45	1.5
							19.3	7.13	93.8	0.65	32.47	8.45	1.4
14:01	II	MF	844602	817675	10.08	1.00	19.3	7.16	94.1	4.96	32.63	8.45	2.8
							19.2	7.16	94.1	4.73	32.62	8.45	2.2
13:56	CC13	MF	844200	817495	8.12	1.00	19.3	7.03	92.5	1.16	32.57	8.46	2.9
							19.3	7.04	92.6	1.16	32.57	8.46	3.7
							19.3	7.05	92.8	1.25	32.57	8.46	3.3
							19.3	7.06	92.8	1.26	32.57	8.46	3
							19.2	7.07	92.9	1.52	32.59	8.47	2.2
13:24	SWI1	MF	845512	817442	4.28	1.00	19.2	7.07	92.9	1.49	32.59	8.47	1.7
							19.6	7.08	93.6	0.45	32.35	8.47	2.8
							19.6	7.09	93.6	0.46	32.40	8.47	1.9
13:40	C3	MF	843821	816211	15.47	3.28	19.3	7.23	95.1	0.52	32.60	8.49	2.4
							19.3	7.23	95.1	0.51	32.60	8.49	1.5
							19.3	7.15	94.1	0.47	32.58	8.47	2.1
							19.3	7.15	94.1	0.47	32.58	8.47	2.8
							19.2	7.12	93.5	0.40	32.61	8.47	1.9
13:35	C4	MF	844621	815770	16.08	7.74	19.2	7.12	93.5	0.41	32.61	8.47	2.6
							19.2	7.10	93.2	0.36	32.62	8.47	1.4
							19.2	7.10	93.2	0.36	32.62	8.47	2
							19.3	7.29	95.8	0.40	32.60	8.47	1.8
							19.3	7.30	96.0	0.39	32.61	8.48	1.7
14:01	II	MF	844602	817675	10.08	8.04	19.2	7.33	96.4	0.38	32.62	8.48	2.7
							19.2	7.33	96.4	0.38	32.62	8.48	2.7
							19.2	7.27	95.4	0.27	32.63	8.48	1
							19.2	7.26	95.3	0.28	32.63	8.48	1.6
							19.3	7.24	95.2	0.62	32.54	8.46	1.9
13:56	CC13	MF	844200	817495	8.12	1.00	19.3	7.24	95.2	0.61	32.54	8.46	1.1
							19.3	7.24	95.1	0.57	32.59	8.47	2.1
							19.3	7.23	95.1	0.58	32.59	8.47	2
							19.2	7.07	92.9	1.87	32.65	8.47	2.8
							19.2	7.06	92.7	1.97	32.65	8.47	2.1

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide
 For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 4-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
12:31	CC1	ME	843201	816416	7.43	1.00	19.3	7.28	95.8	0.86	32.59	8.46	<1.0
						19.4	7.24	95.4	0.86	32.51	8.47	<1.0	
						3.72	19.3	7.17	94.3	0.86	32.70	8.47	<1.0
						19.3	7.17	94.3	0.86	32.70	8.47	<1.0	
						6.43	19.3	7.14	93.9	0.96	32.72	8.47	<1.0
						19.3	7.14	93.9	0.96	32.72	8.47	<1.0	
12:38	CC2	ME	844076	817091	12.14	1.00	19.4	7.32	96.5	0.84	32.54	8.44	<1.0
						19.4	7.33	96.6	0.84	32.54	8.45	<1.0	
						6.07	19.2	7.11	93.5	0.98	32.65	8.48	2.3
						19.2	7.11	93.4	0.98	32.65	8.48	3.2	
						11.14	19.2	7.05	92.6	1.19	32.65	8.48	4.4
						19.2	7.04	92.6	1.21	32.65	8.48	4	
12:53	CC3	ME	844606	817941	9.19	1.00	19.6	7.46	98.7	0.89	32.45	8.45	<1.0
						19.6	7.48	98.9	0.90	32.46	8.45	<1.0	
						4.60	19.4	7.36	97.0	1.16	32.58	8.47	1
						19.4	7.34	96.7	1.18	32.59	8.47	1	
						8.19	19.3	7.23	95.1	1.29	32.62	8.47	1.5
						19.3	7.20	94.8	1.32	32.62	8.47	1.5	
12:12	CC4	ME	845444	815595	2.44	1.22	19.3	7.15	94.1	1.67	32.62	8.45	2.8
						19.3	7.05	92.7	1.66	32.64	8.47	2.1	
12:43	CC13	ME	844200	817495	8.06	1.00	19.3	7.26	95.6	0.85	32.58	8.44	<1.0
						19.3	7.26	95.5	0.92	32.58	8.44	<1.0	
						4.03	19.3	7.16	94.1	0.90	32.62	8.47	1.8
						19.3	7.15	94.1	0.91	32.62	8.47	1.6	
						7.06	19.3	7.12	93.7	0.95	32.62	8.47	1.4
						19.3	7.12	93.6	0.95	32.62	8.47	1.7	
12:04	SWI1	ME	845512	817442	3.86	1.00	19.4	7.19	94.8	0.85	32.59	8.54	2
						19.4	7.19	94.7	0.86	32.59	8.54	2.9	
						2.86	19.3	7.22	95.0	0.81	32.59	8.51	2.1
						19.3	7.22	95.0	0.82	32.59	8.51	2.9	
						1.00	19.4	7.28	95.9	0.78	32.59	8.43	1.2
						19.4	7.28	96.0	0.77	32.59	8.43	1	
12:25	C3	ME	843821	816211	15.23	7.62	19.4	7.20	94.9	0.81	32.59	8.47	<1.0
						19.4	7.20	94.9	0.81	32.59	8.47	<1.0	
						14.23	19.3	7.13	93.8	0.89	32.70	8.47	<1.0
						19.3	7.12	93.7	0.92	32.71	8.47	1	
						1.00	19.4	7.35	96.9	0.71	32.56	8.48	2.9
						19.4	7.35	96.9	0.71	32.56	8.48	2.1	
12:18	C4	ME	844621	815770	16.23	8.12	19.2	7.26	95.5	0.71	32.68	8.49	2.1
						19.2	7.26	95.4	0.71	32.69	8.49	1.6	
						15.23	19.2	7.14	93.9	0.86	32.78	8.48	<1.0
						19.2	7.14	93.9	0.84	32.78	8.48	<1.0	
						1.00	19.6	7.31	96.5	1.21	32.42	8.45	1.3
						19.6	7.31	96.5	1.21	32.42	8.45	2	
12:49	II	ME	844602	817675	10.05	5.03	19.3	7.21	94.9	1.34	32.58	8.47	1.9
						19.3	7.20	94.8	1.34	32.59	8.47	2.5	
						9.05	19.2	7.02	92.2	1.20	32.66	8.47	2
						19.2	7.02	92.2	1.19	32.66	8.47	1.2	
						1.00	19.4	7.39	97.4	0.84	32.57	8.47	2.1
						19.4	7.38	97.4	0.84	32.51	8.47	2.3	
15:21	CC1	MF	843201	816416	9.13	4.57	19.4	7.24	95.4	0.90	32.58	8.47	2
						19.4	7.25	95.5	0.89	32.57	8.47	1.5	
						8.13	19.4	7.25	95.6	0.87	32.58	8.47	1.3
						19.4	7.24	95.5	0.85	32.59	8.47	2	
						1.00	19.3	7.32	96.4	0.94	32.55	8.44	4.3
						19.4	7.32	96.4	0.96	32.55	8.45	3.4	
15:27	CC2	MF	844076	817091	12.03	6.02	19.3	7.28	95.8	0.86	32.62	8.47	2.1
						19.3	7.27	95.7	0.85	32.63	8.47	2.1	
						11.03	19.2	7.13	93.8	1.07	32.69	8.48	2.2
						19.2	7.13	93.8	1.06	32.69	8.48	1.8	
						1.00	19.4	7.45	98.3	1.11	32.50	8.46	1.7
						19.4	7.46	98.4	1.13	32.51	8.46	1.2	
15:43	CC3	MF	844606	817941	9.07	4.54	19.4	7.41	97.7	0.99	32.59	8.47	<1.0
						19.4	7.40	97.5	1.01	32.59	8.47	1.2	
						8.07	19.3	7.34	96.6	1.06	32.60	8.48	1.1
						19.3	7.32	96.3	1.10	32.61	8.48	<1.0	
						1.00	19.3	7.21	94.8	1.09	32.64	8.47	1.4
						19.3	7.21	94.8	1.09	32.64	8.47	<1.0	
15:33	CC13	MF	844200	817495	8.41	1.00	19.3	7.16	94.2	1.09	32.59	8.46	2.2
						19.3	7.16	94.3	1.08	32.57	8.46	1.6	
						4.21	19.3	7.16	94.3	1.07	32.58	8.47	<1.0
						19.3	7.16	94.3	1.06	32.58	8.47	<1.0	
						7.41	19.3	7.10	93.4	1.19	32.65	8.47	2.7
						19.3	7.09	93.3	1.19	32.66	8.47	2	
15:00	SWI1	MF	845512	817442	3.84	1.00	19.3	7.22	95.1	0.89	32.60	8.57	1.3
						19.3	7.24	95.3	0.88	32.60	8.57	1.9	
						2.84	19.3	7.20	94.7	1.47	32.62	8.58	6.4
						19.3	7.20	94.7	1.46	32.62	8.58	5.6	
						1.00	19.3	7.20	94.9	0.86	32.62	8.47	2.2
						19.3	7.21	94.9	0.85	32.62	8.48	1.8	
15:17	C3	MF	843821	816211	15.7	7.85	19.3	7.13	93.7	0.80	32.68	8.48	1.1
						19.3	7.12	93.7	0.80	32.68	8.48	1.1	
						14.70	19.3	7.06	92.9	0.88	32.70	8.47	3.9
						19.3	7.06	92.8	0.90	32.70	8.47	3.1	
						1.00	19.4	7.38	97.3	0.90	32.58	8.49	<1.0
						19.4	7.39	97.4	0.86	32.58	8.49	1.2	
15:10	C4	MF	844621	815770	16.03	8.02	19.4	7.36	96.9	0.81	32.59	8.49	1.3
						19.4	7.35	96.8	0.80	32.59	8.49	1.6	
						15.03	19.2	7.17	94.3	0.91	32.72	8.49	2.4
						19.2	7.17	94.3	0.83	32.71	8.49	2.5	
						1.00	19.6	7.40	97.9	1.04	32.44	8.44	1.2
						19.6	7.41	97.9	1.05	32.45	8.45	1	
15:38	II	MF	844602	817675	9.27	4.64	19.4	7.35	97.0	1.51	32.56	8.46	<1.0
						19.3	7.19	94.6	1.63	32.62	8.47	<1.0	
						8.27	19.2	7.04	92.5	1.16	32.66	8.47	1.6
						19.2	7.04	92.5	1.17	32.66	8.47	1.3	
						1.00	19.6	7.40	97.9	1.04	32.44	8.44	1.2
						19.6	7.41	97.9	1.05	32.45	8.45	1	

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide
 For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 7-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
14:22	CC1	ME	843201	816416	8.82	1.00	19.6	6.93	91.7	0.78	32.69	8.44	1.7
							19.6	6.91	91.5	0.79	32.69	8.44	2.2
						4.41	19.7	6.73	89.3	0.74	32.79	8.46	<1.0
							19.7	6.73	89.3	0.72	32.79	8.46	2.1
						7.82	19.7	6.71	89.0	0.81	32.82	8.46	2.1
							19.7	6.68	88.7	0.80	32.80	8.46	1.9
14:30	CC2	ME	844076	817091	11.22	1.00	19.4	6.91	91.0	0.82	32.34	8.45	2.2
							19.4	6.90	90.9	0.83	32.34	8.45	1.9
						5.61	19.6	6.81	90.1	0.72	32.61	8.46	<1.0
							19.6	6.81	90.1	0.72	32.61	8.46	<1.0
						10.22	19.7	6.73	89.1	0.77	32.74	8.46	1.1
							19.7	6.73	89.2	0.76	32.74	8.46	1
14:50	CC3	ME	844606	817941	8.93	1.00	19.6	6.88	90.7	0.90	32.28	8.43	1.7
							19.6	6.86	90.5	0.90	32.29	8.43	1.6
						4.47	19.6	6.78	89.7	0.83	32.69	8.44	1.4
							19.6	6.78	89.7	0.84	32.68	8.45	1.9
						7.93	19.6	6.80	90.0	0.94	32.71	8.45	2.4
							19.6	6.80	90.0	0.99	32.73	8.45	2.9
14:04	CC4	ME	845444	815595	2.37	1.19	19.6	6.86	90.7	0.65	32.64	8.45	<1.0
							19.6	6.85	90.6	0.64	32.64	8.45	1.6
14:37	CC13	ME	844200	817495	8.14	1.00	19.6	6.82	90.1	1.22	32.49	8.42	3.2
							19.6	6.82	90.1	1.26	32.48	8.42	3.2
						4.07	19.6	6.72	89.0	0.84	32.65	8.44	2.7
							19.6	6.72	89.0	0.83	32.65	8.44	2.2
						7.14	19.7	6.73	89.2	0.90	32.75	8.45	1.3
							19.7	6.73	89.2	0.91	32.76	8.45	<1.0
13:58	SW11	ME	845512	817442	3.73	1.00	19.6	6.41	84.8	1.94	32.62	8.52	4.2
							19.6	6.41	84.8	1.95	32.61	8.52	4
14:16	C3	ME	843821	816211	15.49	1.00	19.7	6.64	88.0	0.79	32.65	8.46	2.9
							19.7	6.64	87.9	0.78	32.65	8.46	2.1
						7.75	19.7	6.66	88.4	0.74	32.78	8.47	1.2
							19.7	6.66	88.4	0.74	32.78	8.47	1.5
						14.49	19.7	6.73	89.4	0.88	32.88	8.47	1.4
							19.7	6.73	89.4	0.86	32.88	8.47	<1.0
14:08	C4	ME	844621	815770	16.07	1.00	19.6	6.76	89.4	0.67	32.57	8.45	2.9
							19.6	6.74	89.2	0.69	32.57	8.45	3.4
						8.04	19.6	6.79	89.9	0.53	32.65	8.48	1.8
							19.6	6.79	89.9	0.52	32.65	8.48	1.3
						15.07	19.7	6.84	91.0	0.75	32.96	8.47	<1.0
							19.7	6.84	91.0	0.73	32.96	8.47	<1.0
14:44	II	ME	844602	817675	9.17	1.00	19.4	7.06	92.7	0.92	31.99	8.39	1.4
							19.4	7.04	92.5	0.92	32.01	8.39	1.8
						4.59	19.6	6.82	90.1	1.08	32.61	8.41	2
							19.6	6.81	90.0	1.08	32.63	8.41	1.2
						8.17	19.7	6.72	89.1	1.93	32.84	8.42	1.3
							19.7	6.69	88.7	1.97	32.84	8.42	2
17:11	CC1	MF	843201	816416	9.17	1.00	19.4	6.86	90.2	0.84	31.93	8.45	1.6
							19.4	6.85	90.0	0.83	31.93	8.45	1.7
						4.59	19.6	6.77	89.2	0.80	32.24	8.45	1
							19.6	6.75	89.1	0.81	32.32	8.45	1.4
						8.17	19.7	6.67	88.4	0.95	32.74	8.45	1.5
							19.7	6.66	88.4	0.99	32.76	8.45	1.8
17:23	CC2	MF	844076	817091	11.93	1.00	19.5	6.99	92.2	0.89	32.36	8.43	2.5
							19.5	6.97	92.0	0.88	32.38	8.43	2.4
						5.97	19.6	6.84	90.5	0.82	32.59	8.44	2.5
							19.6	6.83	90.4	0.81	32.60	8.44	2.4
						10.93	19.7	6.74	89.5	2.46	32.87	8.46	2.5
							19.7	6.74	89.5	2.44	32.87	8.46	2
17:43	CC3	MF	844606	817941	9.15	1.00	19.5	6.94	91.4	0.92	32.13	8.44	1.5
							19.5	6.93	91.2	0.91	32.14	8.44	1.9
						4.58	19.6	6.77	89.6	1.22	32.72	8.45	1.3
							19.6	6.76	89.5	1.23	32.72	8.46	1.3
						8.15	19.6	6.74	89.3	1.27	32.75	8.46	2.6
							19.6	6.74	89.3	1.29	32.76	8.46	3
16:52	CC4	MF	845444	815595	2.5	1.25	19.4	6.96	91.5	0.95	32.17	8.36	1.8
							19.4	6.93	91.2	0.95	32.19	8.36	1.1
17:28	CC13	MF	844200	817495	8.07	1.00	19.6	6.75	89.1	1.17	32.29	8.46	2.2
							19.6	6.75	89.0	1.17	32.30	8.46	1.8
						4.04	19.6	6.76	89.4	0.78	32.62	8.46	1.9
							19.6	6.76	89.4	0.77	32.62	8.46	2.1
						7.07	19.7	6.72	89.1	0.93	32.76	8.46	1.7
							19.7	6.72	89.1	0.89	32.76	8.46	1.5
16:40	SW11	MF	845512	817442	3.42	1.00	19.6	6.55	86.6	1.53	32.61	8.17	2.6
							19.6	6.55	86.7	1.52	32.62	8.18	2.2
17:05	C3	MF	843821	816211	15.93	2.42	19.6	6.67	88.2	1.41	32.69	8.26	1
							19.6	6.67	88.3	1.41	32.68	8.27	<1.0
						1.00	19.4	6.99	91.9	0.91	32.18	8.43	3.2
							19.4	6.97	91.6	0.70	32.19	8.43	3.2
						7.97	19.7	6.71	89.0	0.63	32.76	8.45	2.3
							19.7	6.71	88.9	0.63	32.76	8.45	2
16:57	C4	MF	844621	815770	16.06	1.00	19.7	6.68	88.7	1.17	32.83	8.45	1.8
							19.7	6.68	88.7	1.27	32.83	8.45	1.4
						1.00	19.6	6.56	86.7	0.79	32.43	8.39	1.9
							19.6	6.56	86.7	0.80	32.44	8.40	2
						8.03	19.7	6.59	87.4	0.68	32.65	8.42	1.5
							19.7	6.59	87.4	0.67	32.65	8.42	1.6
17:37	II	MF	844602	817675	9.83	1.00	19.7	6.63	87.9	0.80	32.73	8.43	1.6
							19.7	6.63	87.9	0.82	32.74	8.43	1.7
						4.92	19.4	6.88	90.6	0.87	32.06	8.46	3.8
							19.4	6.88	90.5	0.86	32.05	8.47	3.4
						8.83	19.6	6.82	90.2	0.93	32.68	8.47	4.5
							19.6	6.81	90.2	0.94	32.71	8.47	4.7

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 9-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
12:53	CC1	ME	843201	816416	8.25	1.00	19.6	6.94	92.0	0.98	32.89	8.44	1.1
							19.7	6.91	91.6	0.98	32.90	8.44	1.2
							19.7	6.71	89.1	1.02	32.94	8.45	1.3
						4.13	19.7	6.70	88.9	1.01	32.94	8.45	1.2
							19.7	6.65	88.4	1.11	32.99	8.46	1.2
							19.7	6.65	88.4	1.13	32.99	8.46	1.1
12:59	CC2	ME	844076	817091	12.28	1.00	19.4	6.72	88.6	0.86	32.66	8.45	1.6
							19.4	6.69	88.3	0.85	32.67	8.45	1.5
							19.6	6.60	87.5	0.88	32.86	8.45	1.2
						6.14	19.6	6.60	87.5	0.87	32.86	8.46	1.1
							19.7	6.66	88.5	1.34	33.02	8.46	<1.0
							19.7	6.67	88.6	1.34	33.02	8.46	<1.0
13:15	CC3	ME	844606	817941	9.85	1.00	19.4	6.69	88.1	0.89	32.11	8.43	1.1
							19.4	6.65	87.5	0.88	32.16	8.43	1.7
							19.6	6.53	86.3	0.93	32.64	8.43	2.3
						4.93	19.6	6.52	86.2	0.92	32.69	8.43	2.3
							19.7	6.49	86.1	0.95	32.88	8.43	2.4
							19.7	6.49	86.1	0.98	32.90	8.43	2.7
12:37	CC4	ME	845444	815595	2.5	1.25	19.7	6.79	90.2	1.50	33.04	8.45	2.6
							19.7	6.79	90.2	1.53	33.04	8.45	2.3
							19.6	6.74	89.2	2.01	32.75	8.45	5.6
13:05	CC13	ME	844200	817495	8.46	1.00	19.6	6.72	88.9	2.09	32.75	8.45	6.5
							19.6	6.59	87.2	2.35	32.76	8.45	4.7
							19.6	6.58	87.1	2.42	32.76	8.45	5.1
						4.23	19.6	6.49	85.9	2.28	32.77	8.46	3.8
							19.6	6.49	85.9	2.33	32.77	8.46	3.8
							19.4	6.47	85.4	0.94	32.61	8.45	2.1
12:31	SW11	ME	845512	817442	3.68	1.00	19.4	6.44	85.0	0.92	32.62	8.45	1.4
							19.4	6.45	85.1	0.91	32.66	8.45	1.2
							19.4	6.45	85.2	0.88	32.66	8.45	1.6
12:47	C3	ME	843821	816211	15.97	1.00	19.4	6.74	88.8	0.84	32.60	8.44	<1.0
							19.4	6.69	88.3	0.84	32.61	8.44	<1.0
							19.7	6.65	88.3	0.97	32.98	8.45	<1.0
						7.99	19.7	6.65	88.4	0.98	32.99	8.45	<1.0
							19.8	6.70	89.3	1.30	33.10	8.45	<1.0
							19.8	6.72	89.5	1.37	33.11	8.45	1.2
12:41	C4	ME	844621	815770	16.03	1.00	19.6	6.76	89.5	0.93	32.80	8.45	<1.0
							19.6	6.74	89.2	0.92	32.80	8.45	1
							19.7	6.63	88.1	0.93	32.92	8.46	<1.0
						8.02	19.7	6.63	88.0	0.94	32.92	8.46	<1.0
							19.9	6.70	89.5	1.35	33.25	8.46	<1.0
							20	6.70	89.7	1.37	33.29	8.46	<1.0
13:10	II	ME	844602	817675	10.05	1.00	19.4	6.51	85.6	2.19	32.54	8.45	1.8
							19.4	6.49	85.6	2.21	32.53	8.45	2.5
							19.6	6.42	85.0	1.23	32.80	8.45	3.2
						5.03	19.6	6.41	85.0	1.23	32.80	8.45	4
							19.7	6.55	87.0	1.43	32.94	8.45	4.6
							19.7	6.55	87.0	1.40	32.94	8.45	4.5
9:10	CC1	MF	843201	816416	9.06	1.00	19.4	6.64	87.4	0.87	32.50	8.47	1.1
							19.4	6.63	87.3	0.87	32.49	8.47	<1.0
							19.4	6.54	86.3	0.91	32.62	8.47	1.4
						4.53	19.4	6.54	86.3	0.89	32.62	8.47	1.1
							19.4	6.5	85.9	0.86	32.68	8.46	2
							19.4	6.5	85.9	0.86	32.68	8.46	1.3
9:20	CC2	MF	844076	817091	12.13	1.00	19.4	6.45	85.1	0.79	32.53	8.46	2.1
							19.4	6.45	85.0	0.79	32.52	8.46	1.3
							19.5	6.46	85.3	0.80	32.67	8.46	1.6
						6.07	19.5	6.46	85.4	0.80	32.68	8.46	1.1
							19.6	6.55	86.6	0.71	32.76	8.46	1.7
							19.6	6.55	86.6	0.72	32.76	8.46	1.3
9:36	CC3	MF	844606	817941	9.86	1.00	19.4	6.67	87.8	1.04	32.47	8.44	1.8
							19.5	6.64	87.6	1.04	32.42	8.44	1.2
							19.6	6.52	86.4	1.15	32.77	8.44	2
						4.93	19.6	6.52	86.4	1.10	32.77	8.44	2
							19.7	6.56	87.1	1.35	32.97	8.45	1.9
							19.7	6.56	87.1	1.33	32.97	8.45	1.7
8:50	CC4	MF	845444	815595	2.44	1.22	19.5	6.39	84.4	1.05	32.66	8.47	2.6
							19.5	6.38	84.3	1.02	32.66	8.47	2.7
							19.5	6.56	86.7	1.16	32.70	8.44	1.8
9:26	CC13	MF	844200	817495	8.03	1.00	19.5	6.55	86.6	1.19	32.70	8.44	1.4
							19.6	6.51	86.1	1.25	32.71	8.45	6.6
							19.6	6.51	86.0	1.23	32.71	8.45	7.1
						4.02	19.5	6.49	85.8	5.60	32.69	8.45	10.6
							19.5	6.49	85.8	5.73	32.69	8.45	10.9
							19.4	6.61	87.1	0.91	32.63	8.55	2.9
8:44	SW11	MF	845512	817442	3.41	1.00	19.4	6.58	86.8	0.92	32.63	8.55	2.2
							19.4	6.50	85.7	0.90	32.64	8.53	1.5
							19.4	6.49	85.6	0.90	32.64	8.53	1.5
9:05	C3	MF	843821	816211	16.11	1.00	19.6	6.62	87.5	0.86	32.76	8.47	2.1
							19.6	6.61	87.4	0.86	32.76	8.47	2.4
							19.8	6.77	90.1	1.34	33.12	8.47	1.2
						8.06	19.8	6.77	90.2	1.37	33.12	8.47	1.1
							19.8	6.78	90.3	1.42	33.13	8.47	1.7
							19.8	6.78	90.3	1.47	33.13	8.47	1
8:54	C4	MF	844621	815770	14.68	1.00	19.6	6.67	88.3	0.86	32.84	8.45	1.6
							19.6	6.66	88.2	0.85	32.83	8.45	1.3
							19.9	6.79	90.6	1.01	33.17	8.47	2.2
						7.34	19.9	6.79	90.6	1.02	33.17	8.47	2.2
							19.9	6.79	90.7	1.05	33.21	8.47	2.5
							19.9	6.79	90.7	1.06	33.21	8.47	2.2
9:32	II	MF	844602	817675	10.09	1.00	19.4	6.66	87.8	0.87	32.45	8.43	1.8
							19.4	6.64	87.6	0.86	32.46	8.43	1.7
							19.5	6.58	86.9	0.86	32.60	8.44	1.8
						5.05	19.5	6.57	86.8	0.85	32.63	8.44	1.9
							19.7	6.61	87.9	1.18	32.98	8.45	1.1
							19.7	6.61	87.8	1.17	32.98	8.45	1.2

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result

Sampling Date: 11-Mar-19																			
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L						
			East	North															
13:57	CC1	ME	843201	816416	9.03	1.00	19.8	6.47	86.2	0.41	32.94	8.37	4.8						
							19.8	6.43	85.6	0.41	32.95	8.37	4.6						
							19.9	6.25	83.5	0.56	33.10	8.4	3.4						
						4.52	19.9	6.25	83.4	0.56	33.11	8.41	3.2						
							19.9	6.21	82.9	0.72	33.15	8.42	2.8						
							19.9	6.20	82.9	0.73	33.16	8.42	2.7						
							19.8	6.46	86.0	0.22	32.85	8.4	3.1						
14:03	CC2	ME	844076	817091	12.1	1.00	19.9	6.45	85.9	0.22	32.85	8.4	3.6						
							19.9	6.33	84.4	0.23	32.95	8.42	2.9						
							19.9	6.32	84.3	0.25	32.97	8.42	2.7						
						6.05	19.9	6.27	83.7	0.47	33.09	8.42	3						
							19.9	6.27	83.7	0.51	33.10	8.42	3.4						
							19.9	6.47	86.1	0.39	32.68	8.40	3.9						
							19.9	6.44	85.7	0.38	32.68	8.40	3.1						
14:17	CC3	ME	844606	817941	9.25	4.63	19.8	6.29	83.6	0.32	32.83	8.42	2.7						
							19.8	6.28	83.6	0.31	32.83	8.42	2.1						
							19.9	6.14	81.8	0.52	33.03	8.42	2.2						
						8.25	19.9	6.13	81.7	0.52	33.03	8.42	2.3						
							19.9	6.47	86.1	0.39	32.68	8.40	3.9						
							19.9	6.44	85.7	0.38	32.68	8.40	3.1						
							19.8	6.29	83.6	0.32	32.83	8.42	2.7						
13:42	CC4	ME	845444	815595	2.47	1.24	19.9	6.43	85.9	0.67	33.04	8.42	1.6						
							19.9	6.42	85.7	0.66	33.05	8.43	2.3						
							19.9	6.25	83.4	0.56	33.10	8.4	3.4						
						14:08	CC13	ME	844200	817495	8.03	1.00	19.9	6.58	87.6	0.55	32.70	8.38	2.5
													19.9	6.53	87.0	0.43	32.72	8.38	2.4
													19.8	6.27	83.4	1.39	32.96	8.41	3
												4.02	19.8	6.26	83.3	1.47	32.97	8.41	3.8
19.9	6.21	82.8	1.22	33.07	8.42								5.5						
19.9	6.21	82.8	1.22	33.08	8.42								4.5						
19.8	6.23	82.9	0.32	32.81	8.52								1.8						
13:36	SW11	ME	845512	817442	3.45	1.00	19.8	6.22	82.8	0.32	32.81	8.52	2.3						
							19.8	6.18	82.2	0.31	32.81	8.52	2.7						
							19.8	6.17	82.0	0.30	32.81	8.52	3.1						
						2.45	19.8	6.23	82.8	0.44	32.65	8.37	2.4						
							19.8	6.21	82.5	0.44	32.65	8.38	2.3						
							19.8	6.13	81.5	0.37	32.76	8.40	1.6						
							19.8	6.13	81.5	0.38	32.78	8.40	2.3						
13:52	C3	ME	843821	816211	16.13	1.00	19.9	6.13	81.8	0.38	32.99	8.42	1.4						
							19.9	6.14	81.9	0.46	33.03	8.42	<1.0						
							19.9	6.33	84.4	0.31	32.88	8.42	5						
						8.07	19.9	6.32	84.3	0.31	32.88	8.42	5.9						
							19.8	6.34	84.5	0.25	33.08	8.44	2.7						
							19.8	6.35	84.6	0.25	33.09	8.44	3.2						
							20.1	6.40	85.9	0.62	33.41	8.45	2.7						
13:46	C4	ME	844621	815770	16.19	1.00	19.9	6.40	85.9	0.65	33.41	8.45	2.6						
							19.9	6.50	86.6	0.28	32.68	8.39	2.3						
							19.9	6.47	86.2	0.28	32.68	8.40	2.6						
						8.10	19.8	6.25	83.3	0.61	32.95	8.42	1.8						
							19.8	6.25	83.2	0.65	32.95	8.42	2						
							19.9	6.10	81.5	1.18	33.14	8.43	2.8						
							19.9	6.09	81.4	1.24	33.14	8.43	2.1						
10:20	CC1	MF	843201	816416	8.91	1.00	19.6	6.65	88.0	0.31	32.75	8.42	2.5						
							19.6	6.6	87.4	0.31	32.75	8.42	3.1						
							19.7	6.28	83.4	0.30	32.90	8.45	3.2						
						4.46	19.7	6.28	83.3	0.31	32.89	8.45	3						
							19.7	6.22	82.6	0.34	32.91	8.45	2.6						
							19.4	6.5	83.9	0.86	32.68	8.46	2.1						
							19.6	6.45	85.3	0.29	32.76	8.42	2.8						
10:26	CC2	MF	844076	817091	12.2	1.00	19.6	6.44	85.2	0.28	32.76	8.43	2.2						
							19.6	6.32	83.8	0.24	32.82	8.45	2.4						
							19.6	6.32	83.7	0.23	32.82	8.45	1.6						
						6.10	19.8	6.3	83.8	0.27	33.00	8.45	2.6						
							19.8	6.3	83.8	0.25	33.00	8.45	3.1						
							19.7	6.42	85.2	0.82	32.75	8.41	3.9						
							19.7	6.39	84.9	0.84	32.78	8.41	3.4						
10:38	CC3	MF	844606	817941	9.46	1.00	19.8	6.20	82.6	0.91	33.05	8.42	3.8						
							19.8	6.19	82.5	0.94	33.05	8.42	3.4						
							19.9	6.13	81.8	1.27	33.15	8.43	3.3						
						4.73	19.9	6.11	81.6	1.34	33.15	8.43	4.1						
							19.6	6.16	81.5	0.51	32.58	8.45	5.4						
							19.6	6.14	81.2	0.52	32.60	8.45	4.8						
							19.6	6.64	87.8	0.51	32.64	8.41	2.8						
10:02	CC4	MF	845444	815595	2.47	1.00	19.6	6.51	86.1	0.50	32.66	8.42	3.6						
							19.8	6.22	82.8	0.94	32.98	8.43	2						
							19.8	6.21	82.6	0.89	32.97	8.43	2.1						
						4.04	19.8	6.19	82.3	0.94	32.98	8.44	2.9						
							19.8	6.18	82.3	0.97	33.00	8.44	3.4						
							19.6	6.21	82.1	0.91	32.73	8.62	2.2						
							19.6	6.20	82.1	0.89	32.73	8.62	2.7						
9:55	SW11	MF	845512	817442	3.46	1.00	19.6	6.20	82.1	0.72	32.77	8.58	4.8						
							19.6	6.20	82.1	0.74	32.77	8.58	4.3						
							19.7	6.30	83.6	0.45	32.86	8.41	2.7						
						2.46	19.7	6.28	83.4	0.44	32.86	8.42	1.9						
							19.8	6.23	83.0	0.45	32.99	8.44	3						
							19.8	6.24	83.1	0.48	33.04	8.44	2.4						
							20	6.32	84.6	0.84	33.27	8.46	2.8						
10:14	C3	MF	843821	816211	15.27	1.00	20	6.32	84.6	0.82	33.27	8.46	2.2						
							19.7	6.29	83.4	0.51	32.79	8.42	2.9						
							19.7	6.27	83.1	0.48	32.79	8.42	2.3						
						7.64	19.9	6.30	84.0	0.72	33.17	8.45	2.8						
							19.9	6.33	84.6	0.74	33.21	8.45	2.4						
							19.9	6.49	86.9	0.76	33.30	8.47	4.4						
							19.9	6.49	86.9	0.75	33.30	8.47	4.1						
10:07	C4	MF	844621	815770	16.04	1.00	19.7	6.45	85.6	0.73	32.75	8.41	3						
							19.7	6.42	85.3	0.74	32.74	8.41	2.7						
							19.8	6.33	84.1	0.58	32.89	8.43	3.2						
						5.01	19.8	6.33	84.1	0.56	32.90	8.43	3						
							19.9	6.28	83.9	1.07	33.17	8.44	3.1						
							19.9	6.28	83.8	1.08	33.17	8.44	3.4						
							19.9	6.28	83.8	1.08	33.17	8.44	3.4						
10:35	II	MF	844602	817675	10.01	1.00	19.7	6.45	85.6	0.73	32.75	8.41	3						
							19.7	6.42	85.3	0.74	32.74	8.41	2.7						
							19.8	6.33	84.1	0.58	32.89	8.43	3.2						
						9.01	19.8	6.33	84.1	0.56	32.90	8.43	3						
							19.9	6.28	83.9	1.07	33.17	8.44	3.1						
							19.9	6.28	83.8	1.08	33.17	8.44	3.4						
							19.9	6.28	83.8	1.08	33.17	8.44	3.4						

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 13-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
15:39	CC1	ME	843201	816416	9.1	1.00	20.2	6.72	90.2	0.28	32.95	8.43	2.4
							20.2	6.68	89.7	0.28	32.95	8.43	2.9
						4.55	20.2	6.38	85.5	0.38	33.02	8.44	3.3
							20.2	6.37	85.5	0.39	33.02	8.44	3.7
							20.2	6.29	84.4	0.48	33.10	8.44	3.6
15:43	CC2	ME	844076	817091	11.91	1.00	20.2	6.73	90.2	0.22	32.91	8.4	5.4
							20.2	6.70	89.8	0.21	32.91	8.4	6
							20.2	6.47	86.8	0.18	32.97	8.44	4.4
						5.96	20.2	6.47	86.8	0.18	32.97	8.44	4.6
							20.2	6.30	84.6	0.60	33.20	8.45	6.1
15:59	CC3	ME	844606	817941	9.16	1.00	20.2	6.34	85.2	0.79	33.28	8.45	6
							20.3	6.74	90.4	0.36	32.87	8.43	6.1
							20.3	6.71	90.1	0.33	32.87	8.43	6.3
						4.58	20.3	6.62	88.8	0.43	32.87	8.43	5.3
							20.3	6.59	88.4	0.45	32.87	8.44	5.8
15:24	CC4	ME	845444	815595	2.41	1.21	20.2	6.26	83.9	0.46	33.00	8.53	6.5
							20.2	6.25	83.8	0.45	33.00	8.53	6.2
						1.00	20.2	6.69	89.6	0.63	32.94	8.42	3.2
							20.2	6.48	86.9	0.57	32.91	8.43	3
						4.23	20.2	6.48	86.9	0.23	33.02	8.45	4.1
15:48	CC13	ME	844200	817495	8.45		20.2	6.48	86.9	0.23	33.02	8.45	4.6
							20.2	6.45	86.6	0.31	33.10	8.45	5.3
						7.45	20.2	6.45	86.6	0.31	33.10	8.45	4.5
							20.2	6.52	87.3	0.49	32.85	8.59	6.3
							20.2	6.51	87.2	0.47	32.85	8.59	6.9
15:20	SW11	ME	845512	817442	3.44	2.44	20.2	6.22	83.2	0.47	32.86	8.61	5.1
							20.2	6.22	83.2	0.49	32.86	8.60	5.2
							20.2	6.39	85.6	0.34	32.91	8.40	3.9
						1.00	20.2	6.36	85.2	0.33	32.91	8.41	4.2
							20.2	6.14	82.2	0.29	32.96	8.44	4.5
15:34	C3	ME	843821	816211	16.1	8.05	20.2	6.12	82.0	0.28	32.96	8.44	4.4
							20.2	6.31	84.6	0.41	33.17	8.45	4.6
							20.2	6.31	84.6	0.41	33.17	8.45	4.8
						1.00	20.2	6.36	85.3	0.36	32.87	8.48	3.2
							20.2	6.35	85.1	0.36	32.87	8.48	3.9
15:28	C4	ME	844621	815770	16.02	8.01	20.2	6.30	84.4	0.48	32.94	8.47	3.8
							20.2	6.29	84.2	0.47	32.93	8.47	3.2
							20.2	6.47	86.8	0.68	33.08	8.47	2.7
						15.02	20.2	6.47	86.8	0.64	33.07	8.47	3.1
							20.3	6.72	90.2	0.36	32.86	8.42	4.8
15:54	II	ME	844602	817675	10.03	1.00	20.3	6.69	89.8	0.36	32.87	8.42	5.2
							20.2	6.56	87.9	0.69	32.89	8.42	5
						5.02	20.2	6.29	84.3	0.81	32.89	8.43	4.3
							20.2	6.37	85.6	1.55	33.29	8.44	4.6
						9.03	20.2	6.37	85.6	1.46	33.29	8.44	4.3
11:19	CC1	MF	843201	816416	9.25	1.00	20.1	6.33	84.7	0.55	32.93	8.42	4.7
							20.1	6.32	84.5	0.55	32.93	8.42	4.3
							20.1	6.24	83.5	0.53	32.94	8.42	5
						4.63	20.1	6.23	83.5	0.53	32.95	8.42	5.1
							20.1	6.19	82.9	0.57	32.99	8.43	5
11:25	CC2	MF	844076	817091	12.3	8.25	20.1	6.19	82.9	0.56	32.99	8.43	5
							20.1	6.6	88.2	0.44	32.81	8.37	3.7
							20.1	6.56	87.6	0.44	32.81	8.37	3.6
						1.00	20.1	6.31	84.3	0.50	32.89	8.42	3.6
							20.1	6.29	84.0	0.52	32.90	8.42	3.1
11:41	CC3	MF	844606	817941	9.19	6.15	20.1	6.2	83.0	0.70	32.98	8.43	3
							20.1	6.2	83.0	0.72	32.98	8.43	3.3
							20.2	6.66	89.3	0.66	32.76	8.39	4.8
						1.00	20.2	6.64	89.0	0.66	32.76	8.39	4.5
							20.2	6.42	86.1	0.60	32.92	8.41	3.7
11:02	CC4	MF	845444	815595	2.48	4.60	20.2	6.41	85.9	0.61	32.93	8.41	3.4
							20.2	6.34	84.9	0.84	32.97	8.42	3.7
							20.1	6.32	84.6	0.91	32.99	8.42	3.9
						1.24	20.1	6.03	80.6	0.32	32.75	8.42	5.8
							20.1	6.02	80.4	0.32	32.76	8.42	5.3
11:32	CC13	MF	844200	817495	8.25	1.00	20.2	6.44	86.2	0.46	32.83	8.40	6.2
							20.2	6.44	86.1	0.47	32.83	8.40	5.8
						4.13	20.1	6.40	85.6	0.39	32.84	8.42	4.4
							20.1	6.36	85.0	0.35	32.85	8.42	4.6
							20.1	6.30	84.2	0.35	32.88	8.43	3.4
10:56	SW11	MF	845512	817442	3.44	7.25	20.1	6.26	83.7	0.32	32.90	8.43	3.8
							20.1	6.15	82.3	0.40	32.87	8.59	4.8
							20.1	6.15	82.2	0.43	32.88	8.59	5.1
						2.44	20.1	6.10	81.6	0.50	32.90	8.56	6
							20.1	6.10	81.5	0.49	32.90	8.56	5.9
11:13	C3	MF	843821	816211	15.97	1.00	20.1	6.20	83.1	0.69	32.95	8.42	8.3
							20.1	6.19	82.9	0.69	32.95	8.43	8.5
						7.99	20.2	6.55	88.0	0.83	33.29	8.45	6.5
							20.2	6.56	88.1	0.81	33.29	8.45	6
							20.2	6.45	86.7	1.14	33.38	8.45	6.8
11:07	C4	MF	844621	815770	12.39	14.97	20.2	6.44	86.6	1.15	33.38	8.45	7.4
							20.2	5.97	79.8	0.61	32.79	8.41	7.7
							20.2	5.96	79.7	0.61	32.79	8.42	7.5
						1.00	20.1	6.36	85.1	0.58	32.96	8.43	6.9
							20.1	6.37	85.3	0.59	32.97	8.43	6.7
11:37	II	MF	844602	817675	10.12	6.20	20.2	6.56	88.2	1.02	33.38	8.44	7.7
							20.2	6.56	88.2	1.01	33.38	8.44	7.9
							20.2	6.66	89.3	0.43	32.79	8.37	5.2
						1.00	20.2	6.62	88.7	0.42	32.79	8.38	5.9
							20.2	6.43	86.1	0.53	32.89	8.41	6.7
11:19	CC1	MF	843201	816416	9.25	5.06	20.2	6.42	85.9	0.54	32.90	8.41	7.2
							20.1	6.36	85.1	0.87	32.96	8.42	7.4
							20.1	6.34	84.8	0.97	32.98	8.42	7.5
						9.12	20.1	6.34	84.8	0.97	32.98	8.42	7.5
							20.1	6.34	84.8	0.97	32.98	8.42	7.5

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide

Impact Water Quality Monitoring Result													
Sampling Date: 15-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
17:00	CC1	ME	843201	816416	8.2	1.00	20.1	6.79	91.0	0.79	33.22	8.43	1.5
							20.1	6.76	90.7	0.80	33.22	8.44	1.2
						4.10	20.2	6.61	88.8	0.84	33.30	8.45	1.7
							20.2	6.59	88.6	0.86	33.32	8.45	1.7
							20.3	6.47	87.2	0.97	33.42	8.47	4
							20.3	6.47	87.1	0.97	33.42	8.47	4.3
17:07	CC2	ME	844076	817091	12.16	1.00	20.1	6.92	92.8	0.65	33.28	8.42	2.2
							20.2	6.89	92.4	0.65	33.28	8.43	1.5
						6.08	20.2	6.72	90.4	0.58	33.36	8.45	2.1
							20.2	6.71	90.2	0.55	33.38	8.45	1.8
						11.16	20.5	6.35	86.0	1.05	33.66	8.49	3.4
							20.5	6.35	85.9	1.09	33.66	8.49	3
17:21	CC3	ME	844606	817941	9.56	1.00	20.2	6.32	84.8	1.09	33.15	8.46	2.2
							20.2	6.32	84.9	1.07	33.14	8.46	1.7
						4.78	20.3	6.32	85.1	1.58	33.35	8.46	2.5
							20.3	6.32	85.1	1.67	33.39	8.46	3.1
						8.56	20.4	6.25	84.5	2.30	33.61	8.46	4.1
							20.4	6.24	84.3	2.35	33.61	8.46	4.4
16:44	CC4	ME	845444	815595	2.41	1.21	20.2	6.64	89.2	0.79	33.29	8.53	2
							20.2	6.64	89.2	0.79	33.28	8.53	2.9
17:12	CC13	ME	844200	817495	8.46	1.00	20.2	6.48	87.1	1.36	33.33	8.48	2.8
							20.2	6.48	87.1	1.37	33.33	8.48	2.5
						4.23	20.3	6.52	87.8	0.80	33.41	8.49	3.1
							20.3	6.52	87.8	0.81	33.41	8.49	3.5
						7.46	20.3	6.52	87.8	0.78	33.45	8.49	3
							20.3	6.52	87.8	0.81	33.47	8.49	4.4
16:37	SW11	ME	845512	817442	3.37	1.00	20.3	6.49	87.5	1.30	33.45	8.56	2.7
							20.3	6.49	87.4	1.33	33.46	8.56	2.6
16:56	C3	ME	843821	816211	15.93	1.00	20.2	6.63	88.9	0.59	33.23	8.50	1.3
							20.2	6.62	88.8	0.59	33.22	8.50	2.1
						7.97	20.2	6.61	88.8	0.50	33.29	8.49	1.4
							20.2	6.61	88.8	0.51	33.29	8.49	1.4
						14.93	20.4	6.56	88.7	0.96	33.67	8.49	<1.0
							20.6	6.50	88.2	1.17	33.82	8.48	1.6
16:47	C4	ME	844621	815770	16.09	1.00	20.1	6.99	93.6	0.64	33.18	8.48	1.2
							20.1	6.98	93.4	0.65	33.18	8.48	1.2
						8.05	20.2	6.78	91.1	0.69	33.37	8.49	1.8
							20.2	6.77	91.0	0.67	33.37	8.49	1.7
						15.09	20.6	6.55	88.8	1.23	33.81	8.49	1.9
							20.6	6.54	88.7	1.25	33.83	8.49	1.9
17:18	II	ME	844602	817675	10.15	1.00	20.2	6.56	88.0	0.83	33.10	8.48	2.5
							20.2	6.55	87.9	0.83	33.12	8.48	1.7
						5.08	20.2	6.53	87.7	0.86	33.14	8.48	2
							20.2	6.52	87.6	0.86	33.16	8.49	2.1
						9.15	20.3	6.44	86.8	1.58	33.47	8.49	2.2
							20.4	6.42	86.6	1.71	33.53	8.49	1.5
12:38	CC1	MF	843201	816416	8.8	1.00	20.2	6.45	86.5	0.60	33.19	8.48	3.2
							20.1	6.45	86.5	0.59	33.19	8.48	2.3
						4.40	20.2	6.44	86.6	0.97	33.32	8.48	2.5
							20.2	6.44	86.6	0.98	33.32	8.48	2.3
						7.80	20.3	6.33	85.3	1.28	33.45	8.47	3.2
							20.3	6.33	85.3	1.29	33.45	8.47	2.9
12:44	CC2	MF	844076	817091	12.11	1.00	20.1	6.55	87.7	1.28	33.14	8.47	3
							20.1	6.55	87.7	1.27	33.13	8.47	3.3
						6.06	20.2	6.52	87.7	1.12	33.38	8.48	3.9
							20.3	6.51	87.6	1.18	33.40	8.48	3.1
						11.11	20.6	6.32	85.6	1.62	33.74	8.47	2.2
							20.6	6.31	85.5	1.61	33.74	8.47	1.9
13:00	CC3	MF	844606	817941	9.48	1.00	20.2	6.80	91.2	0.50	33.04	8.43	2.6
							20.2	6.77	90.8	0.52	33.05	8.44	2.8
						4.74	20.2	6.56	88.1	0.67	33.16	8.44	1.1
							20.2	6.46	86.7	0.76	33.21	8.45	1.1
						8.48	20.2	6.05	81.4	1.95	33.27	8.46	1.8
							20.2	6.04	81.2	1.91	33.27	8.46	1.4
12:20	CC4	MF	845444	815595	2.43	1.22	20	6.94	92.8	0.99	33.17	8.46	1.7
							20	6.91	92.4	1.00	33.17	8.47	2.2
12:49	CC13	MF	844200	817495	8.09	1.00	20.1	6.75	90.4	1.02	33.10	8.40	2.6
							20.1	6.72	89.9	1.02	33.10	8.41	1.9
						4.05	20.1	6.49	87.0	0.87	33.16	8.43	2.8
							20.2	6.40	85.8	0.84	33.17	8.44	2.5
						7.09	20.2	6.35	85.1	1.39	33.19	8.45	4.1
							20.2	6.34	85.0	1.39	33.19	8.46	4.1
12:14	SW11	MF	845512	817442	3.54	1.00	20.2	6.11	82.2	1.62	33.23	8.55	3.5
							20.2	6.12	82.2	1.63	33.23	8.55	4.4
						2.54	20.2	6.08	81.7	2.08	33.24	8.54	5.3
							20.2	6.07	81.5	2.10	33.24	8.54	5.3
							20.2	6.64	89.1	0.45	33.24	8.47	1.9
							20.2	6.63	89.0	0.44	33.24	8.47	1.4
12:32	C3	MF	843821	816211	15.84	1.00	20.2	6.59	88.5	0.54	33.37	8.48	2.1
							20.2	6.58	88.5	0.55	33.39	8.48	2
						7.92	20.7	6.36	86.6	1.61	33.89	8.48	1.8
							20.7	6.36	86.5	1.59	33.89	8.48	1.5
						14.84	20.2	6.77	91.0	0.87	33.36	8.49	2.1
							20.2	6.77	90.9	0.88	33.36	8.49	2.3
12:26	C4	MF	844621	815770	16.17	8.09	20.3	6.71	90.3	0.49	33.47	8.48	2.3
							20.3	6.70	90.2	0.51	33.47	8.48	1.9
						15.17	20.7	6.51	88.7	1.49	33.96	8.47	3.6
							20.8	6.49	88.4	1.62	33.96	8.47	4
							20.1	6.83	91.4	0.54	33.01	8.43	1.5
							20.1	6.81	91.2	0.55	33.02	8.44	1.7
12:56	II	MF	844602	817675	10.28	5.14	20.2	6.63	88.9	0.65	33.11	8.45	2.3
							20.2	6.59	88.4	0.66	33.13	8.45	2.3
							20.2	6.54	87.9	1.87	33.30	8.48	2.9
						9.28	20.2	6.56	88.2	1.79	33.31	8.49	3.2

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 18-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
11:41	CC1	ME	843201	816416	8.01	1.00	19.4	7.30	97.7	1.53	35.22	8.17	3.8
							19.6	7.27	97.5	1.71	35.11	8.17	3.7
						4.01	19.6	6.78	91.1	0.46	35.10	8.14	2.8
							19.6	6.78	91.1	0.45	35.09	8.14	2.8
							19.6	6.71	90.2	0.68	35.10	8.14	3.4
11:47	CC2	ME	844076	817091	9.2	1.00	20.3	6.47	87.1	0.97	33.42	8.47	3.8
							19.7	6.81	91.7	0.56	35.11	8.13	4
							19.7	6.81	91.6	0.55	35.11	8.13	3.8
						4.60	19.7	6.74	90.7	0.87	35.12	8.13	3
							19.7	6.72	90.4	0.87	35.12	8.13	2.3
12:01	CC3	ME	844606	817941	7.52	1.00	19.7	6.63	89.2	1.02	35.13	8.13	4.2
							19.7	6.63	89.1	1.03	35.13	8.13	4.5
							19.6	6.91	92.6	0.69	35.04	8.12	3.2
							19.8	6.80	91.6	0.55	34.87	8.12	2.8
						3.76	19.8	6.71	90.5	0.47	35.03	8.12	3.1
11:26	CC4	ME	845444	815595	2.53	1.00	19.8	6.71	90.4	0.48	35.05	8.12	2.5
							19.8	6.72	90.5	0.51	35.16	8.12	2.3
							19.8	6.72	90.6	0.53	35.18	8.12	2.2
						1.27	19.7	6.58	88.6	0.63	35.14	8.11	2.3
							19.7	6.58	88.6	0.61	35.15	8.11	2.6
11:52	CC13	ME	844200	817495	8.39	1.00	19.7	6.73	90.5	1.62	35.15	8.12	8.6
							19.7	6.70	90.2	1.68	35.12	8.12	8.8
						4.20	19.7	6.60	88.9	1.09	35.11	8.12	8
							19.7	6.57	88.5	1.14	35.12	8.12	8.8
							19.7	6.53	88.0	1.15	35.12	8.12	5.5
11:19	SW11	ME	845512	817442	4.08	1.00	19.7	6.53	87.9	1.26	35.12	8.12	5.7
							19.8	6.36	85.7	0.36	35.13	8.09	3.7
							19.8	6.36	85.7	0.36	35.13	8.09	4.6
						3.08	19.8	6.38	86.0	0.52	35.15	8.11	2.8
							19.8	6.38	85.9	0.53	35.15	8.11	2.3
11:35	C3	ME	843821	816211	14.24	1.00	19.6	7.15	96.0	0.55	35.12	8.15	3.7
							19.6	7.08	95.1	0.44	35.09	8.15	3.9
						7.12	19.6	6.81	91.5	0.40	35.10	8.14	2.2
							19.6	6.81	91.4	0.44	35.10	8.14	2.3
							19.6	6.67	89.7	0.53	35.10	8.13	2.6
11:30	C4	ME	844621	815770	17.6	1.00	19.6	6.68	89.7	0.52	35.10	8.13	2.8
							19.5	7.52	100.8	0.41	35.04	8.17	2.8
							19.5	7.51	100.7	0.40	35.04	8.17	2.1
						8.80	19.5	7.31	98.0	0.39	35.08	8.17	2.1
							19.6	7.27	97.5	0.38	35.09	8.17	1.7
11:56	II	ME	844602	817675	8.07	1.00	19.6	7.04	94.5	1.75	35.10	8.16	2.1
							19.6	7.03	94.3	2.05	35.10	8.15	1.4
							19.8	6.84	92.0	0.63	34.80	8.12	3.8
						4.04	19.8	6.80	91.6	0.63	34.82	8.12	3.6
							19.8	6.63	89.3	0.52	35.01	8.12	3.9
14:19	CC1	MF	843201	816416	8.14	1.00	19.8	6.60	88.9	0.50	35.04	8.12	3.9
							19.8	6.54	88.1	0.64	35.12	8.11	3.9
							19.8	6.62	89.2	0.49	35.20	8.12	4.8
						4.07	19.7	7.18	96.7	1.14	35.18	8.14	2.7
							19.8	7.09	95.6	1.17	35.12	8.14	3.3
14:25	CC2	MF	844076	817091	9.11	1.00	19.8	6.88	92.7	0.44	35.09	8.14	3.4
							19.8	6.82	91.8	0.49	35.10	8.14	3.5
							19.7	6.81	91.8	0.48	35.10	8.14	3.8
						4.56	19.7	6.91	92.9	1.12	35.21	8.15	3.8
							19.8	6.85	92.3	1.35	35.10	8.15	3.6
14:37	CC3	MF	844606	817941	8.11	1.00	19.8	6.81	91.8	0.37	35.10	8.15	3.5
							19.7	6.81	91.7	0.35	35.10	8.15	4.1
							19.7	6.9	92.7	0.38	35.10	8.15	4
							19.7	6.91	92.9	0.35	35.10	8.15	3.3
						4.06	19.9	6.88	92.8	0.67	35.07	8.14	<1.0
14:07	CC4	MF	845444	815595	2.43	1.00	19.9	6.86	92.6	0.51	35.01	8.14	1.6
							19.8	6.79	91.6	0.56	35.14	8.14	2
							19.8	6.79	91.5	0.53	35.14	8.14	2.8
							19.8	6.74	90.9	0.74	35.19	8.14	3.4
						1.22	19.8	6.74	90.9	0.66	35.18	8.14	4
14:30	CC13	MF	844200	817495	9.19	1.00	19.8	6.84	92.1	0.44	35.14	8.16	2
							19.7	6.82	91.8	1.56	35.12	8.15	5
							19.7	6.80	91.5	1.51	35.11	8.15	4.9
						4.60	19.7	6.70	90.2	2.71	35.12	8.14	4.2
							19.7	6.69	90.1	2.90	35.12	8.14	4.3
14:00	SW11	MF	845512	817442	4.06	1.00	19.7	6.67	89.9	2.57	35.11	8.14	3.7
							19.7	6.67	89.8	2.46	35.11	8.14	3
							20.1	6.67	90.3	0.44	35.00	8.18	2
							19.9	6.66	90.0	0.48	35.09	8.18	1.5
						3.06	19.8	6.55	88.4	0.61	35.13	8.16	2.4
14:15	C3	MF	843821	816211	17.07	1.00	19.8	6.53	88.1	0.64	35.14	8.16	2
							19.7	6.84	92.1	0.34	35.20	8.16	2.3
							19.7	6.80	91.5	0.36	35.18	8.15	2.2
						8.54	19.7	6.56	88.3	0.47	35.10	8.14	2.4
							19.7	6.53	87.9	0.46	35.11	8.14	3.2
14:11	C4	MF	844621	815770	17.22	1.00	19.7	5.99	80.6	1.67	35.10	8.13	3.6
							19.7	6.03	81.2	1.68	35.06	8.13	2.9
							19.4	7.42	99.4	0.44	35.22	8.20	3.7
							19.6	7.44	99.9	0.44	35.15	8.20	4.1
						8.61	19.7	7.08	95.2	0.67	35.08	8.19	4.7
14:34	II	MF	844602	817675	9.06	1.00	19.7	7.07	95.0	0.66	35.09	8.18	4.3
							19.7	6.82	91.7	0.67	35.10	8.16	4.2
							19.6	6.74	90.5	0.68	35.10	8.16	4.7
							19.8	7.00	94.4	1.09	35.00	8.15	2.6
						4.53	19.9	6.96	94.0	1.06	34.91	8.15	2
14:07	CC1	MF	843201	816416	8.14	1.00	19.8	6.60	88.9	1.15	35.12	8.14	1.9
							19.8	6.57	88.5	1.18	35.13	8.14	1.8
							19.8	6.54	88.2	0.90	35.17	8.13	2.2
						8.06	19.8	6.56	88.4	0.78	35.18	8.13	2.5
							19.8	6.56	88.4	0.78	35.18	8.13	2.5

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 20-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
16:28	CC1	ME	843201	816416	8.05	1.00	19.6	6.96	84.3	1.51	35.48	8.09	3.6
							19.7	6.87	84.3	1.51	35.42	8.09	3.4
							19.6	6.68	84.4	1.38	35.39	8.09	4
						4.03	19.6	6.66	84.4	1.40	35.39	8.09	4.5
							19.6	6.60	84.4	1.45	35.40	8.09	3.2
							19.6	6.59	83.9	1.40	35.40	8.09	3.8
							19.5	6.69	83.9	1.31	35.51	8.1	4.3
16:33	CC2	ME	844076	817091	9.03	1.00	19.6	6.63	83.9	1.31	35.40	8.1	4.9
							19.6	6.59	85.7	1.33	35.40	8.1	4.5
							19.6	6.59	85.7	1.31	35.40	8.1	3.9
						4.52	19.5	6.68	85.7	1.34	35.40	8.1	5.4
							19.5	6.69	85.7	1.31	35.40	8.1	6.3
							19.7	6.66	90.2	0.98	35.37	8.09	5.6
							19.8	6.64	90.2	0.95	35.31	8.09	6
16:43	CC3	ME	844606	817941	8.03	4.02	19.7	6.57	90.2	1.52	35.44	8.09	5.3
							19.7	6.57	89.9	1.49	35.44	8.09	5.3
							19.6	6.52	89.3	1.70	35.49	8.09	5.7
						7.03	19.6	6.52	89.3	1.62	35.48	8.09	6.4
							19.7	6.66	90.2	0.98	35.37	8.09	5.6
							19.8	6.64	90.2	0.95	35.31	8.09	6
							19.7	6.57	89.9	1.49	35.44	8.09	5.3
16:14	CC4	ME	845444	815595	2.34	1.17	19.7	6.62	90.7	1.42	35.41	8.10	5.4
							19.6	6.57	89.9	1.44	35.42	8.09	4.6
							19.6	6.60	85.7	1.52	35.42	8.10	7.8
						4.56	19.6	6.58	89.9	1.47	35.41	8.10	7.7
							19.6	6.48	88.6	1.34	35.42	8.09	6.2
							19.6	6.47	88.5	1.34	35.42	8.09	7.1
							19.6	6.45	88.3	1.19	35.41	8.09	5.2
16:35	CC13	ME	844200	817495	9.11	8.11	19.6	6.45	88.2	1.19	35.41	8.09	5.5
							19.9	6.45	88.7	1.01	35.37	8.13	4.9
							19.7	6.44	88.4	1.14	35.39	8.13	5.3
						1.00	19.7	6.33	86.8	1.27	35.43	8.11	6.3
							19.7	6.31	86.5	1.30	35.44	8.11	6.7
							19.5	6.62	90.5	1.30	35.50	8.11	5.8
							19.6	6.58	89.9	1.32	35.48	8.10	5.2
16:08	SW11	ME	845512	817442	3.97	1.00	19.5	6.34	86.7	1.43	35.40	8.09	6.1
							19.5	6.31	86.3	1.42	35.41	8.09	5.9
							19.5	5.77	86.3	1.45	35.40	8.08	6.3
						2.97	19.6	5.81	86.3	1.42	35.36	8.08	6.4
							19.3	6.54	97.8	1.30	35.52	8.15	4.9
							19.4	6.54	98.3	1.30	35.45	8.15	4.9
							19.5	6.54	93.6	1.13	35.38	8.14	5.8
16:24	C3	ME	843821	816211	16.98	8.49	19.5	6.54	93.4	1.12	35.39	8.13	5.3
							19.5	6.54	90.1	1.19	35.40	8.11	4.8
							19.4	6.52	88.9	1.34	35.40	8.11	5.2
						15.98	19.7	6.74	92.4	1.16	35.30	8.10	5.3
							19.8	6.74	92.4	1.16	35.21	8.10	6
							19.6	6.38	87.3	1.11	35.42	8.09	6.6
							19.6	6.35	86.9	1.14	35.43	8.09	6.3
16:19	C4	ME	844621	815770	17.13	1.00	19.6	6.32	86.6	0.86	35.47	8.08	5.4
							19.6	6.34	86.8	0.74	35.48	8.08	5.4
							20.4	6.46	84.7	0.72	35.06	8.04	5.7
						4.14	20.4	6.45	84.6	0.72	35.06	8.04	5.7
							20.3	6.27	85.1	1.57	35.15	8.04	7.6
							20.3	6.26	85.3	1.57	35.15	8.04	7.8
							20.3	6.26	85.3	1.66	35.19	8.04	8.1
13:14	CC1	MF	843201	816416	8.27	7.27	20.3	6.27	85.1	1.65	35.19	8.04	7.6
							20.4	6.45	84.6	1.61	35.05	8.01	7.9
							20.4	6.43	84.4	1.60	35.05	8.01	8
						1.00	20.4	6.26	82.1	1.55	35.11	8.02	7.1
							20.4	6.27	82.1	1.61	35.12	8.02	7.1
							20.3	6.42	84.4	1.79	35.46	8.03	6.9
							20.3	6.44	84.6	1.88	35.48	8.03	6.7
13:32	CC3	MF	844606	817941	9.47	1.00	20.7	6.34	88.1	1.36	34.88	8.09	3.1
							20.6	6.31	87.7	1.34	34.98	8.09	3.4
							20.5	6.16	85.7	1.20	35.02	8.09	4.1
						4.74	20.5	6.16	85.6	1.19	35.01	8.09	4.4
							20.4	6.01	83.4	1.26	35.14	8.09	7.2
							20.4	5.99	83.2	1.28	35.11	8.09	7.5
							20.4	6.47	85.1	1.73	35.26	8.11	6.9
13:02	CC4	MF	845444	815595	2.4	1.20	20.4	6.45	84.7	1.72	35.25	8.11	6.1
							20.5	6.46	84.8	1.34	34.89	8.01	9.7
							20.5	6.44	84.5	1.34	34.89	8.01	9.7
						3.80	20.5	6.33	83.1	1.35	34.89	8.01	10
							20.5	6.32	82.9	1.34	34.89	8.01	10
							20.5	6.16	82.9	1.57	35.76	8.01	10.1
							20.5	6.15	82.9	1.57	35.76	8.01	9.3
13:20	CC2	MF	844076	817091	12.04	1.00	20.6	6.29	83.7	1.45	35.05	8.17	14.4
							20.6	6.28	83.6	1.43	35.05	8.16	14.1
							20.6	6.15	83.8	1.40	34.97	8.12	14.7
						2.38	20.6	6.13	83.4	1.37	34.95	8.20	15.1
							21.2	6.50	86.3	0.57	34.55	8.06	6.9
							20.9	6.48	85.7	0.52	34.79	8.06	6.9
							20.4	6.52	85.8	1.44	35.35	8.07	7
13:11	C3	MF	843821	816211	15.56	7.78	20.4	6.53	85.9	1.44	35.39	8.07	7.4
							20.4	6.67	87.9	1.72	35.61	8.09	7.7
							20.4	6.67	87.9	1.72	35.61	8.09	7.3
						14.56	20.4	6.66	87.7	1.72	35.33	8.04	7.1
							20.4	6.65	87.5	1.72	35.33	8.04	7.4
							20.4	6.64	87.5	1.83	35.54	8.10	7.5
							20.4	6.65	87.6	1.89	35.54	8.10	7.8
13:06	C4	MF	844621	815770	16.09	8.05	20.4	6.71	88.6	1.20	35.74	8.10	8.9
							20.4	6.72	88.7	1.18	35.76	8.10	8.2
							20.6	6.51	85.6	0.60	34.77	8.04	6.1
						15.09	20.6	6.50	85.4	0.60	34.78	8.04	6.2
							20.4	6.28	82.2	1.25	35.05	8.04	6.4
							20.4	6.27	82.2	1.24	35.05	8.04	5.8
							20.3	6.23	82.2	1.52	35.13	8.04	5.9
13:28	II	MF	844602	817675	10.08	9.08	20.3	6.22	82.2	1.55	35.14	8.04	5.7
							20.3	6.22	82.2	1.55	35.14	8.04	5.7

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide

Impact Water Quality Monitoring Result

Sampling Date: 22-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
11:56	CC1	ME	843201	816416	8.05	1.00	20.6	6.69	91.5	0.57	35.23	8.08	<1.0
						20.6	6.68	91.4	0.52	35.22	8.08	<1.0	
						4.03	20.6	6.64	90.8	0.45	35.26	8.09	<1.0
						20.6	6.64	90.7	0.44	35.26	8.09	1.7	
						7.05	20.5	6.62	90.5	0.52	35.28	8.09	<1.0
20.5	6.61	90.4	0.54	35.28	8.1	1.1							
12:01	CC2	ME	844076	817091	12.12	1.00	20.6	6.56	89.7	0.44	35.07	8.07	1.1
						20.6	6.56	89.6	0.42	35.07	8.07	<1.0	
						6.06	20.5	6.39	87.2	0.39	35.03	8.08	<1.0
						20.5	6.39	87.2	0.38	35.03	8.08	<1.0	
						11.12	20.5	6.39	87.3	0.60	35.16	8.09	<1.0
20.5	6.40	87.4	0.63	35.18	8.09	<1.0							
12:11	CC3	ME	844606	817941	9.55	1.00	20.7	6.18	84.3	3.59	34.41	8.03	<1.0
						20.7	6.18	84.3	3.45	34.42	8.03	<1.0	
						4.78	20.6	6.14	83.7	0.82	34.65	8.04	<1.0
						20.6	6.15	83.8	0.68	34.67	8.04	<1.0	
						8.55	20.4	5.86	79.8	1.45	34.96	8.04	<1.0
20.4	5.85	79.6	1.58	34.98	8.05	<1.0							
11:42	CC4	ME	845444	815595	2.47	1.24	20.7	6.36	87.0	0.64	34.91	8.06	<1.0
						20.6	6.27	85.7	0.64	34.91	8.07	1.3	
12:04	CC13	ME	844200	817495	7.84	1.00	20.6	6.32	86.2	1.13	34.94	8.06	<1.0
						20.6	6.30	86.0	1.12	34.94	8.06	1.3	
						3.92	20.5	6.31	86.2	1.46	35.15	8.07	1.1
						20.4	6.32	86.3	1.48	35.16	8.07	1.4	
						6.84	20.4	6.38	87.1	1.81	35.20	8.09	1.3
20.4	6.38	87.1	1.90	35.20	8.09	<1.0							
11:36	SW11	ME	845512	817442	3.31	1.00	20.7	6.42	87.7	0.44	34.54	8.13	<1.0
						20.7	6.36	86.7	0.41	34.56	8.13	1.6	
						2.31	20.6	5.91	80.5	0.72	34.60	8.08	<1.0
20.6	5.92	80.6	0.53	34.60	8.08	<1.0							
11:53	C3	ME	843821	816211	15.55	1.00	20.6	6.41	87.4	0.66	34.73	8.07	1.3
						20.6	6.37	86.9	0.47	34.77	8.07	1.8	
						7.78	20.6	6.36	86.9	0.29	35.03	8.08	1.1
						20.6	6.39	87.3	0.26	35.07	8.08	1.7	
						14.55	20.5	6.59	90.2	0.41	35.37	8.11	3.2
20.5	6.59	90.2	0.41	35.37	8.11	3.5							
11:48	C4	ME	844621	815770	16.25	1.00	20.8	6.59	90.4	0.55	34.84	8.10	2.5
						20.8	6.58	90.3	0.53	34.85	8.09	2.3	
						8.13	20.6	6.49	88.7	0.44	35.12	8.09	2.1
						20.6	6.49	88.7	0.44	35.12	8.09	2.4	
						15.25	20.6	6.53	89.4	0.60	35.32	8.10	2.2
20.6	6.54	89.6	0.62	35.36	8.10	1.6							
12:07	II	ME	844602	817675	10.12	1.00	21.2	6.35	87.4	0.28	34.10	8.04	<1.0
						20.8	6.35	86.9	0.32	34.41	8.04	<1.0	
						5.06	20.5	6.31	86.0	0.20	34.83	8.05	<1.0
						20.5	6.31	86.1	0.20	34.83	8.05	1.2	
						9.12	20.5	6.31	86.2	1.23	35.13	8.07	1.3
20.5	6.32	86.2	1.30	35.14	8.07	1.7							
8:43	CC1	MF	843201	816416	8.36	1.00	20.6	6.33	86.3	2.92	34.76	8.09	1.5
						20.6	6.32	86.2	2.63	34.76	8.09	<1.0	
						4.18	20.5	6.14	83.7	0.61	34.85	8.09	1.3
						20.5	6.13	83.6	0.62	34.85	8.09	1.5	
						7.36	20.5	6.13	83.7	0.70	34.89	8.09	1.3
20.5	6.14	83.7	0.69	34.89	8.09	<1.0							
8:48	CC2	MF	844076	817091	12.12	1.00	20.6	6.32	86.2	0.35	34.75	8.06	1.7
						20.6	6.3	86.0	0.34	34.75	8.06	2.1	
						6.06	20.6	6.13	83.7	0.59	34.81	8.07	1.2
						20.6	6.14	83.7	0.65	34.82	8.07	<1.0	
						11.12	20.5	6.29	86.0	1.83	35.16	8.08	<1.0
20.5	6.31	86.2	1.92	35.18	8.08	<1.0							
9:00	CC3	MF	844606	817941	9.56	1.00	20.8	6.56	89.7	0.40	34.58	8.02	2.2
						20.8	6.53	89.3	0.38	34.60	8.02	2.3	
						4.78	20.7	6.38	87.3	0.24	34.70	8.04	<1.0
						20.7	6.38	87.2	0.23	34.71	8.04	<1.0	
						8.56	20.6	6.23	83.0	0.30	34.80	8.05	<1.0
20.6	6.21	84.8	0.32	34.81	8.05	<1.0							
8:31	CC4	MF	845444	815595	2.49	1.25	20.6	6.34	86.7	0.77	34.96	8.16	1.4
						20.6	6.32	86.3	0.76	34.95	8.16	1.5	
8:52	CC13	MF	844200	817495	7.69	1.00	20.7	6.33	86.4	0.38	34.59	8.05	1.7
						20.7	6.31	86.1	0.38	34.59	8.05	1.4	
						3.85	20.7	6.20	84.7	0.39	34.59	8.05	1.1
						20.7	6.19	84.5	0.38	34.59	8.05	1.7	
						6.69	20.7	6.03	82.3	0.61	34.70	8.05	2
20.7	6.02	82.3	0.61	34.70	8.05	2.1							
8:23	SW11	MF	845512	817442	3.46	1.00	20.8	6.16	84.3	0.49	34.75	8.32	1.7
						20.8	6.15	84.2	0.47	34.75	8.31	1.7	
						2.46	20.7	6.02	82.4	0.44	34.67	8.27	2.2
20.7	6.00	82.0	0.41	34.65	8.25	2.1							
8:39	C3	MF	843821	816211	15.65	1.00	21.3	6.37	87.9	0.61	34.25	8.11	2.4
						21.1	6.35	87.3	0.56	34.49	8.11	2.9	
						7.83	20.6	6.39	87.4	0.48	35.05	8.12	1.6
						20.6	6.40	87.5	0.48	35.09	8.12	1.4	
						14.65	20.6	6.54	89.5	0.76	35.31	8.14	1.6
20.6	6.54	89.5	0.76	35.31	8.14	1.4							
8:34	C4	MF	844621	815770	16.18	1.00	20.6	6.53	89.3	0.76	35.03	8.09	2
						20.6	6.52	89.1	0.76	35.03	8.09	1.3	
						8.09	20.6	6.51	89.1	0.87	35.24	8.15	2.1
						20.6	6.52	89.2	0.93	35.24	8.15	1.7	
						15.18	20.6	6.58	90.2	1.24	35.44	8.15	1.6
20.6	6.59	90.3	1.22	35.46	8.15	2.3							
8:57	II	MF	844602	817675	10.17	1.00	20.8	6.38	87.2	0.44	34.47	8.04	1.6
						20.8	6.37	87.0	0.44	34.48	8.04	2.4	
						5.09	20.6	6.15	83.8	0.29	34.75	8.06	1.5
						20.6	6.14	83.8	0.28	34.75	8.06	2.3	
						9.17	20.4	6.10	83.0	0.56	34.83	8.06	1.5
20.4	6.09	83.0	0.59	34.84	8.06	2.1							

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.

Impact Water Quality Monitoring Result													
Sampling Date: 25-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
13:59	CC1	ME	843201	816416	9.11	1.00	20.7	6.85	94.1	1.10	35.50	8.16	4
						20.7	6.82	93.6	1.08	35.49	8.16	4.2	
						4.56	20.7	6.66	91.6	1.11	35.50	8.16	3.7
						20.7	6.66	91.6	1.12	35.50	8.16	4.7	
						8.11	20.7	6.65	91.4	1.07	35.50	8.16	6.6
20.7	6.65	91.4	1.07	35.50	8.16	5.6							
14:05	CC2	ME	844076	817091	12.22	1.00	20.6	6.82	93.4	0.84	35.23	8.15	4.8
						20.6	6.81	93.2	0.83	35.23	8.15	3.8	
						6.11	20.7	6.71	92.0	0.98	35.31	8.15	4.3
						20.7	6.70	91.8	1.00	35.32	8.15	4.1	
						11.22	20.7	6.65	91.3	1.64	35.54	8.15	7.2
20.7	6.65	91.4	1.68	35.55	8.15	7.3							
14:17	CC3	ME	844606	817941	9.51	1.00	20.7	6.53	89.5	0.99	35.11	8.14	5.7
						20.7	6.52	89.4	1.00	35.11	8.14	4.9	
						4.76	20.7	6.46	88.6	1.23	35.21	8.13	5.6
						20.7	6.46	88.6	1.23	35.22	8.13	5	
						8.51	20.7	6.43	88.2	1.75	35.37	8.13	5.8
20.7	6.43	88.2	1.80	35.38	8.13	6.3							
13:44	CC4	ME	845444	815595	2.31	1.16	20.7	6.56	90.0	1.39	35.32	8.17	5.4
						20.7	6.55	89.9	1.37	35.31	8.17	5.6	
14:09	CC13	ME	844200	817495	9.06	1.00	20.6	6.70	91.6	0.89	35.27	8.15	4.4
						20.6	6.69	91.5	0.90	35.28	8.15	3.9	
						4.53	20.7	6.58	90.2	1.30	35.36	8.14	5.8
						20.7	6.58	90.2	1.31	35.36	8.14	5.5	
						8.06	20.7	6.55	89.9	1.61	35.38	8.14	4.8
20.7	6.55	89.8	1.65	35.39	8.14	5.2							
13:38	SW11	ME	845512	817442	3.16	1.00	20.7	6.65	91.2	0.68	35.32	8.21	3.8
						20.7	6.65	91.1	0.67	35.32	8.20	3.7	
13:54	C3	ME	843821	816211	16.04	2.16	20.7	6.60	90.5	0.73	35.32	8.20	3.8
						20.7	6.60	90.5	0.74	35.32	8.19	4.3	
						1.00	20.5	6.85	93.7	0.79	35.49	8.16	7
						20.6	6.83	93.6	0.78	35.43	8.16	6.3	
						8.02	20.8	6.72	92.5	0.93	35.56	8.16	6.1
20.8	6.72	92.5	0.93	35.56	8.16	7							
15.04	20.8	6.70	92.2	1.11	35.56	8.16	6.9						
20.8	6.70	92.2	1.13	35.56	8.16	6.1							
13:50	C4	ME	844621	815770	15.9	1.00	20.7	6.84	93.9	0.71	35.31	8.16	4.8
						20.7	6.84	93.9	0.71	35.31	8.16	5.7	
						7.95	20.8	6.70	92.1	0.76	35.47	8.16	5.1
						20.8	6.70	92.2	0.78	35.49	8.16	5.2	
						14.90	20.9	6.70	92.5	2.08	35.68	8.17	3.7
20.9	6.70	92.4	2.13	35.68	8.17	4.6							
14:13	II	ME	844602	817675	10.14	1.00	20.7	6.72	92.4	0.72	35.07	8.14	4.9
						20.7	6.70	91.8	0.75	35.08	8.14	5.5	
						5.07	20.7	6.62	90.7	1.25	35.11	8.13	4.5
						20.7	6.60	90.4	1.37	35.13	8.13	5	
						9.14	20.7	6.48	89.0	1.84	35.47	8.14	3.7
20.7	6.49	89.1	1.86	35.48	8.14	3.1							
10:05	CC1	MF	843201	816416	10.14	1.00	20.5	6.6	90.2	1.49	35.17	8.14	7.9
						20.5	6.6	90.1	1.47	35.17	8.13	7	
						5.07	20.5	6.55	89.5	1.02	35.19	8.13	7.1
						20.5	6.55	89.5	0.99	35.19	8.13	8	
						9.14	20.5	6.49	88.6	0.79	35.21	8.13	5.6
20.5	6.49	88.6	0.79	35.21	8.13	5.3							
10:10	CC2	MF	844076	817091	12.16	1.00	20.5	6.55	89.4	0.76	35.12	8.13	6.2
						20.5	6.55	89.4	0.77	35.12	8.13	6.3	
						6.08	20.5	6.53	89.2	0.74	35.17	8.13	5.5
						20.5	6.53	89.2	0.72	35.18	8.13	6.4	
						11.16	20.6	6.55	89.6	0.75	35.30	8.13	8.3
20.6	6.55	89.6	0.74	35.30	8.13	8.2							
10:26	CC3	MF	844606	817941	9.19	1.00	20.6	6.38	87.3	0.99	35.08	8.13	3.8
						20.6	6.38	87.3	0.98	35.08	8.12	4.1	
						4.60	20.7	6.38	87.3	1.22	35.22	8.12	6.4
						20.7	6.38	87.3	1.25	35.23	8.12	7.3	
						8.19	20.7	6.37	87.3	1.54	35.36	8.12	6.7
20.7	6.37	87.4	1.60	35.38	8.12	7.6							
9:49	CC4	MF	845444	815595	2.49	1.25	20.5	6.75	92.2	0.96	35.17	8.16	5.3
						20.5	6.74	92.0	0.96	35.17	8.16	4.4	
10:16	CC13	MF	844200	817495	8.05	1.00	20.6	6.51	89.0	0.75	35.21	8.13	3.8
						20.6	6.50	88.9	0.76	35.21	8.13	3.1	
						4.03	20.6	6.49	88.7	0.75	35.24	8.13	2.6
						20.6	6.49	88.8	0.75	35.24	8.13	3	
						7.05	20.6	6.52	89.2	0.74	35.27	8.13	4.3
20.6	6.53	89.3	0.74	35.27	8.13	5.1							
9:42	SW11	MF	845512	817442	3.62	1.00	20.6	6.56	89.7	0.93	35.29	8.20	5.8
						20.6	6.54	89.4	0.94	35.29	8.20	5.5	
						2.62	20.6	6.49	88.7	0.98	35.30	8.19	9.6
						20.6	6.48	88.7	0.98	35.31	8.19	9.5	
10:00	C3	MF	843821	816211	15.94	1.00	20.6	6.64	91.0	0.87	35.30	8.14	9.2
						20.6	6.64	90.9	0.87	35.30	8.14	8.4	
						7.97	20.7	6.68	91.8	1.51	35.55	8.15	8.4
						20.7	6.68	91.8	1.51	35.55	8.15	8.7	
						14.94	20.7	6.67	91.7	1.65	35.56	8.16	5.5
20.7	6.67	91.7	1.66	35.56	8.16	5.6							
9:54	C4	MF	844621	815770	16.03	1.00	20.6	6.74	92.3	0.77	35.36	8.16	3.4
						20.6	6.73	92.2	0.76	35.36	8.16	3.8	
						8.02	20.7	6.69	91.8	0.88	35.47	8.15	3.6
						20.7	6.69	91.9	0.89	35.48	8.15	4	
						15.03	20.8	6.71	92.4	2.33	35.66	8.17	3.8
20.8	6.71	92.4	2.26	35.66	8.17	3.8							
10:22	II	MF	844602	817675	10.07	1.00	20.6	6.48	88.5	0.71	35.03	8.13	4.9
						20.6	6.47	88.4	0.70	35.02	8.13	5.3	
						5.04	20.6	6.44	88.1	0.80	35.22	8.12	2.9
						20.6	6.44	88.1	0.82	35.24	8.12	3.3	
						9.07	20.7	6.49	89.1	1.00	35.45	8.13	3.5
20.7	6.50	89.2	1.00	35.45	8.13	4.4							

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide

Impact Water Quality Monitoring Result

Sampling Date: 27-Mar-19

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
16:22	CC1	ME	843201	816416	9.42	1.00	21.0	6.75	93.2	1.08	35.42	8.15	2.8
						21.0	6.72	92.7	1.10	35.41	8.15	3.5	
						4.71	21.0	6.63	91.4	1.12	35.43	8.14	2.4
						21.0	6.62	91.4	1.12	35.44	8.14	2.2	
						8.42	21.0	6.52	90.0	1.46	35.58	8.14	3.1
16:28	CC2	ME	844076	817091	12.34	1.00	21.0	6.52	90.0	1.46	35.58	8.14	2.7
						20.8	7.00	96.3	0.65	35.42	8.14	2.9	
						20.8	6.77	93.1	0.67	35.40	8.14	3.1	
						6.17	20.9	6.53	90.0	1.53	35.49	8.14	3.1
						20.9	6.52	90.0	1.53	35.49	8.14	3.2	
16:46	CC3	ME	844606	817941	9.13	1.00	20.9	6.45	89.0	2.23	35.55	8.13	6.2
						21.0	6.44	88.9	2.41	35.56	8.13	6.4	
						20.8	6.54	89.9	1.49	35.22	8.14	3.5	
						4.57	20.9	6.53	89.8	1.50	35.19	8.14	3.4
						20.9	6.48	89.2	1.35	35.25	8.14	3	
16:01	CC4	ME	845444	815595	2.35	1.00	20.9	6.48	89.1	1.35	35.25	8.14	3.7
						20.8	6.47	89.0	1.30	35.35	8.13	2.4	
						20.8	6.45	88.8	1.35	35.36	8.13	2.9	
						1.18	20.9	6.38	88.0	1.47	35.41	8.13	3.3
						20.9	6.38	88.0	1.47	35.41	8.13	3.7	
16:36	CC13	ME	844200	817495	8.61	1.00	20.9	6.64	91.5	0.80	35.34	8.14	2.9
						20.9	6.64	91.4	0.80	35.34	8.14	3.5	
						4.31	21.1	6.59	90.9	1.97	35.23	8.12	1.5
						20.8	6.63	91.2	0.91	35.32	8.13	3.1	
						7.61	20.8	6.62	91.1	0.91	35.32	8.13	4
15:51	SWI1	ME	845512	817442	3.51	1.00	20.9	6.53	90.0	1.51	35.46	8.13	4
						20.9	6.52	89.9	1.55	35.48	8.13	3.8	
						20.8	6.47	89.0	1.30	35.35	8.13	2.4	
						20.8	6.45	88.8	1.35	35.36	8.13	2.9	
						20.9	6.68	92.0	0.79	35.33	8.14	3.5	
16:16	C3	ME	843821	816211	16.09	1.00	20.9	6.68	92.0	0.79	35.33	8.14	4
						20.9	6.64	91.5	0.80	35.34	8.14	2.9	
						2.51	20.9	6.64	91.4	0.80	35.34	8.14	3.5
						1.00	21.1	6.59	90.9	1.97	35.23	8.12	1.5
						20.9	6.57	90.6	0.70	35.29	8.12	<1.0	
16:05	C4	ME	844621	815770	16.15	8.05	20.9	6.57	90.6	0.70	35.30	8.12	2.2
						20.9	6.57	90.6	0.70	35.30	8.12	2.2	
						15.09	21.0	6.53	90.1	2.03	35.54	8.13	2.5
						21.0	6.53	90.1	1.97	35.54	8.13	2.7	
						1.00	20.8	6.97	95.9	0.72	35.39	8.15	1.5
16:43	II	ME	844602	817675	10.09	1.00	20.8	6.95	95.6	0.73	35.37	8.14	1.4
						8.08	21.0	6.75	93.2	0.55	35.50	8.15	1.2
						21.0	6.75	93.2	0.55	35.50	8.15	1.8	
						15.15	21.1	6.62	91.6	2.30	35.66	8.15	1.3
						21.1	6.62	91.6	2.29	35.66	8.15	1.4	
11:10	CC1	MF	843201	816416	9.2	1.00	20.9	6.57	90.5	1.17	35.23	8.13	2.6
						20.9	6.57	90.5	1.15	35.23	8.13	2.6	
						5.05	20.9	6.44	88.6	1.53	35.35	8.13	2
						20.9	6.43	88.4	1.57	35.36	8.13	2.6	
						9.09	20.9	6.40	88.1	1.71	35.42	8.13	2.4
11:17	CC2	MF	844076	817091	12.17	1.00	20.9	6.40	88.1	1.73	35.43	8.13	2.5
						20.8	6.66	91.4	0.98	35.26	8.14	4.3	
						20.8	6.65	91.4	0.96	35.27	8.14	3.9	
						4.60	20.8	6.57	90.2	0.95	35.29	8.13	2.9
						20.8	6.56	90.2	0.95	35.29	8.13	2.7	
11:38	CC3	MF	844606	817941	10.05	8.20	20.8	6.46	88.8	1.22	35.34	8.12	2.4
						20.8	6.45	88.7	1.23	35.34	8.12	3.2	
						1.00	20.4	6.77	92.4	0.79	35.61	8.13	3.3
						20.4	6.75	92.3	0.78	35.55	8.13	3	
						6.09	20.8	6.57	90.3	1.02	35.29	8.12	2.5
10:52	CC4	MF	845444	815595	2.42	11.17	20.8	6.57	90.2	1.03	35.29	8.12	3.2
						20.9	6.43	88.7	2.12	35.53	8.12	3.5	
						20.9	6.42	88.6	2.22	35.54	8.12	3.8	
						1.00	20.8	6.41	88.1	1.56	35.13	8.12	3.5
						20.8	6.41	88.1	1.55	35.12	8.12	2.8	
11:25	CC13	MF	844200	817495	8.25	5.03	20.8	6.32	86.9	1.48	35.37	8.12	3.2
						20.8	6.32	86.9	1.47	35.37	8.12	3	
						9.05	20.8	6.02	82.8	3.63	35.49	8.11	3.8
						20.8	6.01	82.8	3.73	35.49	8.11	3	
						1.21	20.8	6.60	90.7	0.95	35.19	8.13	2.8
11:04	C3	MF	843821	816211	16.2	20.8	6.58	90.5	0.97	35.19	8.13	2.6	
						1.00	20.8	6.63	91.2	1.06	35.28	8.13	7.2
						20.8	6.63	91.1	1.05	35.28	8.13	6.5	
						4.13	20.8	6.55	90.0	0.92	35.30	8.13	4.3
						20.8	6.55	90.0	0.92	35.30	8.13	3.6	
10:37	SWI1	MF	845512	817442	3.53	7.25	20.8	6.53	89.7	0.89	35.34	8.13	3.5
						20.8	6.52	89.7	0.88	35.34	8.13	4.1	
						1.00	20.9	6.55	90.1	0.86	35.34	8.16	3.2
						20.9	6.55	90.1	0.87	35.34	8.16	3.6	
						2.53	20.9	6.53	89.9	0.89	35.34	8.15	4
10:58	C4	MF	844621	815770	16.1	20.9	6.53	89.9	0.90	35.35	8.15	3	
						1.00	20.9	6.56	90.3	0.75	35.32	8.13	3.4
						20.9	6.56	90.3	0.75	35.32	8.13	3.3	
						8.10	20.9	6.56	90.5	1.19	35.50	8.13	1.2
						20.9	6.56	90.5	1.16	35.53	8.13	1.7	
11:31	II	MF	844602	817675	10.05	15.20	21.1	6.55	90.5	2.68	35.63	8.14	1.2
						21.1	6.54	90.5	2.67	35.62	8.14	1.5	
						1.00	20.8	6.63	91.1	0.76	35.29	8.14	<1.0
						8.05	20.8	6.62	91.1	0.76	35.29	8.14	1.1
						20.9	6.64	91.6	0.73	35.49	8.14	1.5	

Remarks: MF - Middle Flood tide

ME - Middle Ebb tide

For SS, if the monitoring result is less than Limit of Report 1mg/L, the result value will be assumed as 1 for the calculation.


Impact Water Quality Monitoring Result													
Sampling Date: 30-Mar-19													
Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/L
			East	North									
17:03	CC1	ME	843201	816416	9.67	1.00	21.0	6.67	92.1	1.06	35.39	8.15	2
						21.0	6.67	92.0	1.08	35.39	8.15	2	
						4.84	21.0	6.54	90.3	1.39	35.55	8.14	2.3
						21.0	6.53	90.3	1.37	35.54	8.14	2.4	
						8.67	21.0	6.50	89.8	1.63	35.59	8.14	2.1
						21.0	6.50	89.8	1.64	35.59	8.14	2.3	
17:09	CC2	ME	844076	817091	12.13	1.00	20.9	6.72	92.6	0.68	35.37	8.14	2
						20.9	6.70	92.3	0.69	35.31	8.14	2.1	
						6.07	20.9	6.46	89.0	1.38	35.41	8.13	2.7
						20.9	6.46	89.0	1.38	35.41	8.13	2.6	
						11.13	21.0	6.44	88.9	2.41	35.56	8.13	2.6
						21.0	6.44	88.9	2.43	35.56	8.13	3	
17:27	CC3	ME	844606	817941	9.53	1.00	20.9	6.51	89.6	1.46	35.18	8.14	4.1
						20.9	6.51	89.6	1.45	35.20	8.14	4.6	
						4.77	20.8	6.48	89.2	1.13	35.31	8.13	6.2
						20.8	6.49	89.3	1.11	35.30	8.13	5.8	
						8.53	20.8	6.17	85.0	2.26	35.46	8.12	7
						20.8	6.17	85.0	2.28	35.46	8.12	6.8	
16:41	CC4	ME	845444	815595	2.56	1.28	20.9	6.38	87.8	1.48	35.41	8.13	3.6
						20.9	6.37	87.8	1.46	35.41	8.13	3.8	
17:17	CC13	ME	844200	817495	8.43	1.00	20.9	6.73	92.7	0.86	35.29	8.14	2
						20.9	6.73	92.7	0.86	35.29	8.14	1.9	
						4.22	20.8	6.57	90.4	0.95	35.33	8.13	2.3
						20.8	6.57	90.4	0.95	35.33	8.13	2.2	
						7.43	20.9	6.49	89.6	1.81	35.53	8.13	2.4
						20.9	6.49	89.6	1.83	35.53	8.13	2.3	
16:32	SW11	ME	845512	817442	3.26	1.00	20.9	6.68	92.1	0.76	35.33	8.15	2
						20.9	6.68	92.1	0.77	35.33	8.15	2.3	
16:57	C3	ME	843821	816211	16.2	1.00	20.9	6.65	91.7	0.81	35.33	8.14	2.5
						20.9	6.65	91.6	0.80	35.33	8.14	2.2	
						21.1	6.59	90.9	1.84	35.23	8.12	1.4	
16:46	C4	ME	844621	815770	16.51	8.10	20.9	6.58	90.6	0.73	35.30	8.12	2.4
						20.9	6.58	90.6	0.73	35.31	8.12	2.1	
						15.20	21.0	6.53	90.1	1.96	35.55	8.13	2.2
						21.0	6.53	90.1	2.12	35.56	8.14	2.3	
						1.00	20.9	6.87	94.6	0.70	35.32	8.14	1.7
						20.9	6.85	94.3	0.69	35.30	8.14	1.6	
17:24	I1	ME	844602	817675	10	8.26	21.0	6.74	93.1	0.52	35.50	8.14	1.7
						21.0	6.74	93.1	0.52	35.50	8.14	1.9	
						15.51	21.1	6.59	91.2	4.42	35.66	8.15	2.3
						21.1	6.59	91.2	4.42	35.66	8.15	2.2	
						1.00	20.9	6.56	90.4	1.17	35.23	8.13	1.7
						20.9	6.56	90.4	1.17	35.23	8.13	2	
9:30	CC1	MF	843201	816416	9.86	5.00	20.9	6.41	88.2	1.62	35.39	8.13	1.7
						20.9	6.40	88.2	1.63	35.39	8.13	2.1	
						9.00	20.9	6.37	87.8	1.78	35.46	8.13	2.7
						20.9	6.34	87.3	1.92	35.48	8.13	2.8	
						1.00	20.8	6.65	91.3	0.96	35.27	8.14	1.8
						20.8	6.64	91.3	0.95	35.27	8.14	2.1	
9:38	CC2	MF	844076	817091	12.07	4.93	20.8	6.53	89.7	1.01	35.30	8.13	1.9
						20.8	6.53	89.7	1.01	35.30	8.13	1.6	
						8.86	20.8	6.43	88.4	1.30	35.35	8.12	2
						20.8	6.43	88.4	1.30	35.35	8.12	2.3	
						1.00	20.7	6.68	91.6	0.76	35.35	8.13	2.1
						20.7	6.67	91.5	0.75	35.30	8.13	2.1	
9:59	CC3	MF	844606	817941	9.28	6.04	20.8	6.56	90.1	1.02	35.30	8.12	2.3
						20.8	6.56	90.0	1.01	35.30	8.12	2.2	
						11.07	20.9	6.37	87.9	2.52	35.55	8.13	3
						20.9	6.36	87.8	2.53	35.55	8.13	2.7	
						1.00	20.8	6.40	87.9	1.58	35.10	8.12	1.2
						20.8	6.40	87.9	1.59	35.10	8.12	1.6	
9:12	CC4	MF	845444	815595	2.47	4.64	20.8	6.33	87.0	1.47	35.38	8.12	2.3
						20.8	6.32	87.0	1.50	35.38	8.12	2.2	
						8.28	20.8	6.01	82.7	2.96	35.49	8.11	2.9
						20.8	6.02	82.9	2.83	35.49	8.11	3.2	
						1.24	20.8	6.57	90.3	0.98	35.20	8.13	2.7
						20.8	6.56	90.1	1.01	35.20	8.13	2.9	
9:46	CC13	MF	844200	817495	8.04	1.00	20.8	6.58	90.5	1.01	35.28	8.13	2.1
						20.8	6.58	90.5	1.00	35.28	8.13	2.3	
						4.02	20.8	6.55	90.0	0.86	35.31	8.13	2.8
						20.8	6.55	90.0	0.87	35.31	8.13	3	
						7.04	20.8	6.51	89.5	0.85	35.35	8.13	4.7
						20.8	6.51	89.5	0.85	35.35	8.13	5.1	
8:58	SW11	MF	845512	817442	3.34	1.00	20.9	6.55	90.1	0.88	35.34	8.15	3.5
						20.9	6.55	90.1	0.87	35.34	8.15	3.5	
						2.34	20.9	6.54	90.1	0.87	35.34	8.15	4.6
						20.9	6.54	90.0	0.88	35.34	8.15	4.8	
						1.00	20.9	6.55	90.2	0.80	35.33	8.13	2.3
						20.9	6.55	90.2	0.80	35.33	8.13	2.5	
9:25	C3	MF	843821	816211	15.96	7.98	21.0	6.57	90.8	1.29	35.58	8.13	2.6
						21.0	6.58	90.9	1.36	35.61	8.13	2.8	
						14.96	21.1	6.54	90.5	2.62	35.63	8.14	3.2
						21.1	6.54	90.5	2.63	35.63	8.14	2.8	
						1.00	20.8	6.61	90.9	0.74	35.29	8.13	2.8
						20.8	6.61	90.9	0.74	35.29	8.13	2.6	
9:19	C4	MF	844621	815770	16.01	8.01	20.9	6.65	91.7	0.73	35.50	8.14	4.9
						20.9	6.65	91.7	0.73	35.50	8.14	4.5	
						15.01	21.1	6.64	91.8	2.37	35.66	8.15	5.2
						21.1	6.64	91.9	2.38	35.66	8.15	5.7	
						1.00	20.8	6.52	89.6	1.02	35.18	8.13	3.5
						20.8	6.52	89.6	1.02	35.19	8.13	3.8	
9:52	I1	MF	844602	817675	10.13	5.07	20.8	6.51	89.4	1.07	35.34	8.13	5.2
						20.8	6.51	89.5	1.05	35.33	8.13	5.4	
						9.13	20.9	6.37	87.8	1.87	35.50	8.13	6.3
						20.9	6.36	87.6	1.93	35.51	8.13	6	

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide


Appendix I

Graphical Plots of Monitoring Results


Air Quality – 1 Hour TSP

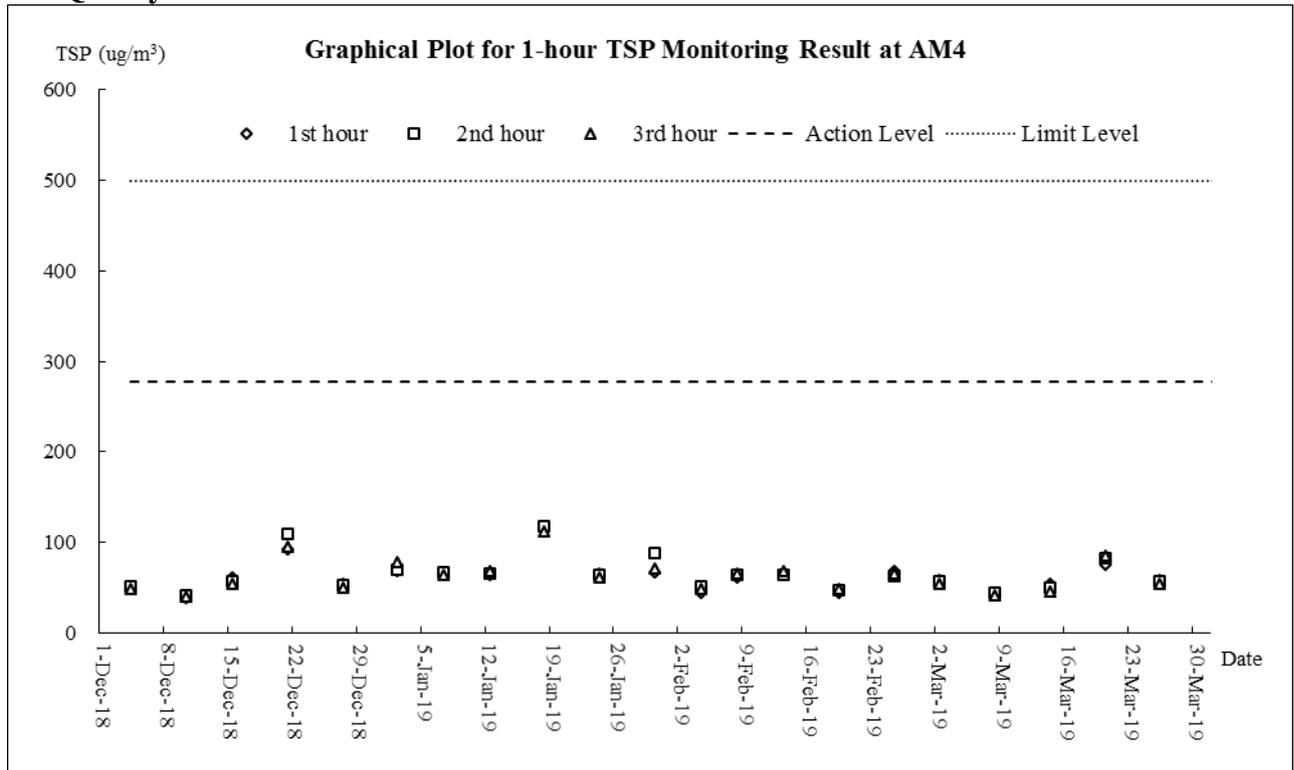




Air Quality - 24-Hour TSP

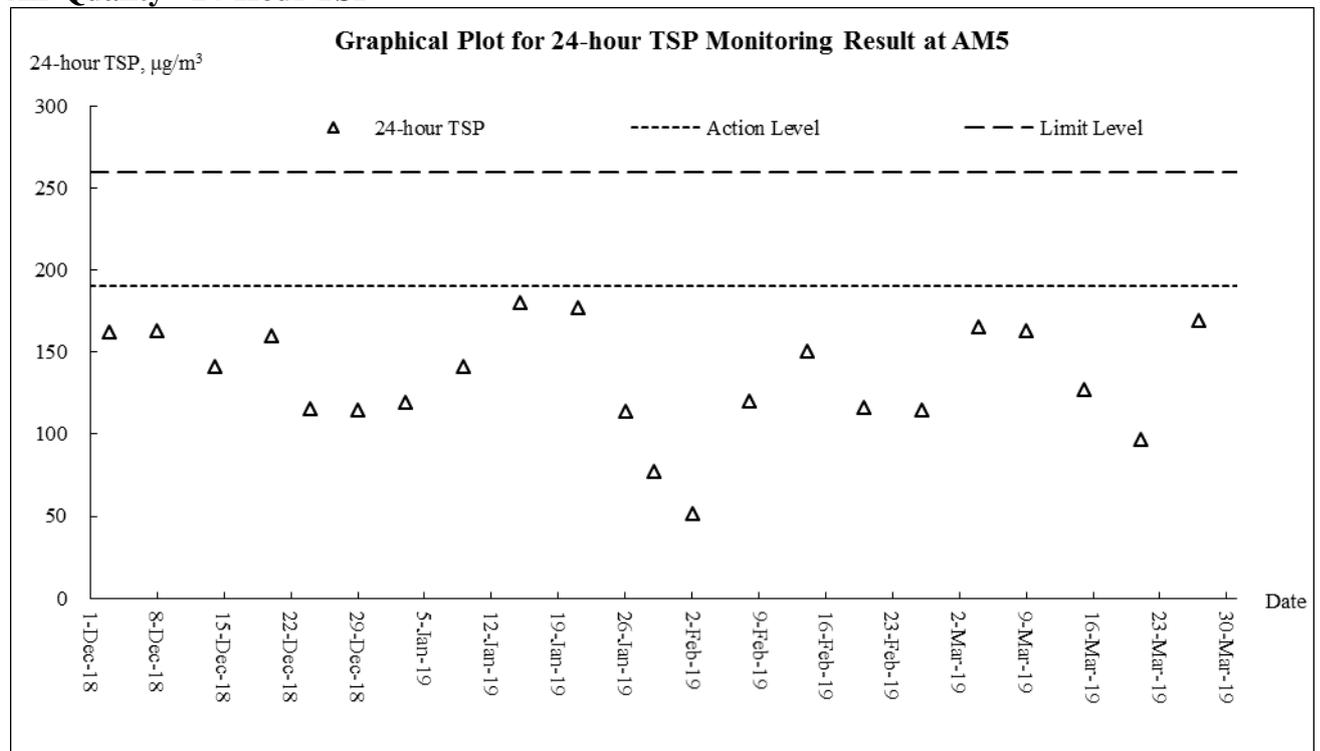




Construction Noise

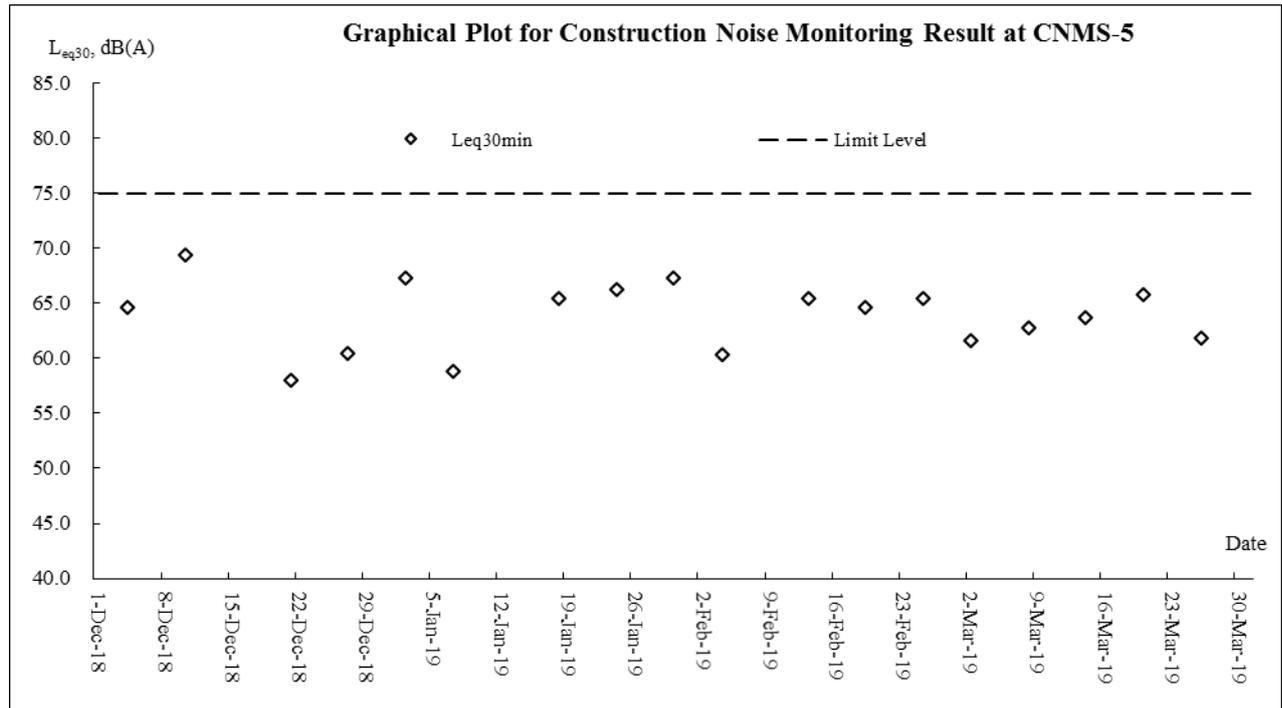




Marine Water Quality – CC1 Mid-ebb

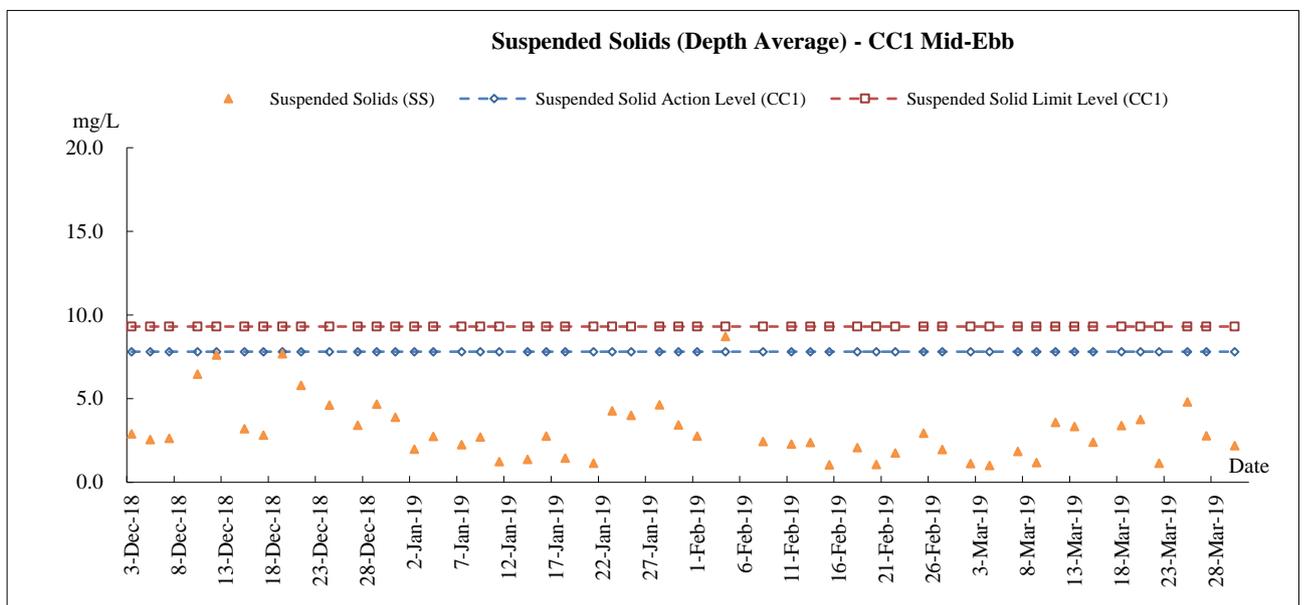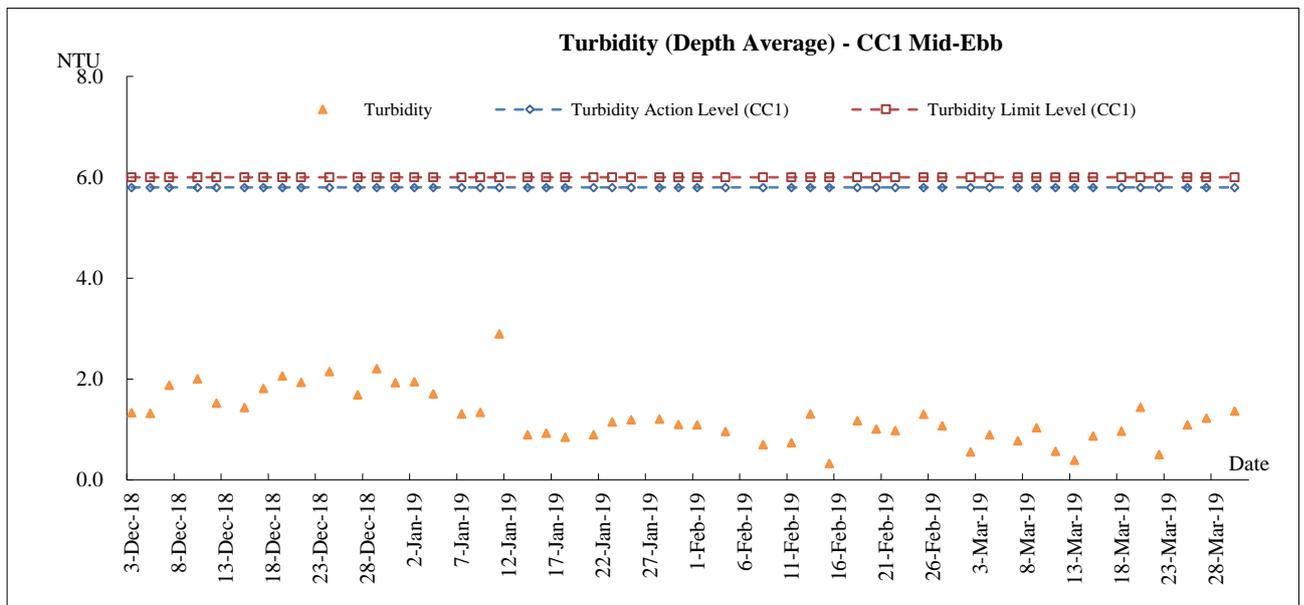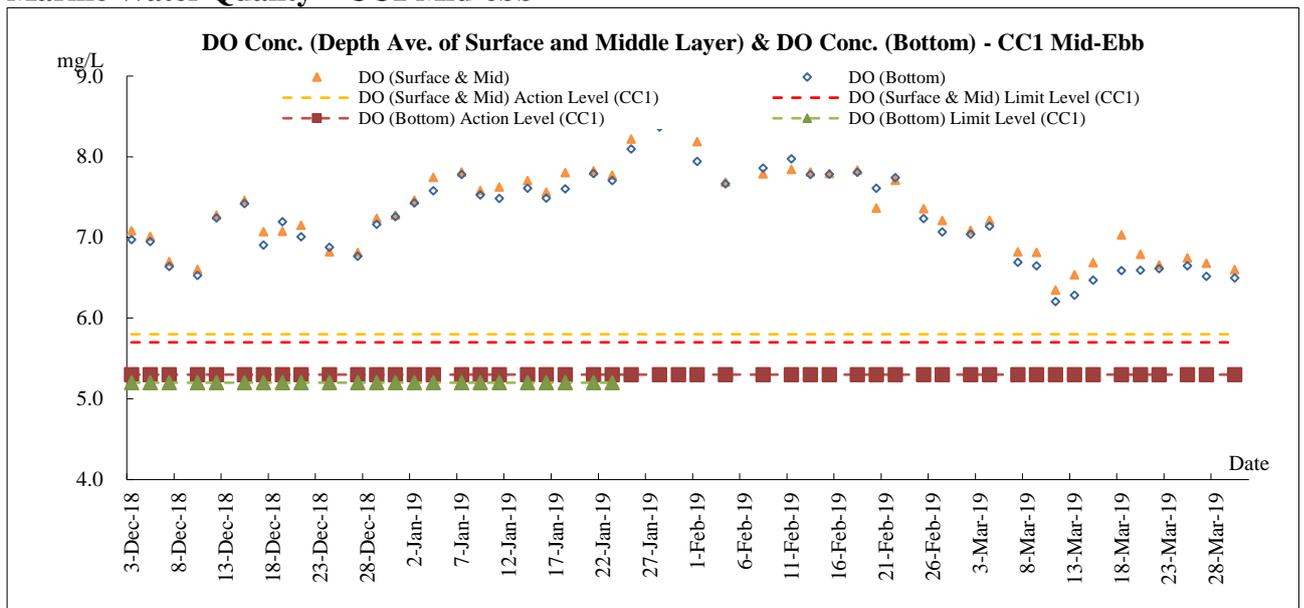




Marine Water Quality – CC2 Mid-ebb

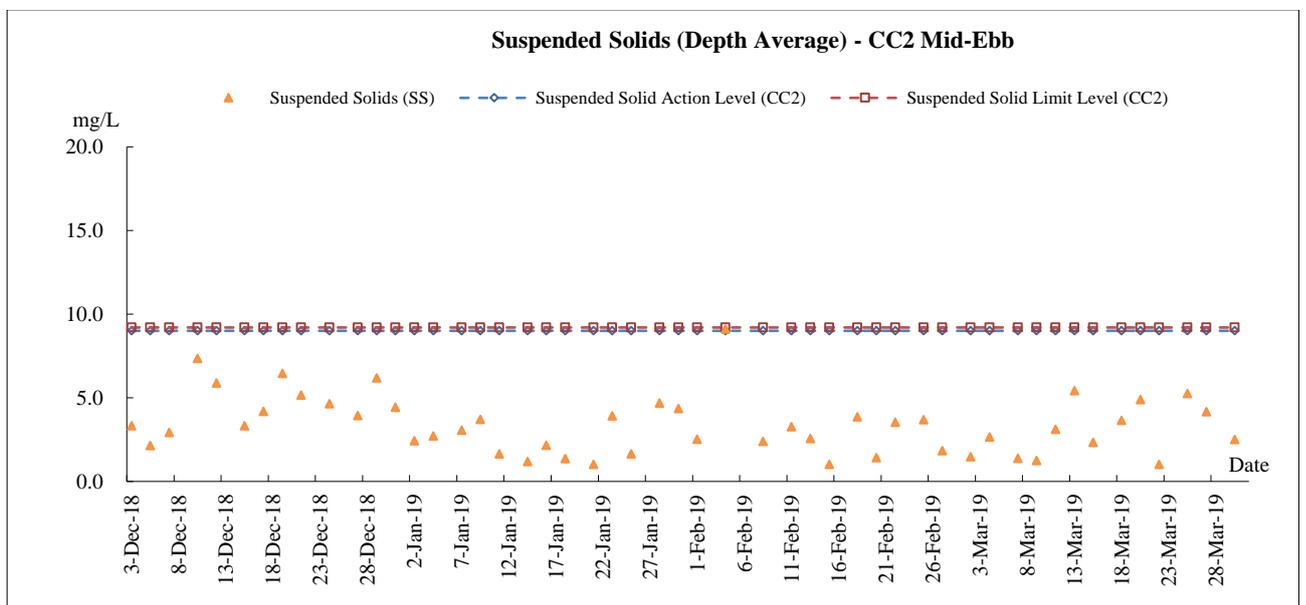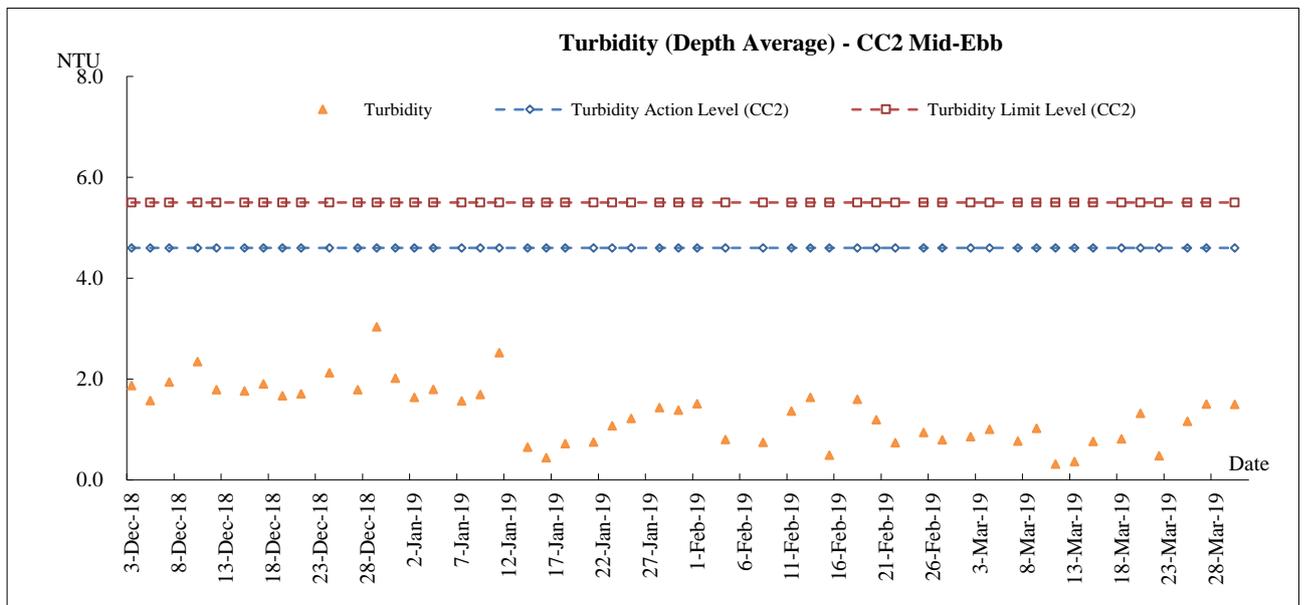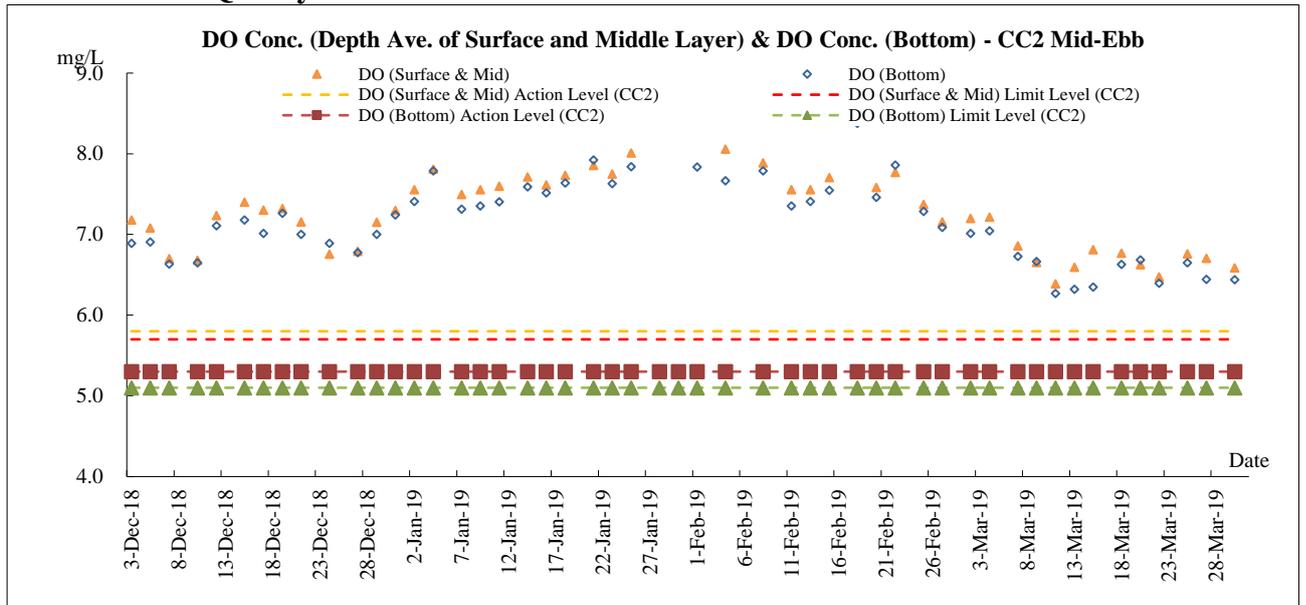




Marine Water Quality – CC3 Mid-ebb

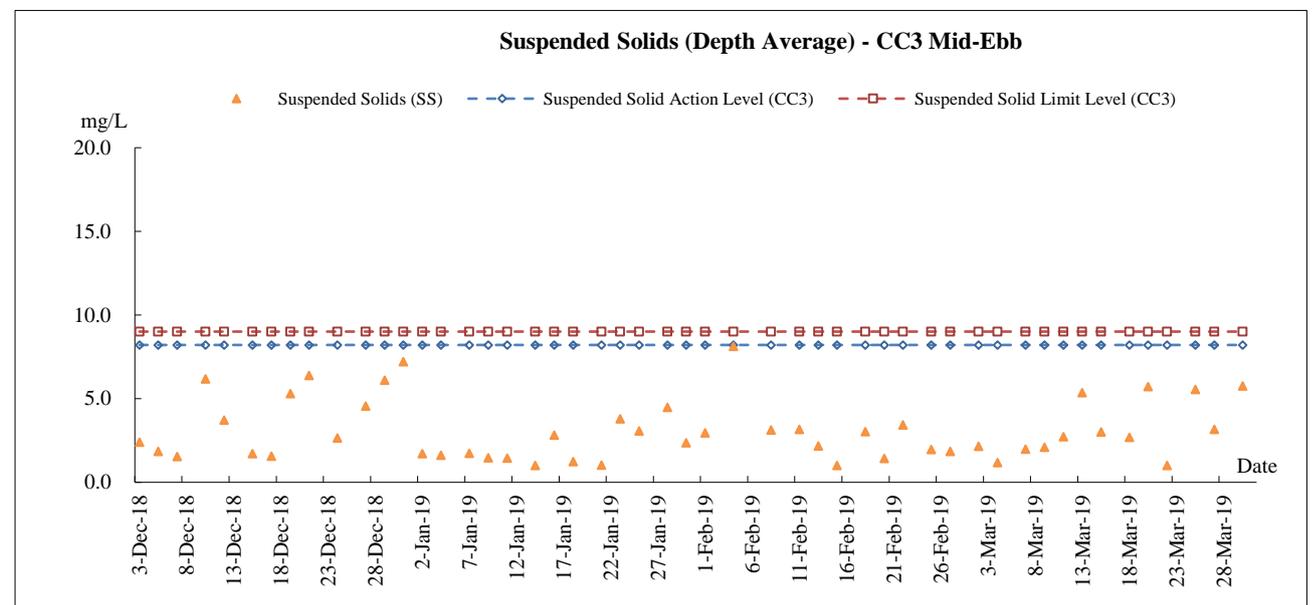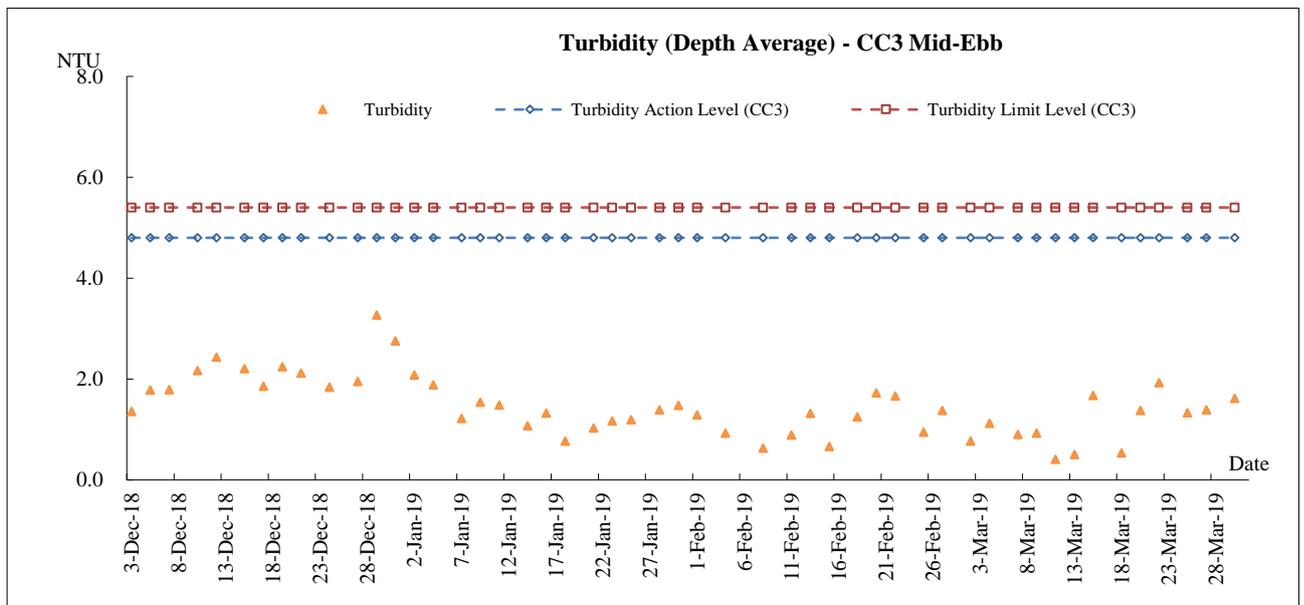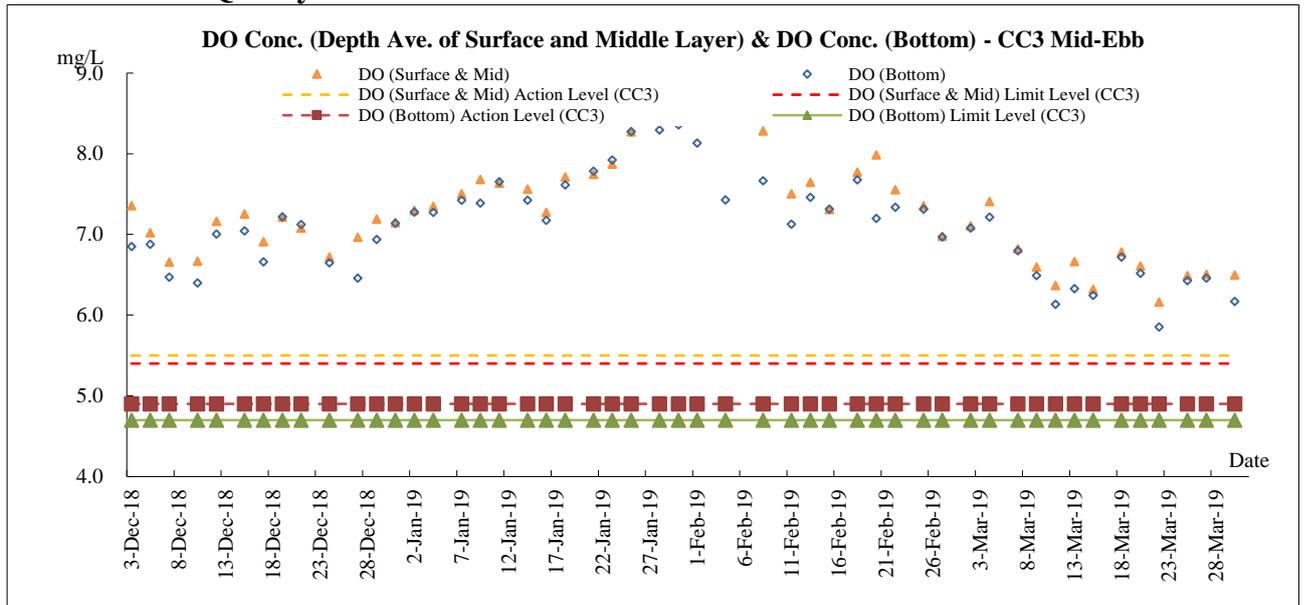




Marine Water Quality – CC4 Mid-ebb

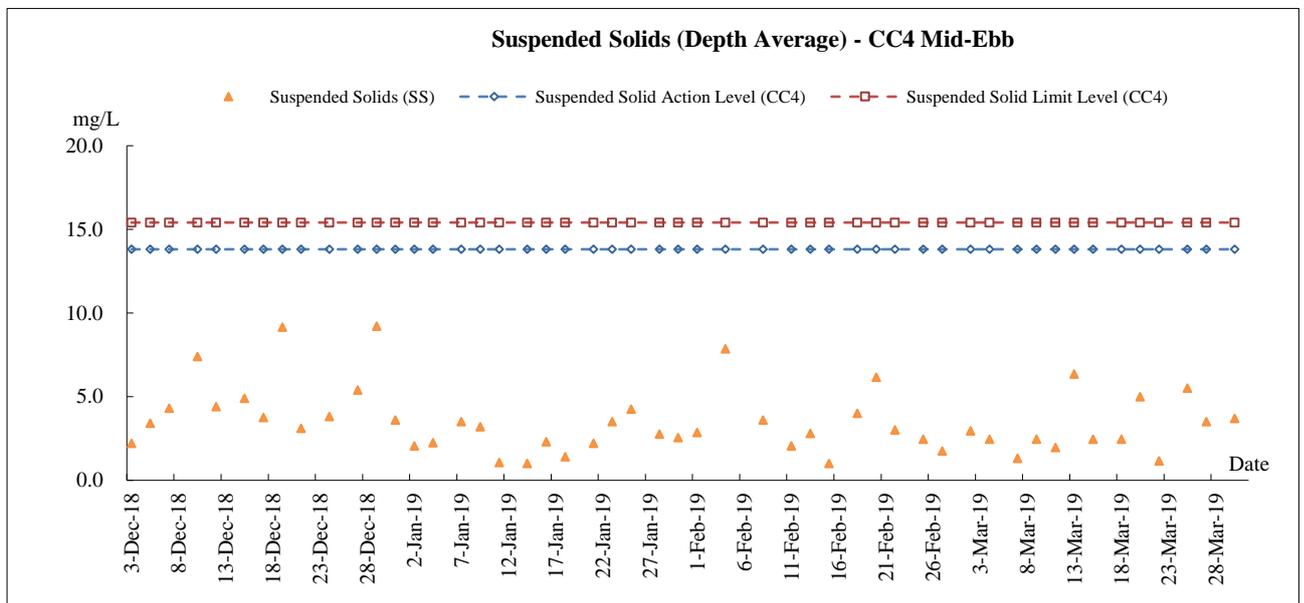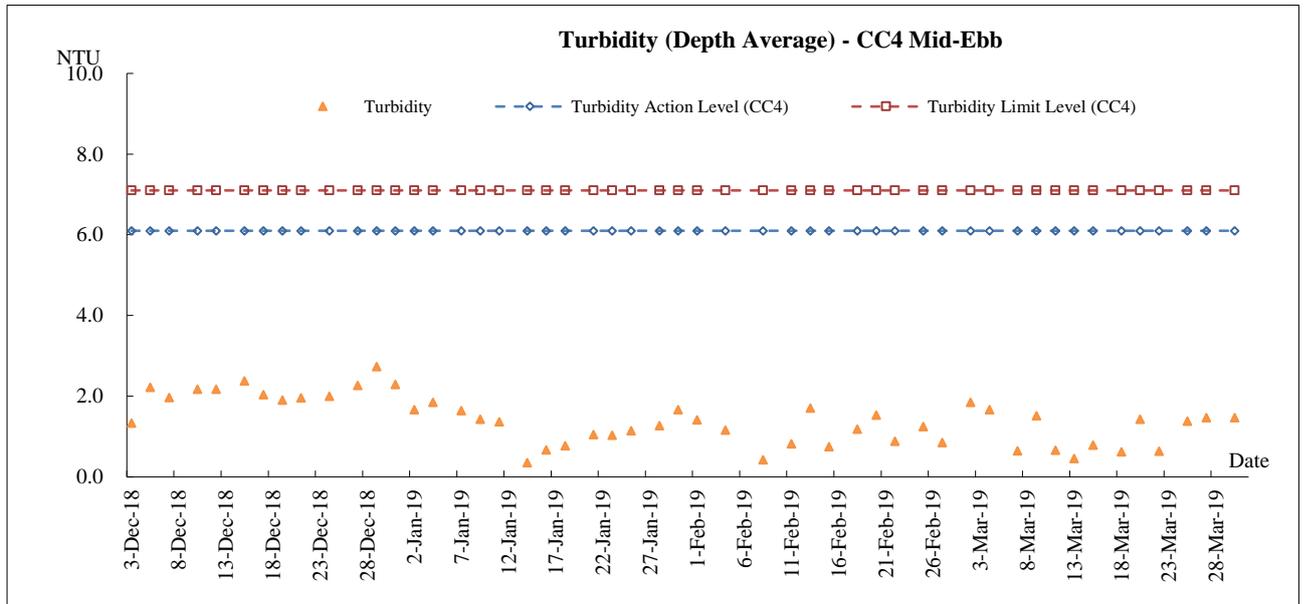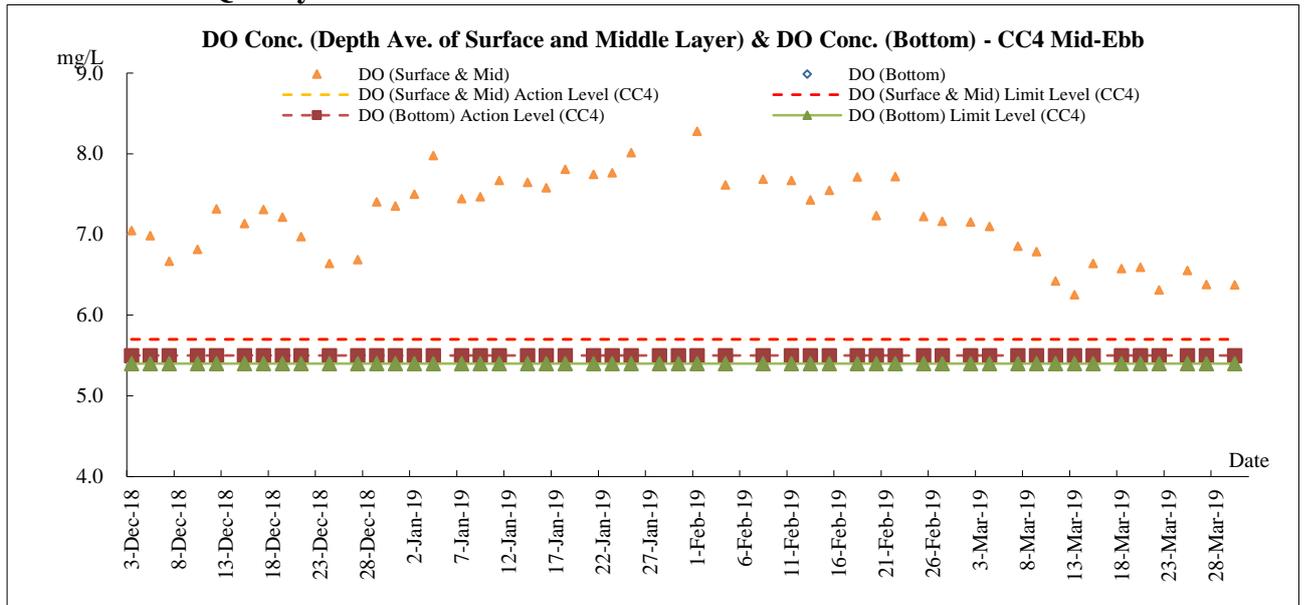




Marine Water Quality – CC13 Mid-ebb

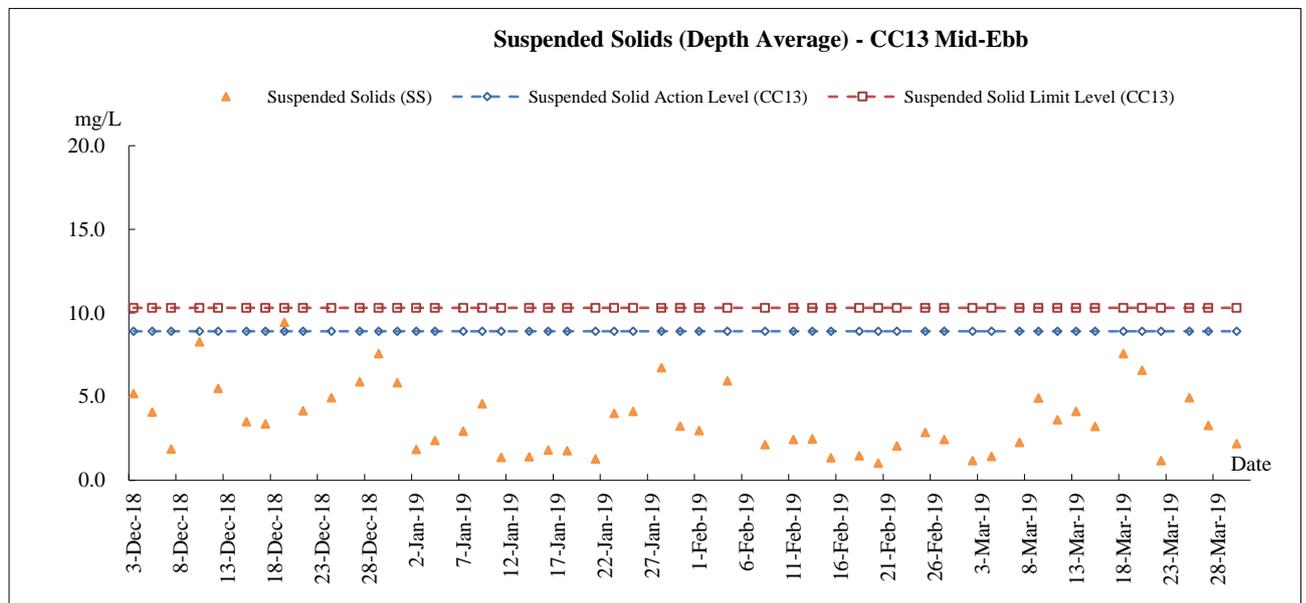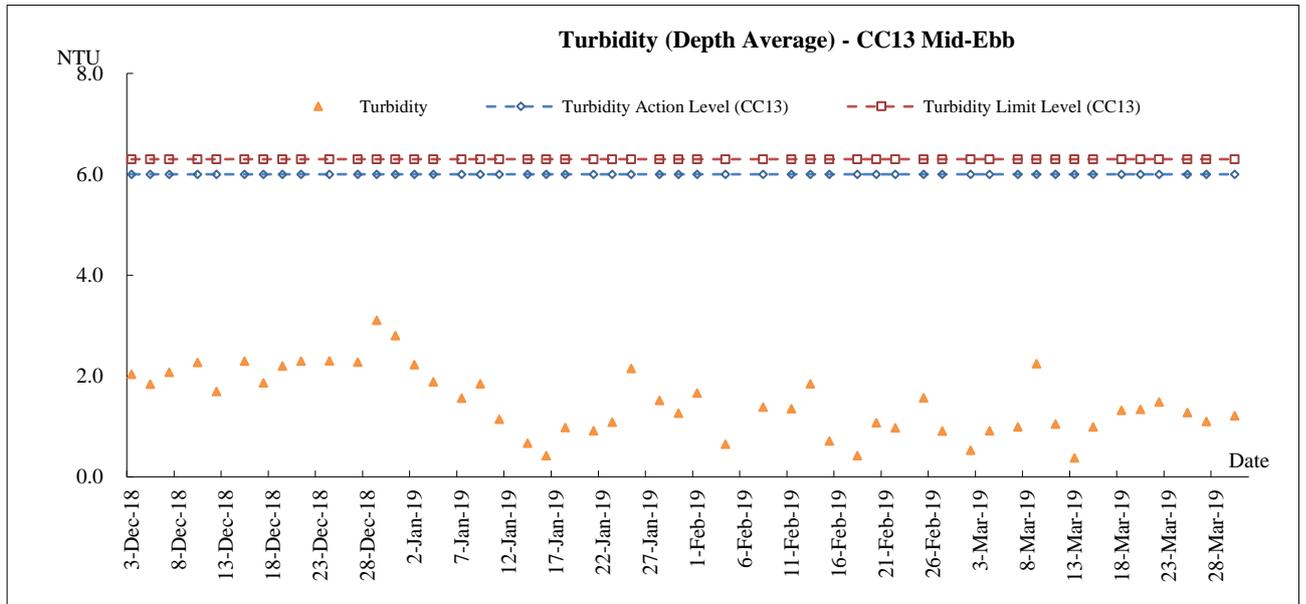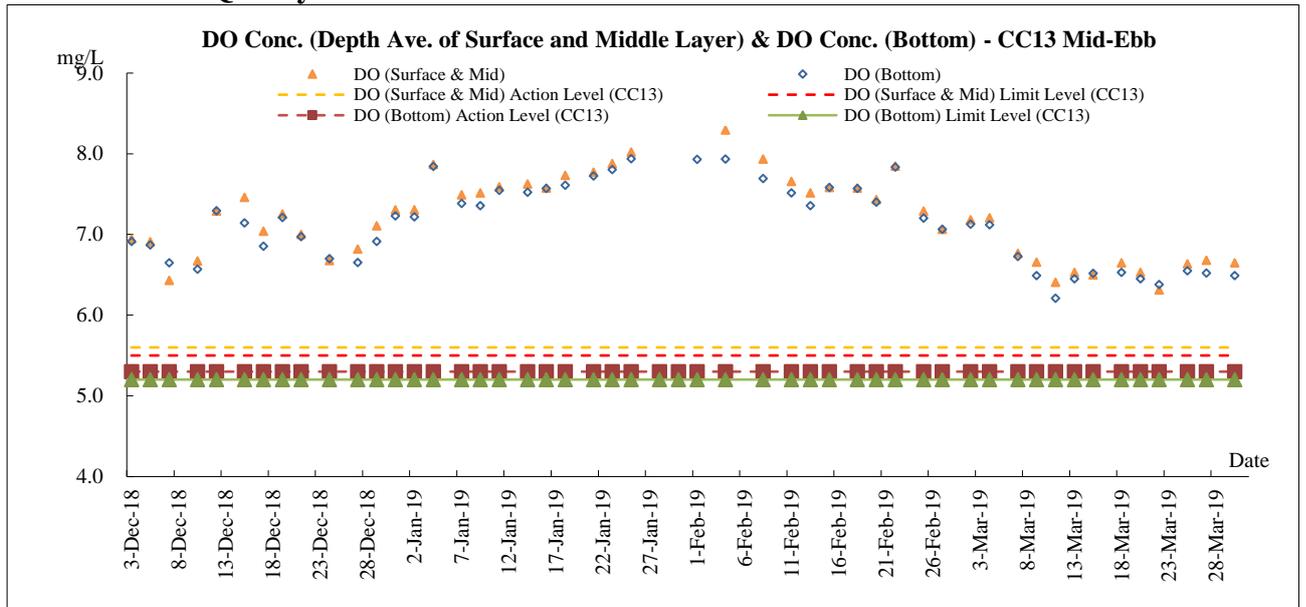




Marine Water Quality – SWI1 Mid-ebb

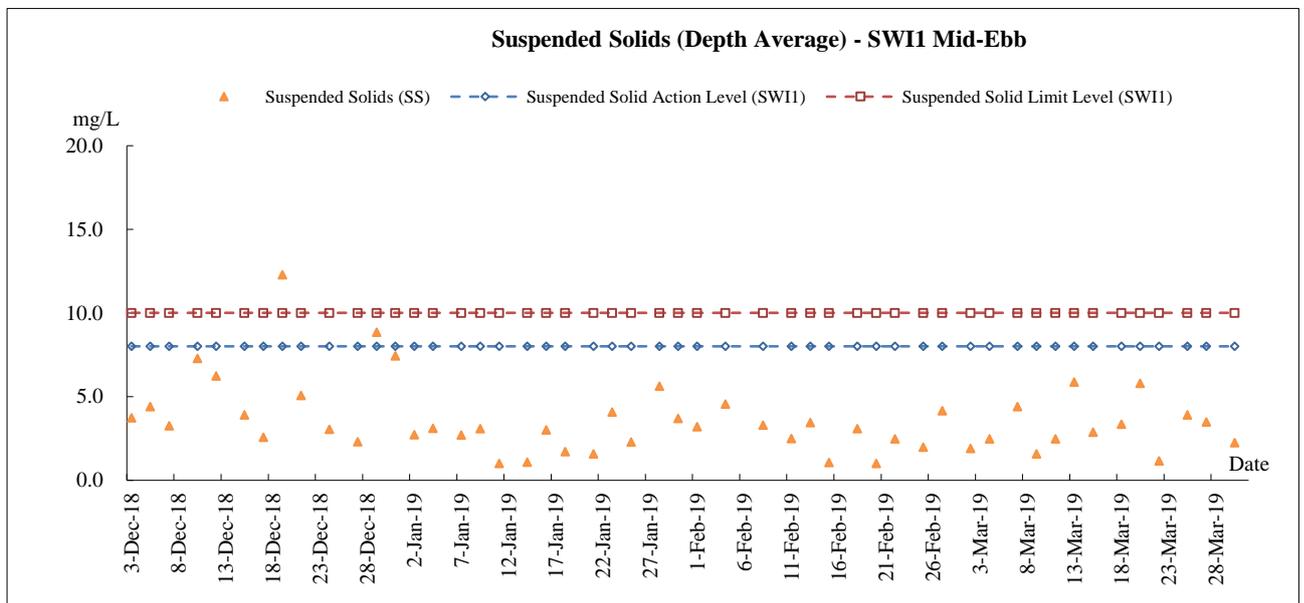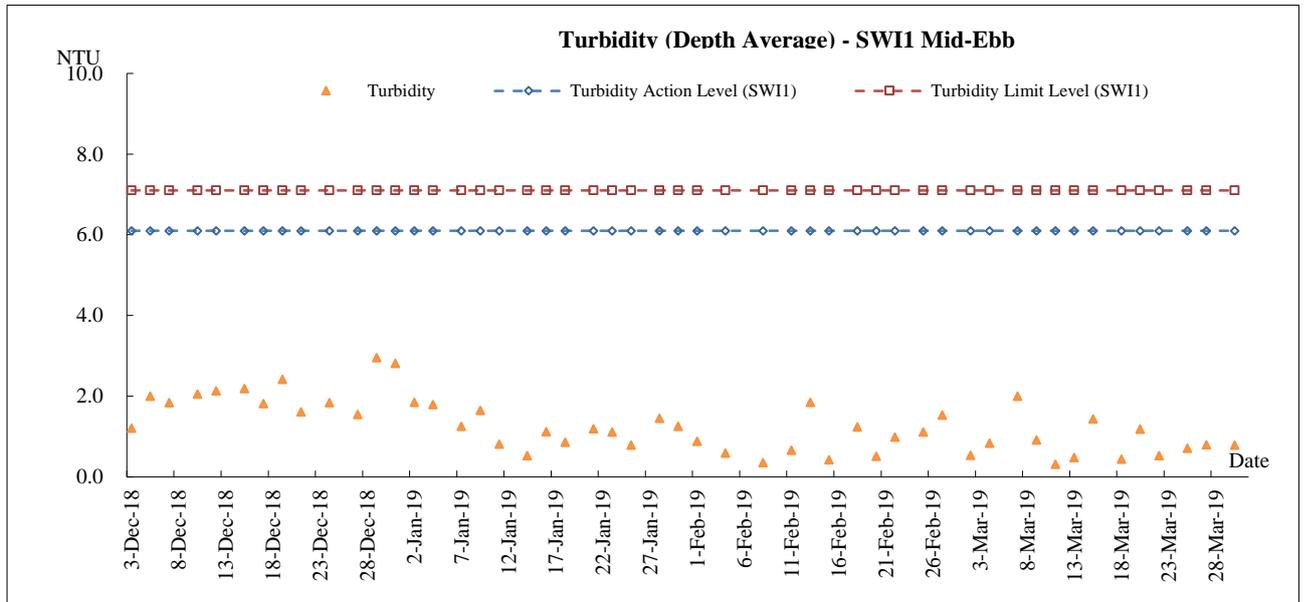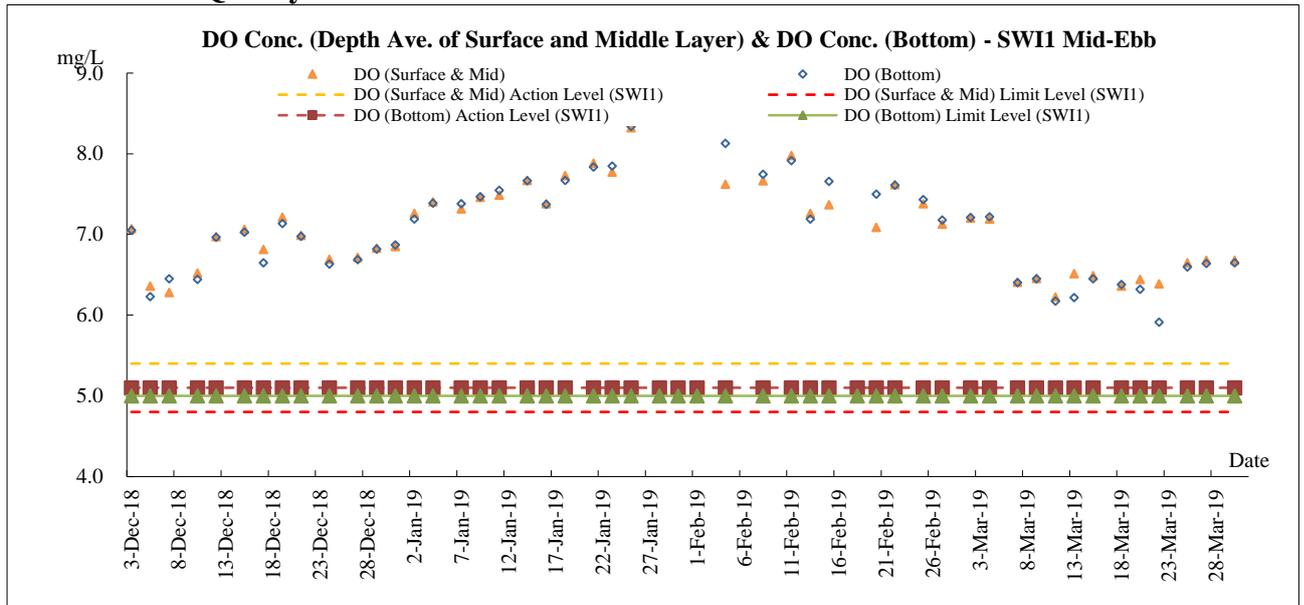




Marine Water Quality – CC1 Mid-Flood

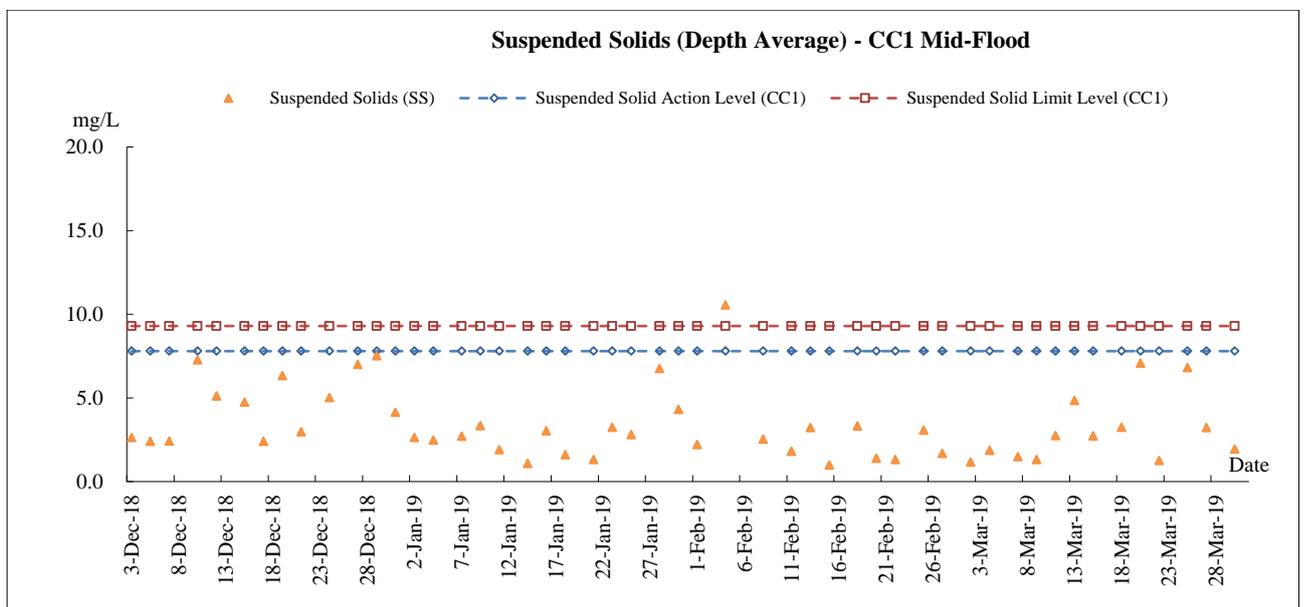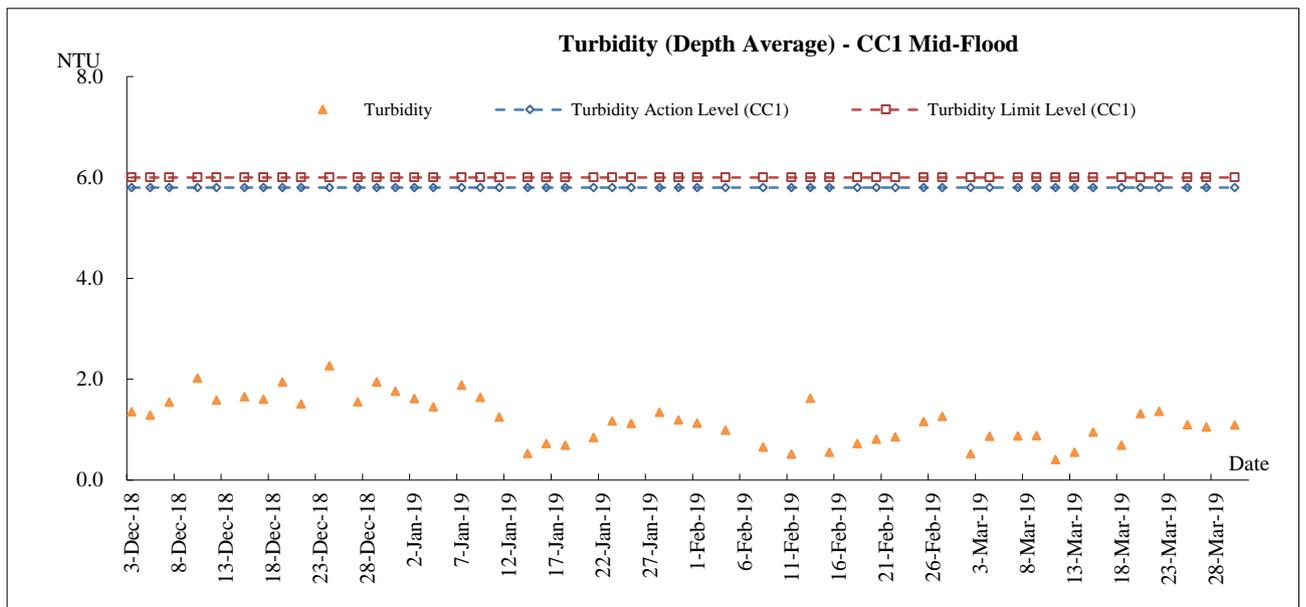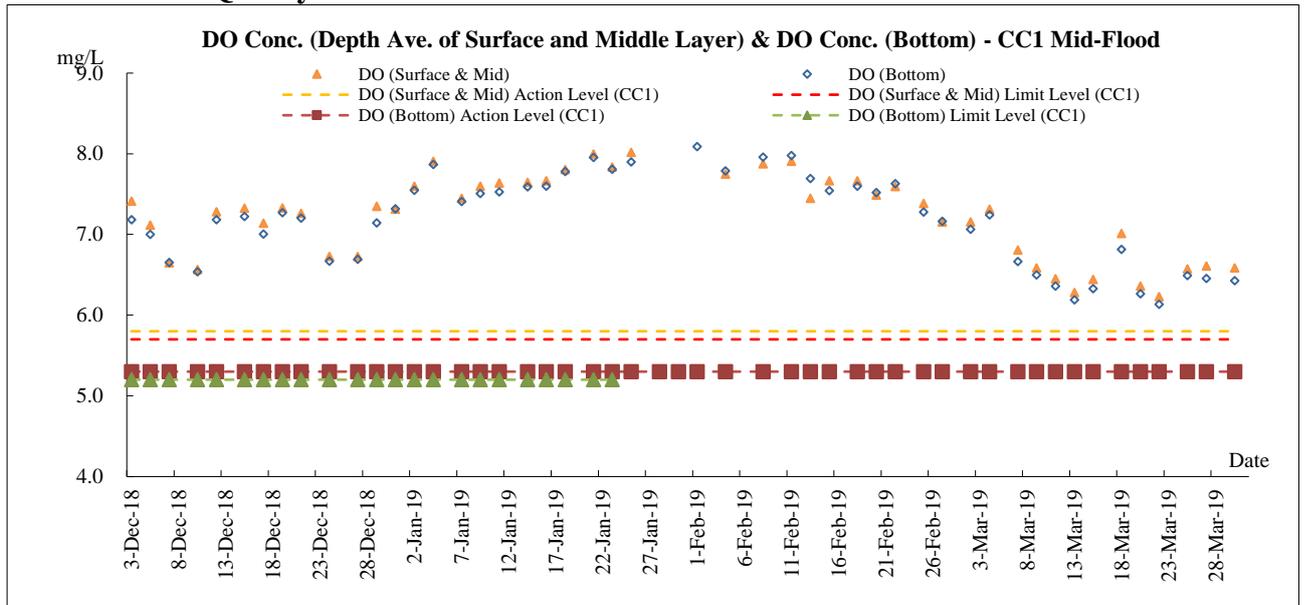




Marine Water Quality – CC2 Mid-Flood

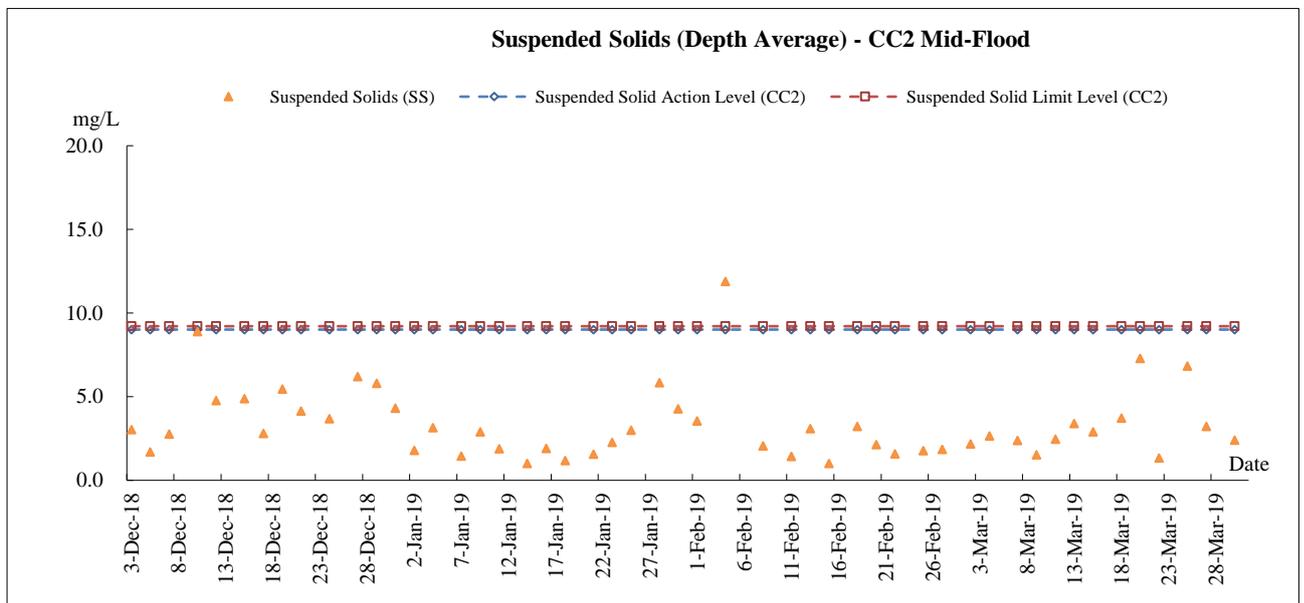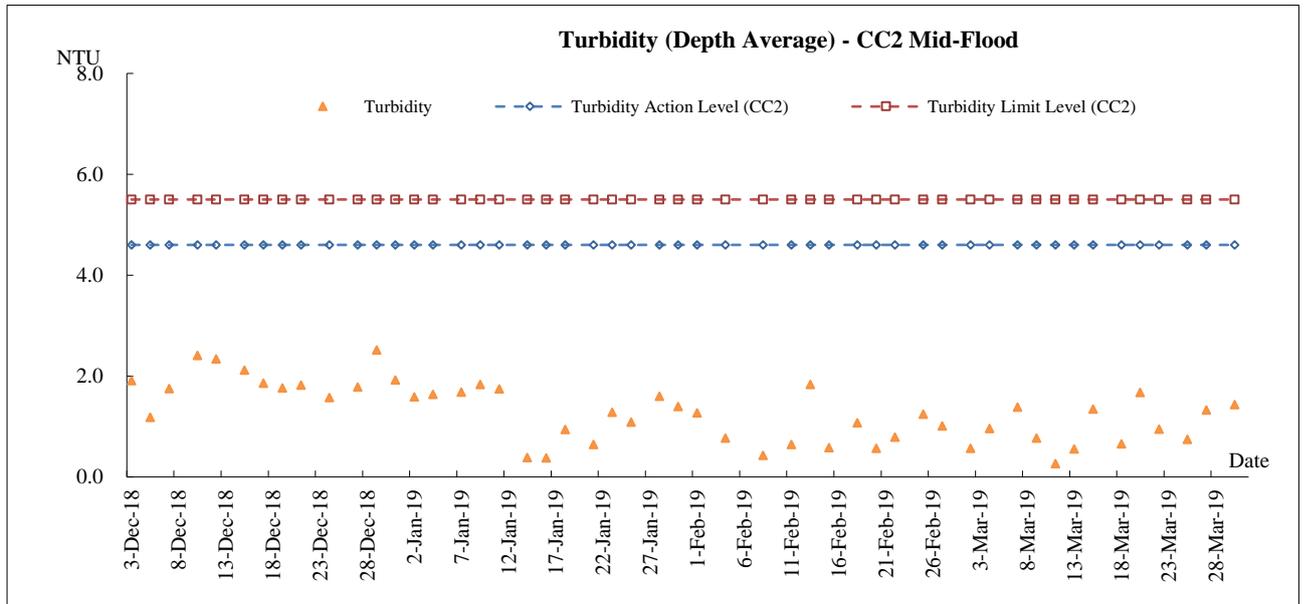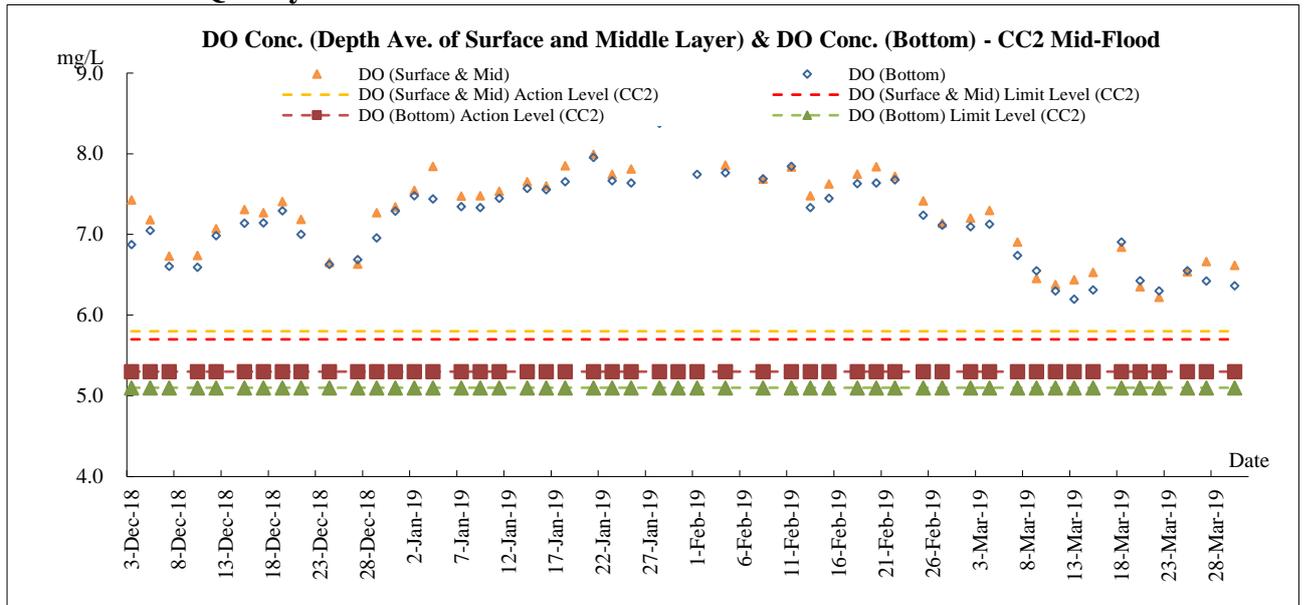




Marine Water Quality – CC3 Mid-Flood

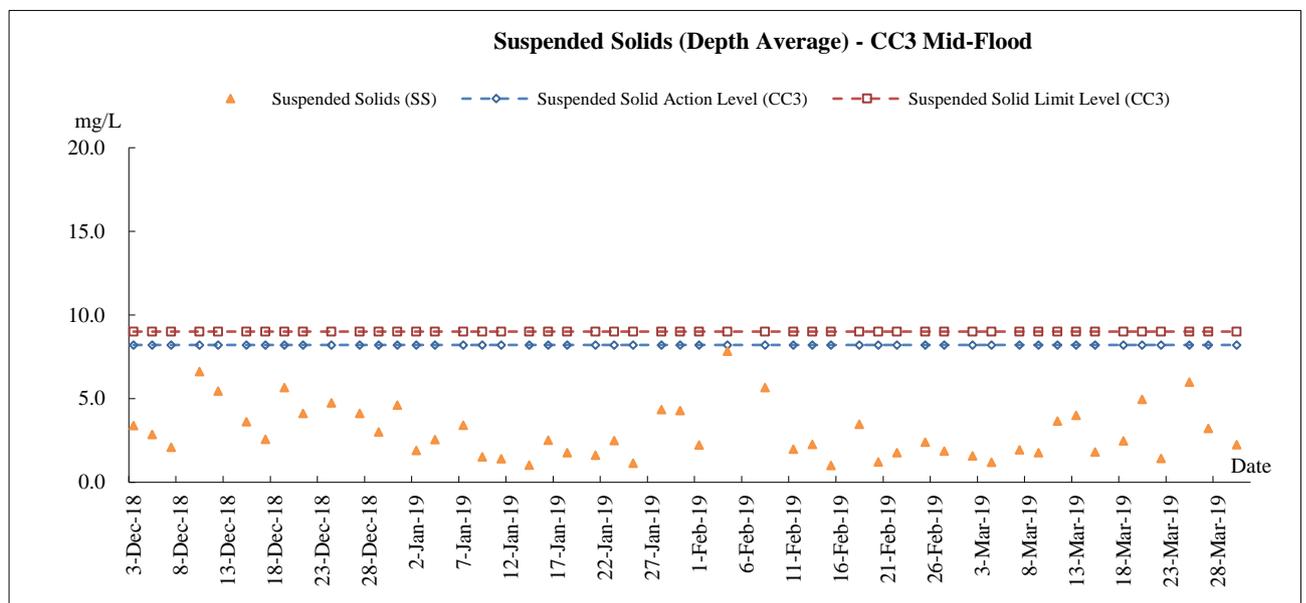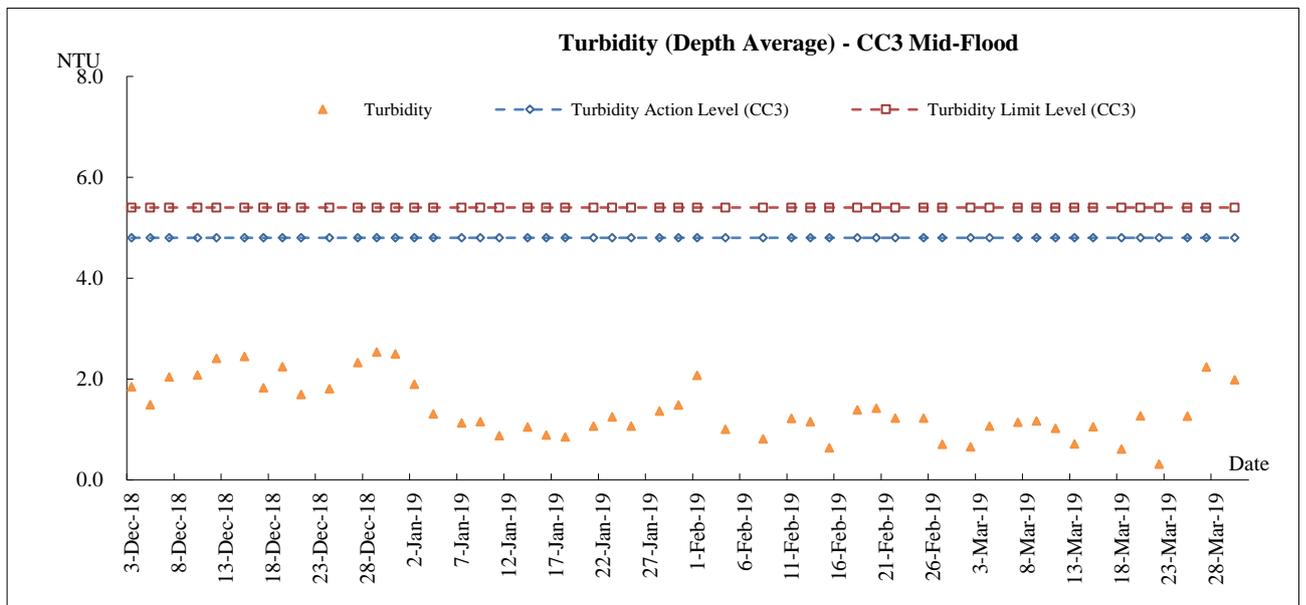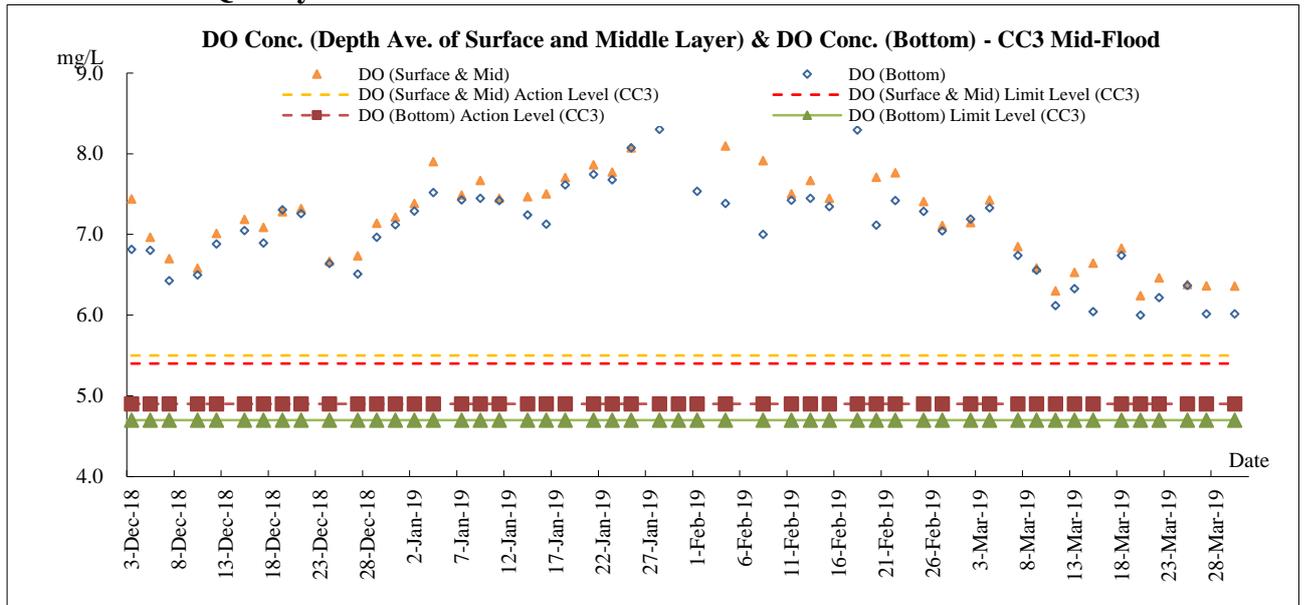




Marine Water Quality – CC4 Mid-Flood

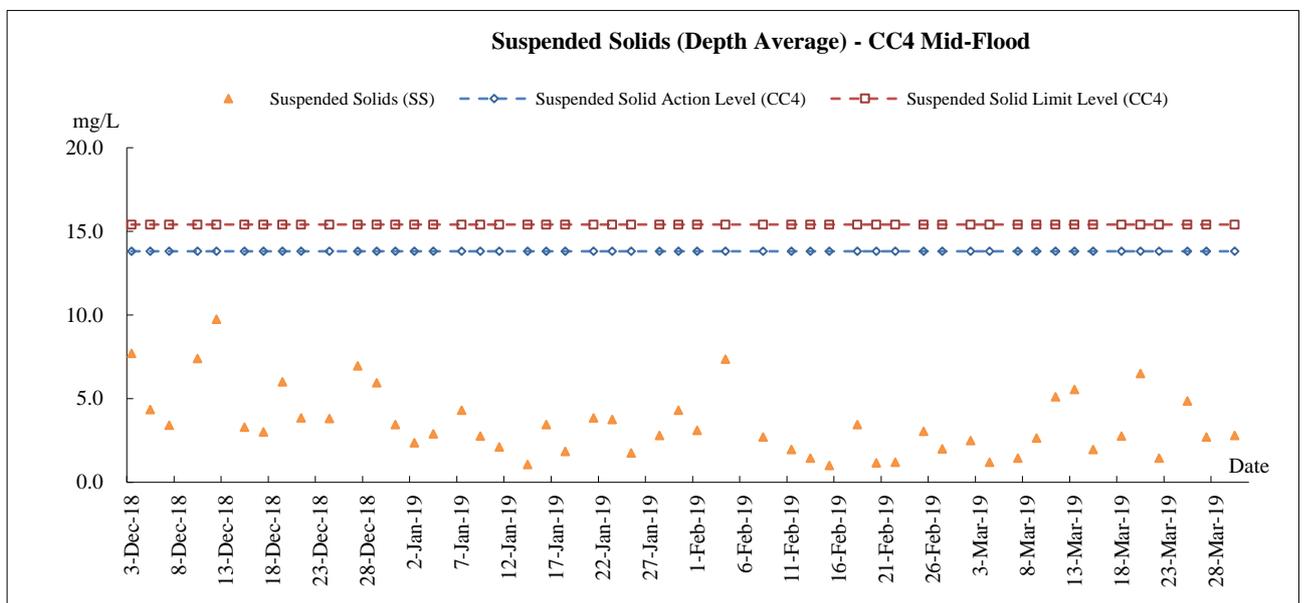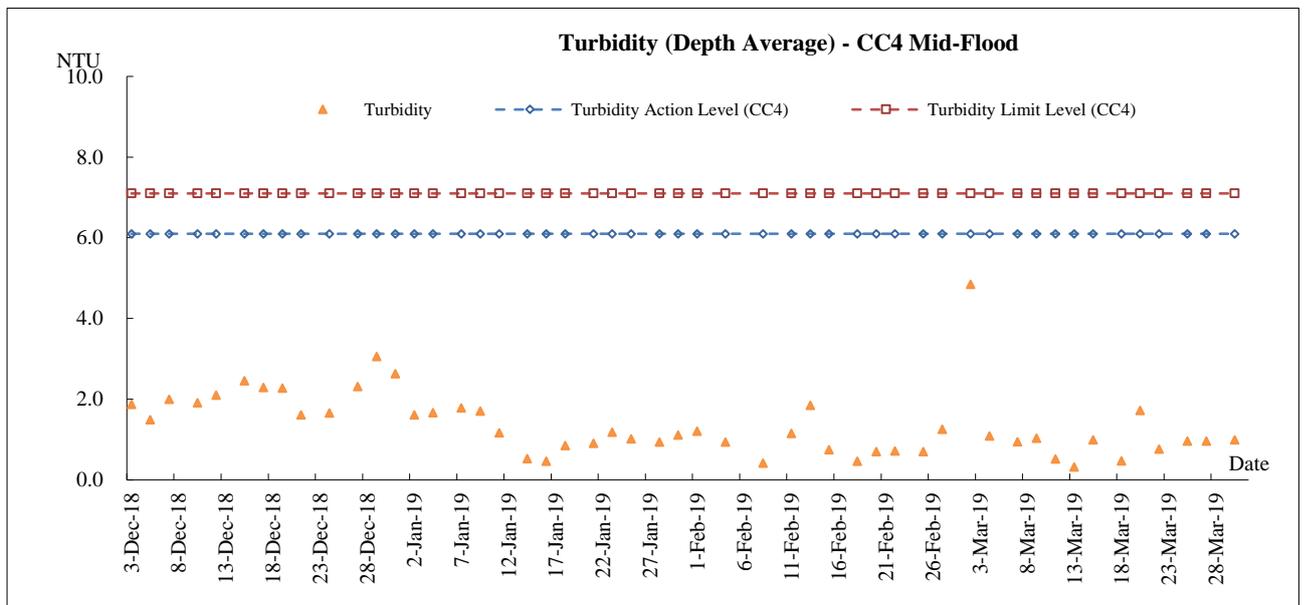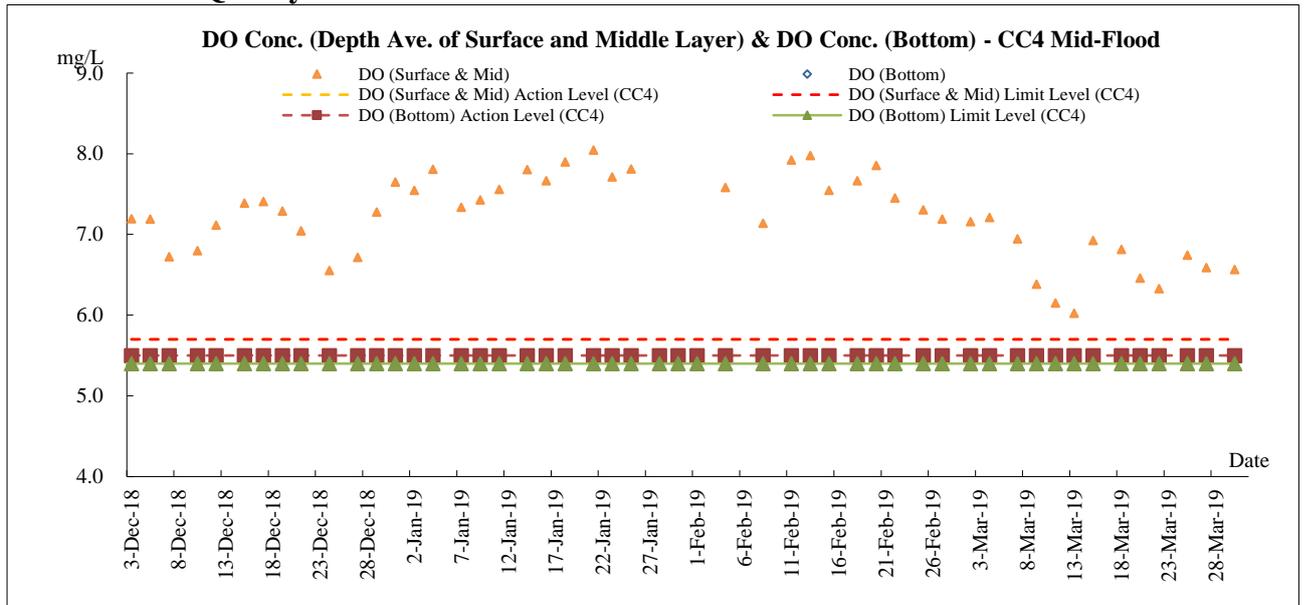

Marine Water Quality – CC13 Mid-Flood

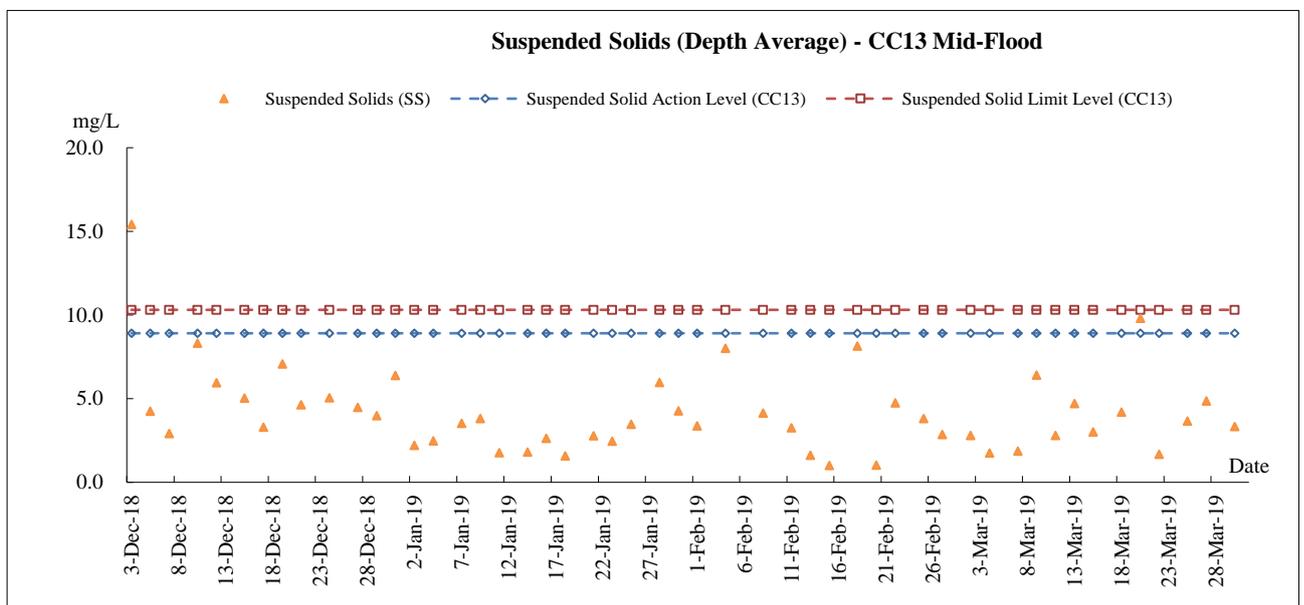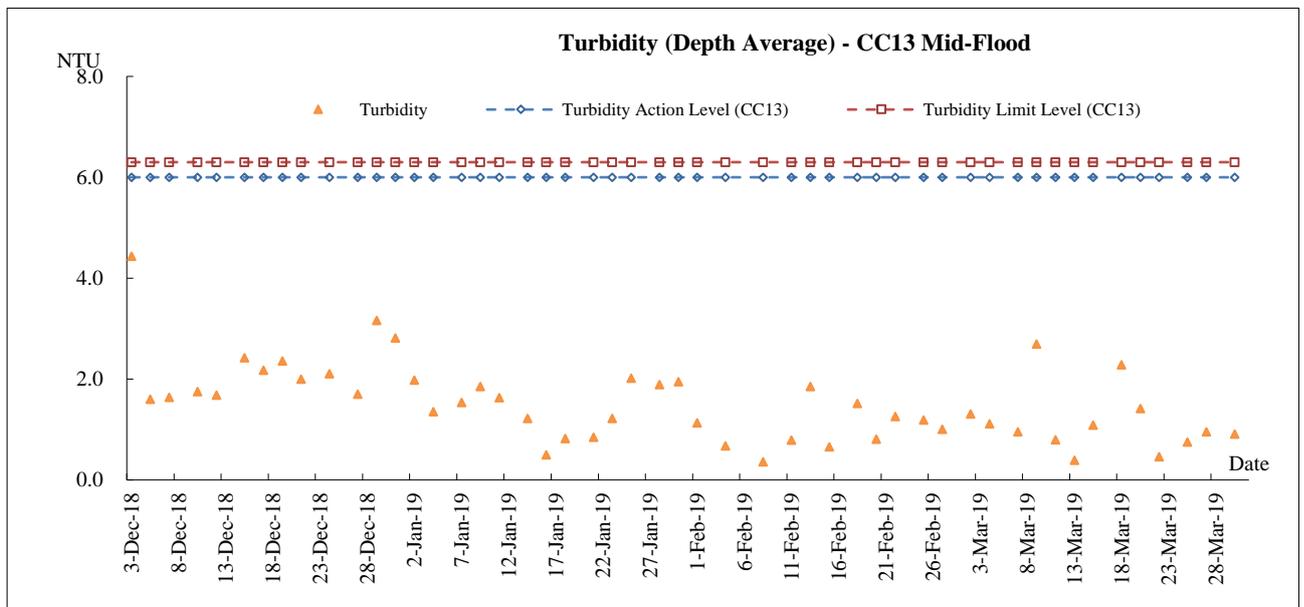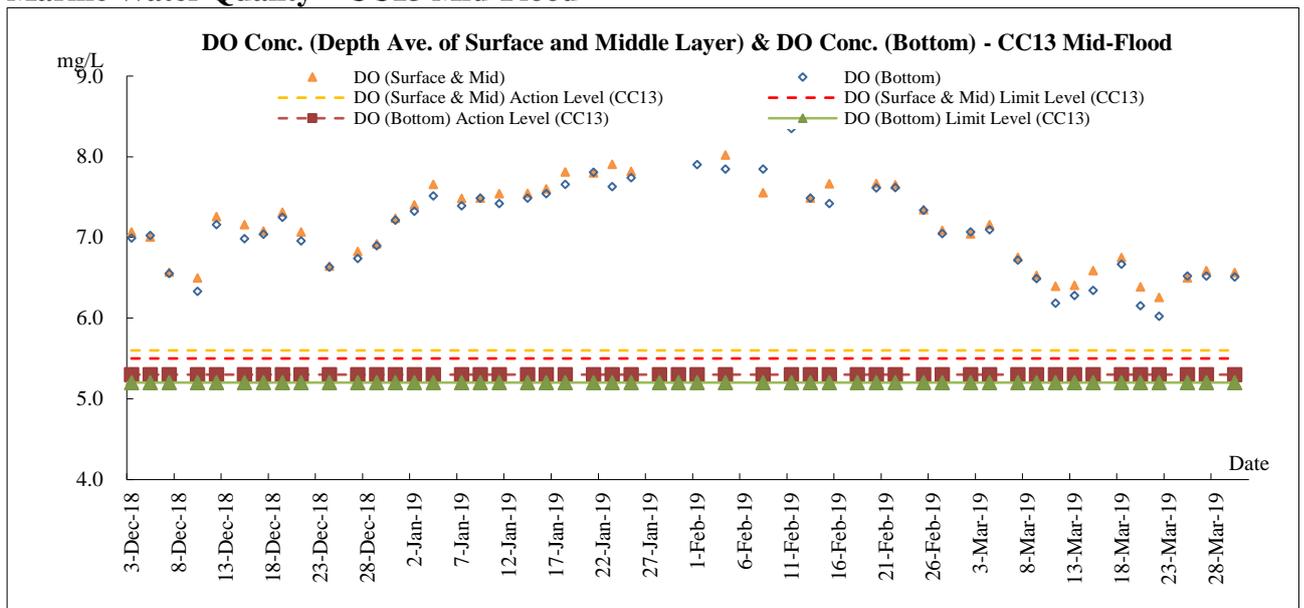

Marine Water Quality – SWI1 Mid-Flood

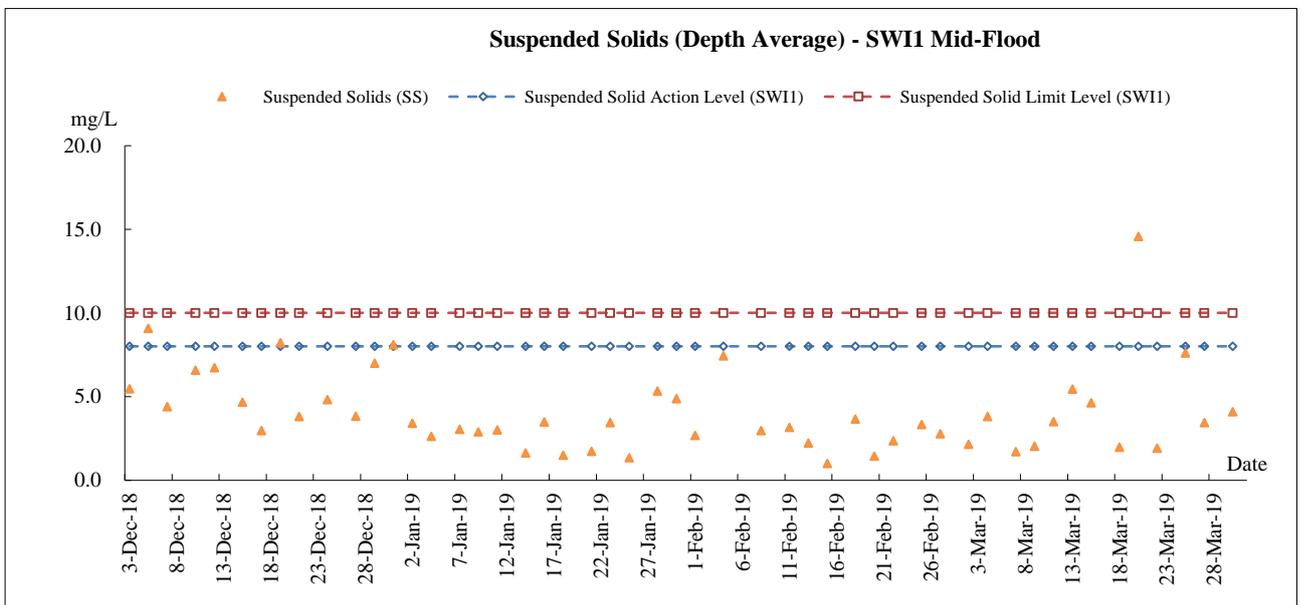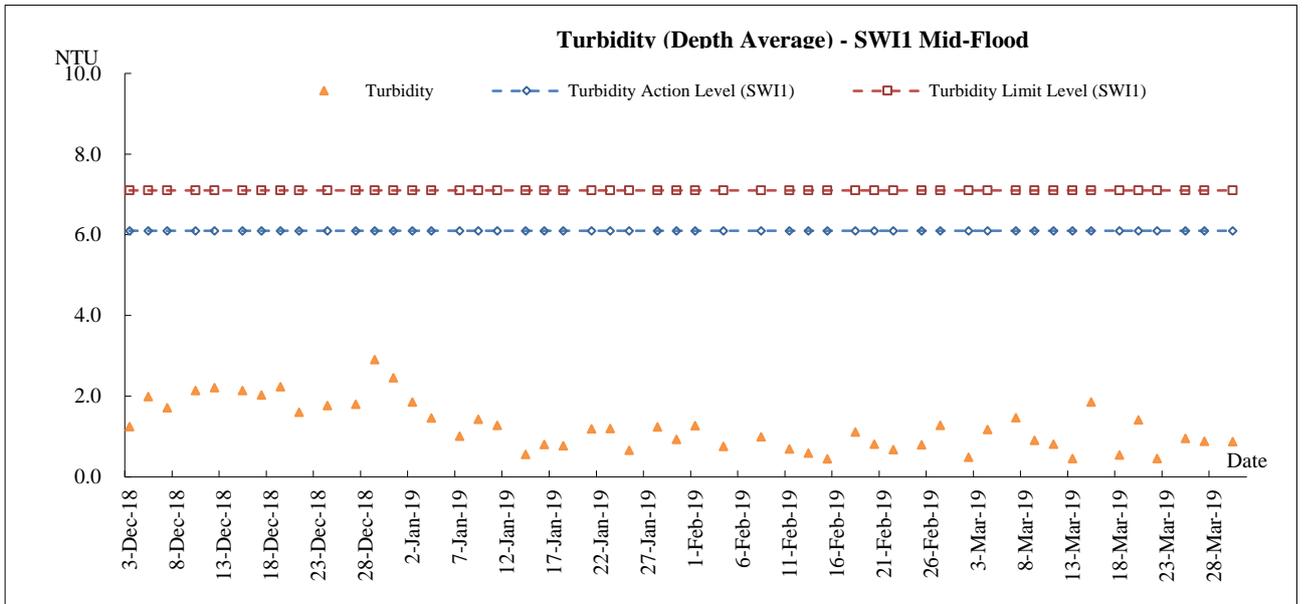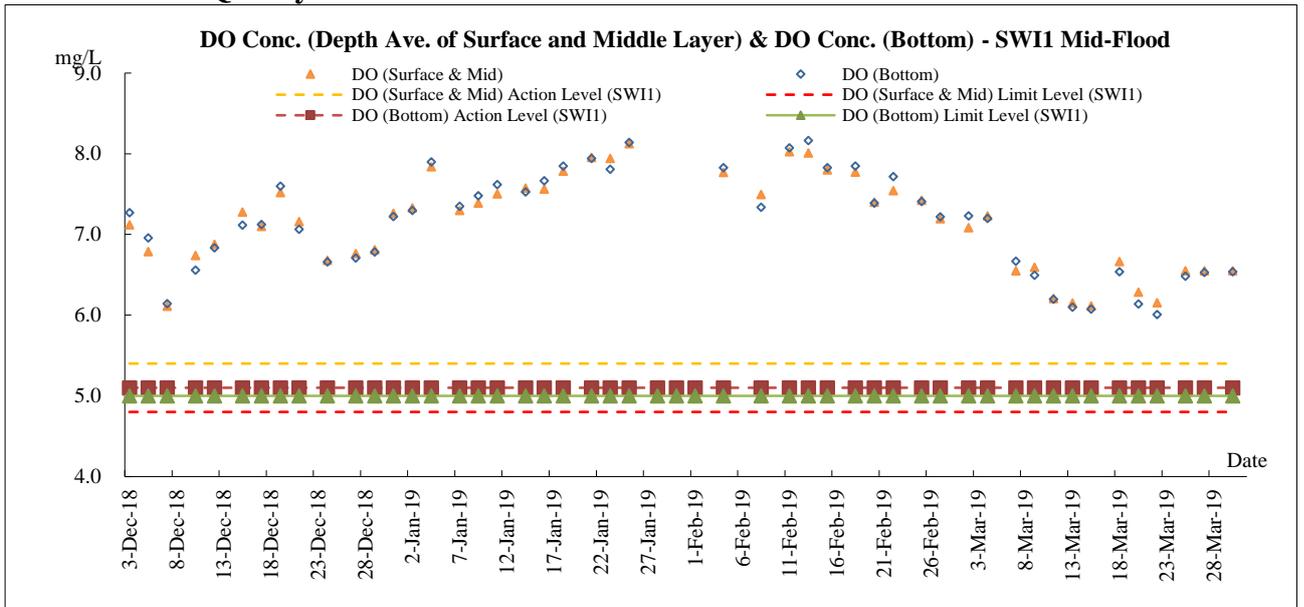

Appendix J

Meteorological Data

Date		Weather	Total Rainfall (mm)	Tseung Kwan O Station			
				Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction (degree)
1-Mar-19	Fri	Moderate southeasterly winds, occasionally strong on high ground.	0.4	20.3	8.4	89	N/NE
2-Mar-19	Sat	Mainly cloudy with one or two showers.	Trace	20.4	6.6	87.7	N/NE
3-Mar-19	Sun	Moderate southeasterly winds, occasionally strong on high ground.	6.3	20.9	9.2	82.5	NW
4-Mar-19	Mon	Mainly cloudy with one or two showers.	10.2	19.6	6.5	82	E/NE
5-Mar-19	Tue	Moderate to fresh east to northeasterly winds.	30.3	21	6.7	90	S/SW
6-Mar-19	Wed	Slightly cooler. Moderate to fresh east to northeasterly winds	45.5	19.6	8.3	93.5	N
7-Mar-19	Thu	Cloudy with occasional showers.	29.6	17	9.5	92.5	N/NE
8-Mar-19	Fri	Mainly cloudy with one or two showers.	11.5	15.5	8.1	91.2	N/NE
9-Mar-19	Sat	Moderate to fresh east to northeasterly winds.	14.5	17.1	5.5	97.5	E/NE
10-Mar-19	Sun	Slightly cooler. Moderate to fresh east to northeasterly winds	4.6	11.9	5.4	91.5	E/NE
11-Mar-19	Mon	Cloudy with occasional showers.	7.6	18.4	5.7	90	E/NE
12-Mar-19	Tue	Fine. Dry in the afternoon. Moderate east to northeasterly winds.	0	18.8	7.3	77	E/NE
13-Mar-19	Wed	Mainly cloudy with a few showers. More showers later tomorrow.	0	19.5	6.9	70	N/NE
14-Mar-19	Thu	Mainly cloudy. One or two light rain patches at first.	6.4	20	8	79.7	N/NE
15-Mar-19	Fri	Moderate to fresh east to northeasterly winds, occasionally strong offshore overnight.	0.4	17.4	8.5	86.2	E/NE
16-Mar-19	Sat	Mainly cloudy with one or two showers.	0	19.5	8	64.7	N/NE
17-Mar-19	Sun	Moderate to fresh east to northeasterly winds.	0	20.2	5.5	80	N/NE
18-Mar-19	Mon	Coastal mist tonight. Light to moderate southerly winds.	0	20.9	6.9	81.5	E/NE
19-Mar-19	Tue	Sunny periods. Warm during the day.	0	22.9	5.6	78.5	S/SE
20-Mar-19	Wed	Mist patches in the morning. Moderate southeasterly winds.	0	22.2	6.5	90.5	N/NE
21-Mar-19	Thu	Warm with sunny periods.	0	24.3	5.6	83	S
22-Mar-19	Fri	Mainly cloudy. Coastal fog in the morning	Trace	24.9	5.6	86.5	S
23-Mar-19	Sat	Sunny periods. Warm during the day.	3.3	19	7.5	90.1	N/NE
24-Mar-19	Sun	Mainly cloudy. Coastal fog in the morning	0.3	16.2	8.3	50.2	E/NE
25-Mar-19	Mon	Moderate south to southeasterly winds.	1	20	6.1	84.5	E/NE
26-Mar-19	Tue	Moderate south to southeasterly winds.	0	21.1	7	86.7	N/NE
27-Mar-19	Wed	Warm with sunny periods during the day.	Trace	22	6.1	81.2	N/NE
28-Mar-19	Thu	Mainly cloudy. A few showers tomorrow.	0	23.9	4.6	84.2	S
29-Mar-19	Fri	Mainly cloudy with a few showers. Isolated thunderstorms tonight.	6.9	24.8	7.5	80.7	S/SW
30-Mar-19	Sat	Fresh east to northeasterly winds, strong offshore and on high ground.	Trace	21.5	7.5	90.5	N/NE
31-Mar-19	Sun	Cloudy with a few rain patches.	7.7	20.9	8.5	95	NE

Appendix K
Waste Flow Table

Contract 1

Monthly Summary Waste Flow Table for 2018 (year)

Name of Person completing the record: Kanny Cho (EO)

Project : Cross Bay Link, TKO, Main Bridge and Associated Works

Contract No.: NE/2017/07

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m ³)
Jan	/										
Feb											
Mar											
Apr											
May											
Jun											
Sub-total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jul	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.837
Sep	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.305
Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.065	0.000	0.000	0.008
Nov	0.000	0.000	0.000	0.000	0.000	0.320	0.000	0.000	0.000	0.000	0.009
Dec	0.000	0.000	0.000	0.000	0.276	0.000	0.000	0.000	0.000	0.000	0.004
Total	0.000	0.000	0.000	0.000	0.276	0.320	0.000	0.065	0.000	0.000	1.163

Note:

1. For non-inert portion of C&D material, assume the density of 1 m³ general refuse is equal to 200 kg.
2. For inert portion of C&D material, assume 6 m³ per each full-filled dump truck.
3. All values are round off to the third decimal places.

Monthly Summary Waste Flow Table for 2019 (year)

Name of Person completing the record: Calvin So (EO)

Project : Cross Bay Link, TKO, Main Bridge and Associated Works

Contract No.: NE/2017/07

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 m ³)
Jan	0.845	0.000	0.000	0.000	0.845	0.000	0.000	0.023	0.000	0.000	0.077
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.032	0.000	0.000	0.036
Mar	0.042	0.000	0.000	0.000	0.042	0.000	0.000	0.029	0.000	0.000	0.081
Apr											
May											
Jun											
Sub-total	0.887	0.000	0.000	0.000	0.887	0.000	0.000	0.084	0.000	0.000	0.194
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	0.887	0.000	0.000	0.000	0.887	0.000	0.000	0.084	0.000	0.000	0.194

Note:

1. For non-inert portion of C&D material, assume the density of 1 m³ general refuse is equal to 200 kg.
2. For inert portion of C&D material, assume 6 m³ per each full-filled dump truck.
3. All values are round off to the third decimal places.

Contract 2

Monthly Summary Waste Flow Table for 2019 Year

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Borken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics (See note 3)	Chemical Waste	Other, e.g. general refuse
	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000m ³]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in '000m ³]
Jan	0.358	0.000	0.358	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.357
Feb	0.022	0.000	0.000	0.000	0.022	0.000	0.000	0.000	0.000	0.000	0.728
Mar	0.042	0.000	0.000	0.000	0.042	0.000	0.000	0.000	0.000	0.000	0.229
Apr											
May											
June											
SUB-TOTAL	0.421	0.000	0.358	0.000	0.063	0.000	0.000	0.000	0.000	0.000	1.313
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
TOTAL	0.421	0.000	0.358	0.000	0.063	0.000	0.000	0.000	0.000	0.000	1.313

Note: Conversion to 1000m³ for general refuse is weight in 1000kg multiply by 0.002

Conversion to 1000m³ for Inert C&D is weight in 1000kg multiply by 0.0005

Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material

Plastics refer to plastic bottles / containers, plastic sheets / foam from packaging material

Assume the loaded volume of a dump truck for internal inert waste transfer is 17.9 m³

Appendix L

**Implementation Schedule for
Environmental Mitigation Measures**

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
Dust Impact (Contraction Phase)						
S5.5.5.1	Regular watering under good site practice shall be adopted. In accordance with the “Control of Open Fugitive Dust Sources” (USEPA AP-42), watering once per hour on exposed worksites and haul road is recommended to achieve dust removal efficiency of 91.7%.	Good construction site practices to control the dust impact on the nearby sensitive receivers to within the relevant criteria	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • APCO (Cap. 311); and • Air Pollution Control (Construction Dust) Regulation
S5.5.5.3	<p>The following dust suppression measures shall also be incorporated by the Contractor to control the dust nuisance throughout the construction phase:</p> <ul style="list-style-type: none"> • Any excavated or stockpiled dusty material shall be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; • Any dusty materials remaining after a stockpile is removed shall be wetted with water and cleared from the surface of roads; • A stockpile of dusty material shall not extend beyond the pedestrian barriers, fencing or traffic cones; • The load of dusty materials on a vehicle leaving a construction site shall be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle; • Where practicable, vehicle washing facilities with high pressure water jet shall be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point shall be paved with concrete, bituminous materials or hardcores; • When there are open excavation and reinstatement works, hoarding of not less than 2.4m high shall be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; • The portion of any road leading to the construction site that is within 30m of a vehicle entrance or exit shall be kept clear 	Good construction site practices to control the dust impact on the nearby sensitive receivers to within the relevant criteria	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • APCO (Cap. 311); and • Air Pollution Control (Construction Dust) Regulation

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	of dusty materials; <ul style="list-style-type: none"> Surfaces where any pneumatic or power driven drilling, cutting, polishing or other mechanical breaking operation takes place shall be sprayed with water or a dust suppression chemical continuously; Any area that involves demolition activities shall be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting shall be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; Any skip hoist for material transport shall be totally enclosed by impervious sheeting; Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies. 					
S5.5.5.4	For the barging facilities at the site compound, the following good site practice is required: <ul style="list-style-type: none"> All road surfaces within the barging facilities shall be paved. Vehicles should pass through designated wheel wash facilities. Continuous water spray shall be installed at the loading point. 	Good construction site practices to control the dust impact on the nearby sensitive receivers to within the relevant criteria	Site compound	Contractor	Construction stage	<ul style="list-style-type: none"> APCO (Cap. 311); and Air Pollution Control (Construction Dust) Regulation
S5.5.5.5	An audit and monitoring programme during the construction phase should be implemented by the Contractor to ensure that the construction dust impacts are controlled to within the HKAQO. Detailed requirements for the audit and monitoring programmes are given separately in the EM&A manual.	Monitor the 1-Hour and 24-Hr TSP levels at the representative dust monitoring stations to ensure compliance with relevant criteria throughout the construction period	Selected representative dust monitoring station (Drawing no. 209506/EMA/AIR/001)	Contractor	Construction stage	<ul style="list-style-type: none"> APCO (Cap. 311); and Air Pollution Control (Construction Dust) Regulation
Noise Impact (Contraction Phase)						

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
S6.6.4.3	Good site practice and noise management techniques: <ul style="list-style-type: none"> • Only well-maintained plant shall be operated on-site and the plant shall be serviced regularly during the construction programme; • Machines and plant (such as trucks, cranes) that are in intermittent use shall be shut down between work periods or throttled down to a minimum; • Plant known to emit noise strongly in one direction, where possible, shall be orientated so that the noise is directed away from nearby NSRs; • Silencers or mufflers on construction equipment shall be properly fitted and maintained during the construction works; • Mobile plant shall be sited as far away from NSRs as possible and practicable; and • Material stockpiles, site office and other structures shall be effectively utilised, where practicable, to screen noise from on-site construction activities. 	To minimize construction noise impact arising from the Project on the affected NSRs	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Annex 5, TM-EIAO
S6.6.4.5-6	Use of quiet powered mechanical equipment and working methods	Reduce noise levels of plant items	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Annex 5, TM-EIAO
S6.6.4.7	Install site hoarding at the site boundaries between noisy construction activities and NSRs	Reduce the construction noise levels at low-level zone of NSRs through partial screening	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Annex 5, TM-EIAO
S6.6.4.8-11	Use of temporary or movable noise barriers and full enclosure for relatively fixed plant source	Screen the noisy plant items to be used at all construction sites	For plant items listed in Table 6.7 and Appendix 6.1 of the EIA report at all construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Annex 5, TM-EIAO
	Implement a noise monitoring programme under the EM&A manual	Monitor the construction noise levels at the selected representative locations	Selected representative noise monitoring stations (Drawing no. 209506/EMA/NS/001 & 209506/EMA/NS/002)	Contractor	Construction stage	<ul style="list-style-type: none"> • Annex 5, TM-EIAO
S6.7.3.1	Partial enclosures along Road D9 and application of low noise surfacing material along CBL and Road D9	To minimize road traffic noise impact arising from the CBL and Road D9 on the affected NSRs	CBL and Road D9 (Drawing no. 209506/EMA/NS/003)	CEDD/ Contractor	During operational stage	<ul style="list-style-type: none"> • Annex 5, TM-EIAO

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
Water Quality Impact (Contraction Phase)						
S8.6.4.3	<p>Marine Piling and Pile Excavation Works Marine piling and pile excavation works shall be undertaken in such a manner as to minimize re-suspension of sediments. Standard good practice measures shall be implemented, including the following requirements:</p> <ul style="list-style-type: none"> • All marine piling and pile excavation works shall be conducted within a floating single silt curtain. • Mechanical closed grabs (with a size of 5m³) shall be designed and maintained to avoid spillage and should seal tightly while being lifted. • Barges shall have tight fitting seals to their bottom openings to prevent leakage of material. • Any pipe leakages shall be repaired quickly. Plant should not be operated with leaking pipes. • Loading of barges shall be controlled to prevent splashing of dredged material to the surrounding water. Barges shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation. • Excess material shall be cleaned from the decks and exposed fittings of barges before the vessel is moved. • Adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action. • All vessels shall be sized such that adequate clearance is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. • The works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site. 	To control potential impacts from marine piling and pile excavation works	During marine piling and pile excavation works	Contractor	Construction stage	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO
S8.6.4.4	<p>Construction Site Runoff</p> <p>In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994 (ProPECC PN 1/94), construction phase mitigation measures, where appropriate, shall include the following:</p> <ul style="list-style-type: none"> • The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The 	Control potential water quality impacts from construction site run-off	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	<p>detailed design of the sand/silt traps shall be undertaken by the contractor prior to the commencement of construction;</p> <ul style="list-style-type: none"> Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ shall be covered with tarpaulin or similar fabric during rainstorms. Measures shall be taken to prevent the washing away of construction materials, soil, silt or debris into any marine water bodies; All vehicles and plant shall be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities shall be provided at every construction site exit where practicable. Wash-water shall have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road shall be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains; Construction solid waste, debris and rubbish on site shall be collected, handled and disposed of properly to avoid water quality impacts; All fuel tanks and storage areas shall be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby; and Regular environmental audit on the construction site shall be carried out in order to prevent any malpractices. Notices shall be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the meander, wetlands and fish ponds. 					
S8.6.4.6	<p>Sewage from workforce</p> <ul style="list-style-type: none"> Portable chemical toilets and sewage holding tanks shall be provided for handling the construction sewage generated by the workforce; A licensed contractor shall be employed to provide 	Control potential water quality impacts from sewage	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> TM-EIAO; and WPCO

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.					
	Monitoring Implement a marine water quality monitoring programme under the EM&A on level of suspended solids (SS) / turbidity and dissolved oxygen (DO) shall be carried out.	Control potential water quality impacts from marine piling and pile excavation works	Selected monitoring stations (Drawing no. 209506/EMA/WQ/001)	Contractor	Construction station	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO
S8.7.3.2	Operational phase – Runoff from road surface Proper drainage systems with silt traps and oil interceptors shall be installed, maintained and cleaned at regular intervals.	Control potential water quality impacts from road surface runoff	CBL and Road D9	Contractor	Construction and operational stage	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO
Waste Management (Contraction Phase)						
S9.5.2	Good Site Practices Recommendations for good site practices: <ul style="list-style-type: none"> • Nomination of an approved personnel to be responsible for the implementation of good site practices, arrangements for collection and effective deposal to an appropriate facility of all wastes generated at the site; • Training of site personnel in proper waste management and chemical handling procedures; • Provision of sufficient waste disposal points and regular collection for disposal; • Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre; • Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and • Implementation of a recording system for the amount of wastes generated/recycled and disposal sites. 	Good site practices which ensure waste generated during construction phase is properly managed	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Waste Disposal Ordinance (Cap. 54); • ETWB TCW No. 19/2005

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
S9.5.4	<p>Waste Reduction Measures Recommendations for achieving waste reduction include:</p> <ul style="list-style-type: none"> • On-site reuse of any material excavated as far as practicable; • Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal; • Collection of aluminum cans and waste paper by individual collectors during construction should be encouraged. Separately labelled recycling bins should also be provided to segregate these wastes from other general refuse by the workforce; • Recycling of any unused chemicals and those with remaining functional capacity as far as possible; • Prevention of the potential damage or contamination to the construction materials through proper storage and good site practices; • Planning and stocking of construction materials should be made carefully to minimize amount of waste generated avoid unnecessary generation of waste; and • Training on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling should be provided to workers. 	To reduce amount of waste generated during construction phase	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Waste Disposal Ordinance (Cap. 54); • ETWB TCW No. 19/2005
S9.5.5-6	<p>Storage, Collection and Transportation of Waste Recommendations for proper storage include:</p> <ul style="list-style-type: none"> • Waste such as soil should be handled and stored well to ensure secure containment; • Stockpiling area should be provided with covers and water spraying system to prevent materials from being washed away and to reduce wind-blown litter; and • Different locations should be designated to stockpile each material to enhance reuse. <p>With respect to the collection and transportation of waste from the construction works, the following is recommended:</p> <ul style="list-style-type: none"> • Remove waste in a timely manner; • Employ trucks with cover or enclosed containers for waste transportations; • Obtain relevant waste disposal permits from the appropriate 	To reduce the environmental implications of improper storage	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • Waste Disposal Ordinance (Cap. 54); • ETWB TCW No. 19/2005

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	authorities; and <ul style="list-style-type: none"> Disposal of waste should be done at licensed waste disposal facilities. 					
S9.5.8-11	<p><u>C&D Materials</u> The following mitigation measures shall be implemented in handling the waste:</p> <ul style="list-style-type: none"> Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; Carry out on-site sorting; Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; Disposal of the C&D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation; Standard formwork or pre-fabrication order to minimise the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage; and The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage. 	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> Waste Disposal Ordinance (Cap. 54); ETWB TCW No. 19/2005 ETWB TCW No. 06/2010
S9.5.13	<p><u>Excavated Marine Sediments</u> During transportation and disposal of the excavated marine sediments, the following measures shall be taken to minimize potential environmental impacts:</p> <ul style="list-style-type: none"> Bottom opening of barges should be fitted with tight fitting 	To minimize potential impacts on water quality	All construction sites where applicable	Contractor	Construction stage	<ul style="list-style-type: none"> ETWBTC (Works) No. 34/2002

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved; <ul style="list-style-type: none"> Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation; Transport barges or vessels should be equipped with automatic self-monitoring devices as specified by the DEP; and Barges should not be filled to a level that would cause the overflow of materials or sediment-laden water during loading or transportation. 					
S9.5.14-17	For those processes which generate chemical waste, the Contractor shall identify any alternatives that generate reduced quantities or even no chemical waste, or less dangerous types of chemical waste. If chemical waste is produced at the construction site, the Contractor is required to register with EPD as chemical waste producers. Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows. Containers used for storage of chemical wastes shall: <ul style="list-style-type: none"> Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specification have been approved by EPD; and Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations. The storage area for chemical wastes shall: <ul style="list-style-type: none"> Be clearly labelled and used solely for the storage of chemical wastes; Be enclosed on at least 3 sides; Have an impermeable floor and bunding of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; 	To ensure proper management of chemical waste	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Labelling and Storage of Chemical Waste

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	<ul style="list-style-type: none"> Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste, if necessary); and Be arranged so that incompatible materials are adequately separated. Disposal of chemical waste shall: <ul style="list-style-type: none"> Be via a licensed waste collector; and Be to a facility licensed to receive chemical waste, such as the CWTC which also offers a chemical waste collection service and can supply the necessary storage containers; or Be to a re-user of the waste, under approval from EPD. 					
S9.5.18	<p>Sewage An adequate number of portable toilets shall be provided for the on-site construction workers. Any waste shall be transferred to a sewage treatment works by a licensed collector.</p>	Proper handling of sewage from worker to avoid odour, pest and litter impacts	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> Waste Disposal Ordinance (Cap. 54)
S9.5.19	<p>General Refuse General refuse generated on-site shall be stored in enclosed bins or compaction units separately from construction and chemical wastes. Recycling bins shall also be provided to encourage recycling. A reputable waste collector shall be employed by the Contractor to remove general refuse from the site on a daily basis separately from the construction and chemical wastes. Burning of refuse on construction sites is prohibited by law.</p>	Minimize production of general refuse and avoid odour, pest and litter impacts	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> Waste Disposal Ordinance (Cap. 54)
S10.7.2.4	Good Site Practices – The integrity and effectiveness of all silt curtains shall be regularly inspected. Effluent monitoring should be incorporated to make sure that the discharged effluent from construction sites meets the relevant effluent discharge guidelines.	To minimize potential impacts on water quality and protect marine communities within Junk Bay	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> TM-EIAO; and WPCO
S10.7.2.5	Site runoff control – For works on land, standard site runoff control measures will be established and strictly enforced to ensure that discharge of contaminated or silt-laden runoff into marine waters is minimized.	To minimize potential impacts on water quality and protect marine communities within Junk Bay	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> TM-EIAO; and WPCO
S10.9.1.1	The marine water quality monitoring programme recommended in Chapter 8 of this EIA report and this EMIS would also serve to protect the marine communities inside Junk Bay.	To minimize potential impacts on water quality and protect marine	Selected monitoring stations (Drawing no. 209506/EMA/WQ/001)	Contractor	Construction stage	<ul style="list-style-type: none"> TM-EIAO; and WPCO

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
		communities within Junk Bay				
S11.6.2.2	Good Site Practices: – The integrity and effectiveness of all silt curtains should be regularly inspected. Effluent monitoring shall be incorporated to make sure that the discharged effluent from construction sites meets the relevant effluent discharge guidelines.	To minimize potential impacts on water quality and protect fishery resources	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO
S11.6.2.3	Site runoff control - For works on land, standard site runoff control measures will be established and strictly enforced to ensure that discharge of contaminated or silt-laden runoff is minimized.	To minimize potential impacts on water quality and protect fishery resources	All construction sites	Contractor	Construction stage	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO
S11.8.1.1	The marine water quality monitoring programme recommended in Chapter 8 of this EIA report and this EMIS would also serve to protect the fishery resources.	To minimize potential impacts on water quality and protect fishery resources	Selected monitoring stations (Drawing no. 209506/EMA/WQ/001)	Contractor	Construction stage	<ul style="list-style-type: none"> • TM-EIAO; and • WPCO
Landscape and Visual						
S13.8.1.2	The following mitigation measures should be implemented in the construction stage <ul style="list-style-type: none"> • CM1 – The construction area and contractor’s temporary works areas should be minimized to avoid impacts on adjacent landscape. • CM2 – Reduction of construction period to practical minimum. • CM3 – Topsoil, where identified, should be stripped and stored for re-use in the construction of the soft landscape works, where the soil material meets acceptable criteria and where practical. The Contract Specification shall include storage and reuse of topsoil as appropriate. • CM4 – Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor’s works areas. (Tree protection measures will be detailed at Tree Removal Application stage). 	Minimize effects of landscape and visual impacts	Work site/during construction	Funded and implemented by CEDD	Construction stage	

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	<ul style="list-style-type: none"> • CM5 – Trees unavoidably affected by the works shall be transplanted where practical. Trees should be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme. • CM6 – Advance screen planting to proposed roads and associated structures. • CM7 – hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone). • CM8 – Screening of construction works by hoardings/noise barriers around works area in visually unobtrusive colours, to screen Works. • CM9 – Control night-time lighting and glare by hooding all lights. • CM10 – Ensure no run-off into water body adjacent to the Project Area. • CM11 – Avoidance of excessive height and bulk of buildings and structures 					
S13.8.1.2	OM1 – Compensatory tree planting for all felled trees shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006.	Minimize effects of landscape and visual impacts	Within the site boundary of the proposed works	Funded and implemented by CEDD. Maintained by CEDD and LCSD.	Design, construction and operational stages	
S13.8.1.2	The following mitigation measures should be implemented in the operational stage: <ul style="list-style-type: none"> • OM2 – A continuous belt of screen planting along the roads. Planting of the belt of trees shall be carried out as advance works ahead of other site formation and building works. • OM3 – Maximise soft landscape of the site, where space permits, roadside berms /slope treatment works should be created. • OM4 – During detailed design, refine structure layout to create a planting strips along the roads to enhance greenery. • OM5 – Use appropriate (visually unobtrusive and 	Minimize effects of landscape and visual impacts	CBL and Road D9/during construction and operation	Funded and implemented by CEDD. Maintained by CEDD and LCSD.	Design, construction and operational stages	

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	non-reflective) building materials and colours, and aesthetic design in built structures. <ul style="list-style-type: none"> • OM6 – Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context, and minimizes potential negative landscape and visual impacts. Lighting units should be directional and minimize unnecessary light spill. • OM7 – Avoidance of excessive height and bulk of buildings and structures 					
Landfill Gas						
S14.7.5	Precautionary measures The following guidance has been extracted from the EPD’s Landfill Gas Hazard Assessment Guidance Note Guidance to ensure a robust and comprehensive set of measures to protect workers are provided. <ul style="list-style-type: none"> • During all works, safety procedures shall be implemented to minimize the risks of fires and explosions, asphyxiation of workers (especially in confined space) and toxicity effects resulting from contact with contaminated soils and groundwater. • Safety officers who are specifically trained with regard to LFG and leachate related hazards and the appropriate actions to take in adverse circumstances shall be present on all worksites throughout the works. • All personnel who work on site and all visitors to the site shall be made aware of the possibility of ignition of gas in the vicinity of the works, the possible presence of contaminated water and the need to avoid physical contact with it. • Those staff who work in, or have responsibility for “at risk” areas, including all excavation workers, supervisors and engineers working within the consultation zone, shall receive appropriate training on working in areas susceptible to LFG hazards. • Enhanced personal hygiene practices including washing thoroughly after working and eating only in “clean” areas shall be adopted where contact may have been made with any groundwater which is thought to be contaminated with 	Health and safety of the workers	Construction sites within 250m Consultation Zone (Drawing no. 209506/EMA/LFG/001)	Contractor	Construction stage	<ul style="list-style-type: none"> • Landfill Gas Hazard Assessment Guidance Note (EPD/TR8/97)

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	<p>leachate.</p> <ul style="list-style-type: none"> • Ground level construction plant shall be fitted with vertical exhausts at least 0.6m above ground level and with spark arrestors. • During piping assembly or ducting construction, all valves/seals shall be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping /ducting shall be capped at the end of each working day. • Mobile offices, equipment stores, mess rooms etc. shall be located on an area which has been proven to be gas free (by survey with portable gas detectors) and ongoing monitoring shall be carried out to ensure that these areas remain gas free. Alternatively, such buildings shall be raised clear of the ground. If buildings are raised clear of the ground, the minimum, clear separation distance (as measured from the highest point on the ground surface to the underside of the lowest floor joist) shall be 500mm. However, in this case, it is highly recommended that all the site offices, equipment stores and mess rooms should be located outside the 250m Consultation Zone. • Smoking and naked flames shall be prohibited within confined spaces. “No Smoking” and “No Naked Flame” notices in Chinese and English shall be posted prominently around the construction site. Safety notices shall be posted warning of the potential hazards. • Welding, flame-cutting or other hot works may only be carried out in confined spaces when controlled by a “permit to work” procedure, properly authorized by the Safety Office. The permit to work procedure shall set down clearly the requirements for continuous monitoring of methane, carbon dioxide and oxygen throughout the period during which the hot works are in progress. The procedure shall also require the presence of an appropriately qualified person who shall be responsible for reviewing the gas measurements as they are made, and who shall have executive responsibility for suspending the work in the event of 					

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	<p>unacceptable or hazardous conditions. Only those workers who are appropriately trained and fully aware of the potentially hazardous conditions which may arise shall be permitted to carry out hot works in confined areas.</p> <ul style="list-style-type: none"> During the construction works, adequate fire extinguishers and breathing apparatus sets shall be made available on site and appropriate training given in their use. 					
S14.7.6	<p>Landfill gas monitoring The following monitoring shall be undertaken when construction works are carried out in confined space within the 250m Consultation Zone:</p> <ul style="list-style-type: none"> The works area shall be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. The monitoring requirements and procedures specified in Paragraphs 8.23 to 8.28 of EPD's Guidance Note shall be followed. The monitoring frequency and areas to be monitored shall be set down prior to commencement of the works. Depending on the results of the measurements, actions required will vary. As a minimum these shall encompass the actions specified in Table 14.6 of the EIA report. When portable monitoring equipment is used, the frequency and areas to be monitored should be set down prior to commencement of the works either by the Safety Officer or by an appropriately qualified person. All measurements shall be made with the monitoring tube located not more than 10mm from the surface. A standard form, detailing the location, time of monitoring and equipment used together with the gas concentrations measured, shall be used when undertaking manual monitoring to ensure that all relevant data are recorded. If methane (flammable gas) or carbon dioxide concentrations are in excess of the trigger levels or that of oxygen is below the level specified in the Emergency Management in the following section, then evacuation shall be initiated. 	Health and safety of the workers	Confined space of construction sites within 250m Consultation Zone	Contractor	Construction stage	<ul style="list-style-type: none"> Landfill Gas Hazard Assessment Guidance Note (EPD/TR8/97)
S14.7.8-9	<p>Emergency management In the event of the trigger levels specified in Table 14.6 of the EIA report being exceeded, a person, such as the Safety</p>	Health and safety of the workers	Confined space of construction sites within 250m Consultation Zone	Contractor	Construction stage	<ul style="list-style-type: none"> Landfill Gas Hazard Assessment

EIA Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to Address	Location/ Timing	Implementation		Requirements and/or Standards to be Achieved
				Agent	Stage	
	<p>Officer, shall be nominated, with deputies, to be responsible for dealing with any emergency which may occur due to LFG.</p> <p>In an emergency situation the nominated person, or his deputies, shall have the necessary authority and shall ensure that the confined space is evacuated and the necessary works implemented for reducing the concentrations of gas.</p>					<p>Guidance Note (EPD/TR8/97)</p>
S14.7.16	<p>Protection measures – Operational phase</p> <ul style="list-style-type: none"> • An assumed presence of landfill gas shall be adopted at all times by maintenance workers; • all maintenance workers inspecting any manhole shall be fully trained in the issue of LFG hazard; • any manhole which is large enough to permit to access to personnel shall be subject to entry safety procedure; • Code of Practice on Safety and Health at Work in Confined Spaces shall be followed to ensures compliance with the Factories and Industrial Undertakings (Confined Spaces) Regulations of the Factories and Industrial Undertakings Ordinance; • a strictly regulated “work permit procedure” shall be implemented and the relevant safety procedures must be rigidly followed; and • Adequate communication with maintenance staff shall be maintained with respect to LFG. 	Health and safety of the workers	Utility maintenance areas within 250m Consultation Zone/during operational period	Utility companies	Operational stage	<ul style="list-style-type: none"> • Landfill Gas Hazard Assessment Guidance Note (EPD/TR8/97); and • Code of Practice on Safety and Health at Work in Confined Space
S14.7.17	<p>General recommended precautionary & protection measures – Operational phase</p> <p>LGF surveillance exercise shall be undertaken by the utility companies at the utility manholes/inspection chambers. The surveillance exercise shall be undertaken for the duration of the site occupancy, or until such time that EPD agree that surveillance is no longer required and this shall be based on all the available monitoring data for methane, carbon dioxide and oxygen.</p>	Health and safety of the workers	Utility maintenance areas within 250m Consultation Zone/during operational period	Utility companies	Operational stage	<ul style="list-style-type: none"> • Landfill Gas Hazard Assessment Guidance Note (EPD/TR8/97); and • Code of Practice on Safety and Health at Work in Confined Space
